

HUEYTOWN HIGH SCHOOL



PROGRESS UPDATE REPORT
August 31, 2010

DOSTER

BASELINE

CONSULTANTS, INC.

Please initial the **meeting** date to show that you were in attendance.

Hueytown High School #29082

9/14	ATTENDEES	CO. NAME	7/20	8/3	8/17	8/31
	Butch Henderson	Accurate Ele.			XX	
	Steven Greeson	Automated Logic				
	Bob Cameron	Bama Concrete Inc.				
	Kyle Norwood	Bama Concrete Inc.				
	Larry Mackey	Bama Concrete Inc.				
	Stephen Franklin	BFS	XX			XX
	David Bullock	Bhate				
	Donnie Rigg	BSCO Inc.				
	Jessie Isom	BSCO Inc.				
	Cecil Smith	C.C.			XX	
	Jim Hacker	C.C.				XX
	Phil Sebring	Coreslab				
	Joe Kuhn	Doster Construction	XX	XX	XX	
	Josh Cronan	Doster Construction	XX	XX	XX	XX
	Justin Petty	Doster Construction	XX	XX	XX	XX
	Tim Robertson	Doster Construction	XX	XX	XX	XX
	Bo Hamilton	Dunn Construction				
	Jason Greene	Green Bldg				XX
	A. Castillo	Green Bldg				XX
	David Ginn	H2K	XX	XX	XX	XX
	Donnie Hall	Hall & Sons Plumbing				XX
	Jerry Fuller	Hall & Sons Plumbing	XX		XX	
	Moe Garner	Hall & Sons Plumbing	XX	XX	XX	XX
	Don Davis	J & K Electric	XX	XX	XX	XX
	John Britton	J & K Electric		XX	XX	XX
	Wayne Skinner	J & K Electric	XX			
	Darryl White	J & Sons				
	Darrell Cole	P&M Mechanical				
	Jimmy Davis	P&M Mechanical				
	Joe Manning	P&M Mechanical	XX	XX	XX	XX
	Micheal Isbell	P&M Mechanical		XX		
	Ed B.	Reliance			XX	
	Michael B. Furniss	Reliance		XX	XX	
	David Torres	Reliance			XX	
	Brian Korfant	Roof Craft	XX		XX	
	Mike Jones	Roof Craft Systems				
	Charles Johnson	Selective Masonry	XX	XX	XX	XX
	Jonathan Watts	Selective Masonry				
	Wes Smith	Selective Masonry	XX	XX	XX	XX
	Mark Smith	Simpson Plastering	XX			
	Mike Kennedy	Simpson Plastering	XX			
	Jay Poole	SMI				
	Jesse Kelley	Southwest Water				
	Willy Shepard	Southwest Water				

If you do not see your name, please print your name and company name in available space.

PROGRESS SUMMARY

**Hueytown High School
August 31, 2010**

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, August 31, 2010, at the Doster Construction Company jobsite trailer.

The next Progress Update Meeting will be held at 10:00 a.m. on Tuesday, September 14, 2010, at Doster Construction Company jobsite trailer.

Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.



AREA F

The following summary is assumed to be a true and factual account of events that transpired in the August 31, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.

GENERAL NOTES

Tim Robertson of Doster Construction Company reviewed general safety issues. Mr. Robertson advised all personnel that daily cleanup must occur. All masonry construction debris must be cleaned out of Areas F, G & E. The soffit framing activities have started and all contractors roughing in the soffits need to use caution while installing to prevent damage to the soffit framing.

The jobsite will be closed September 4, 5, and 6, 2010 in observance of Labor Day.

SITWORK

No work has occurred relating to the 15th Street shoulder and decel lane activities. Mr. Robertson stated that T&K payments have been put on hold until they remobilize.



AREA B

Tie-in of the building rain water leaders to the site drainage system will begin September 7 and run the September 21, 2010.

STRUCTURE

Rain water leaders at Areas G and F have been connected. Non-load bearing CMU is complete in Areas F and E. Two days of non-load bearing CMU are left to complete in Area G with the wrapping of the columns at line 13.

Auditorium catwalk steel installation is ongoing and will complete September 8, 2010. Structural steel in this area will begin September 9, 2010, and CMU at the stage will now begin in conjunction with the structural steel. The dance and riser room slab-on-grade will be poured

September 1, with the concessions and storage areas being poured on September 3, 2010.

The load bearing CMU at the 2nd Floor of Area B is continuing. This work will complete by the end of the week and trusses in this area will begin September 7, 2010. The load bearing CMU at Area C 2nd Floor will now start Tuesday, September 7, 2010.

The topping slab in Area A has been poured and load bearing CMU at the 2nd Floor of this area will follow Area C CMU.

EXTERIOR SKIN

Installation of precast has begun, but brickwork has not started. Damp proofing is underway. Brick installation will begin September 7, 2010.

The flat roof at Area E is ongoing and Area D flat roof activities will begin following the steel installation. Decking of all areas, except for the high roof at the auditorium, will complete by the week of September 6, 2010.

INTERIOR CONSTRUCTION

Fireproofing activities at all available 1st Floor areas are ongoing. Fireproofing will be able to move from the 1st to the 2nd Floor in Areas F and G.

The above ceiling State Inspection in Area F will occur the week of September 13, 2010. Rooms F 111, 114, 118, 122, 126, and 131 will be inspected. All disciplines are tracking to meet this inspection date. Provided that the overhead inspection is obtained, hanging activities at the hard ceilings will begin September 14, 2010. Locker room ceramic tile is on schedule to begin September 27, 2010.

Overhead rough-ins in the kitchen area are underway with sprinkler and HVAC. Auditorium overhead rough-ins will begin following roofing in this area.



AREA G




LOCKER ROOM

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated August 31, 2010.


Hueytown High School

ACTION ITEM LIST						MEETING DATE: August 31, 2010
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	4.	Brick Color Boards	SMI	03/18/10	09/10/10	Build final mock-up on building in place
03/02/10	9.	Settlement Plate	T&K	03/05/10	06/14/10	Monitor
06/22/10	13.	South West Water Company	SWWC	06/22/10	08/17/10	Issue install schedule - work ongoing

HUEYTOWN HIGH SCHOOL

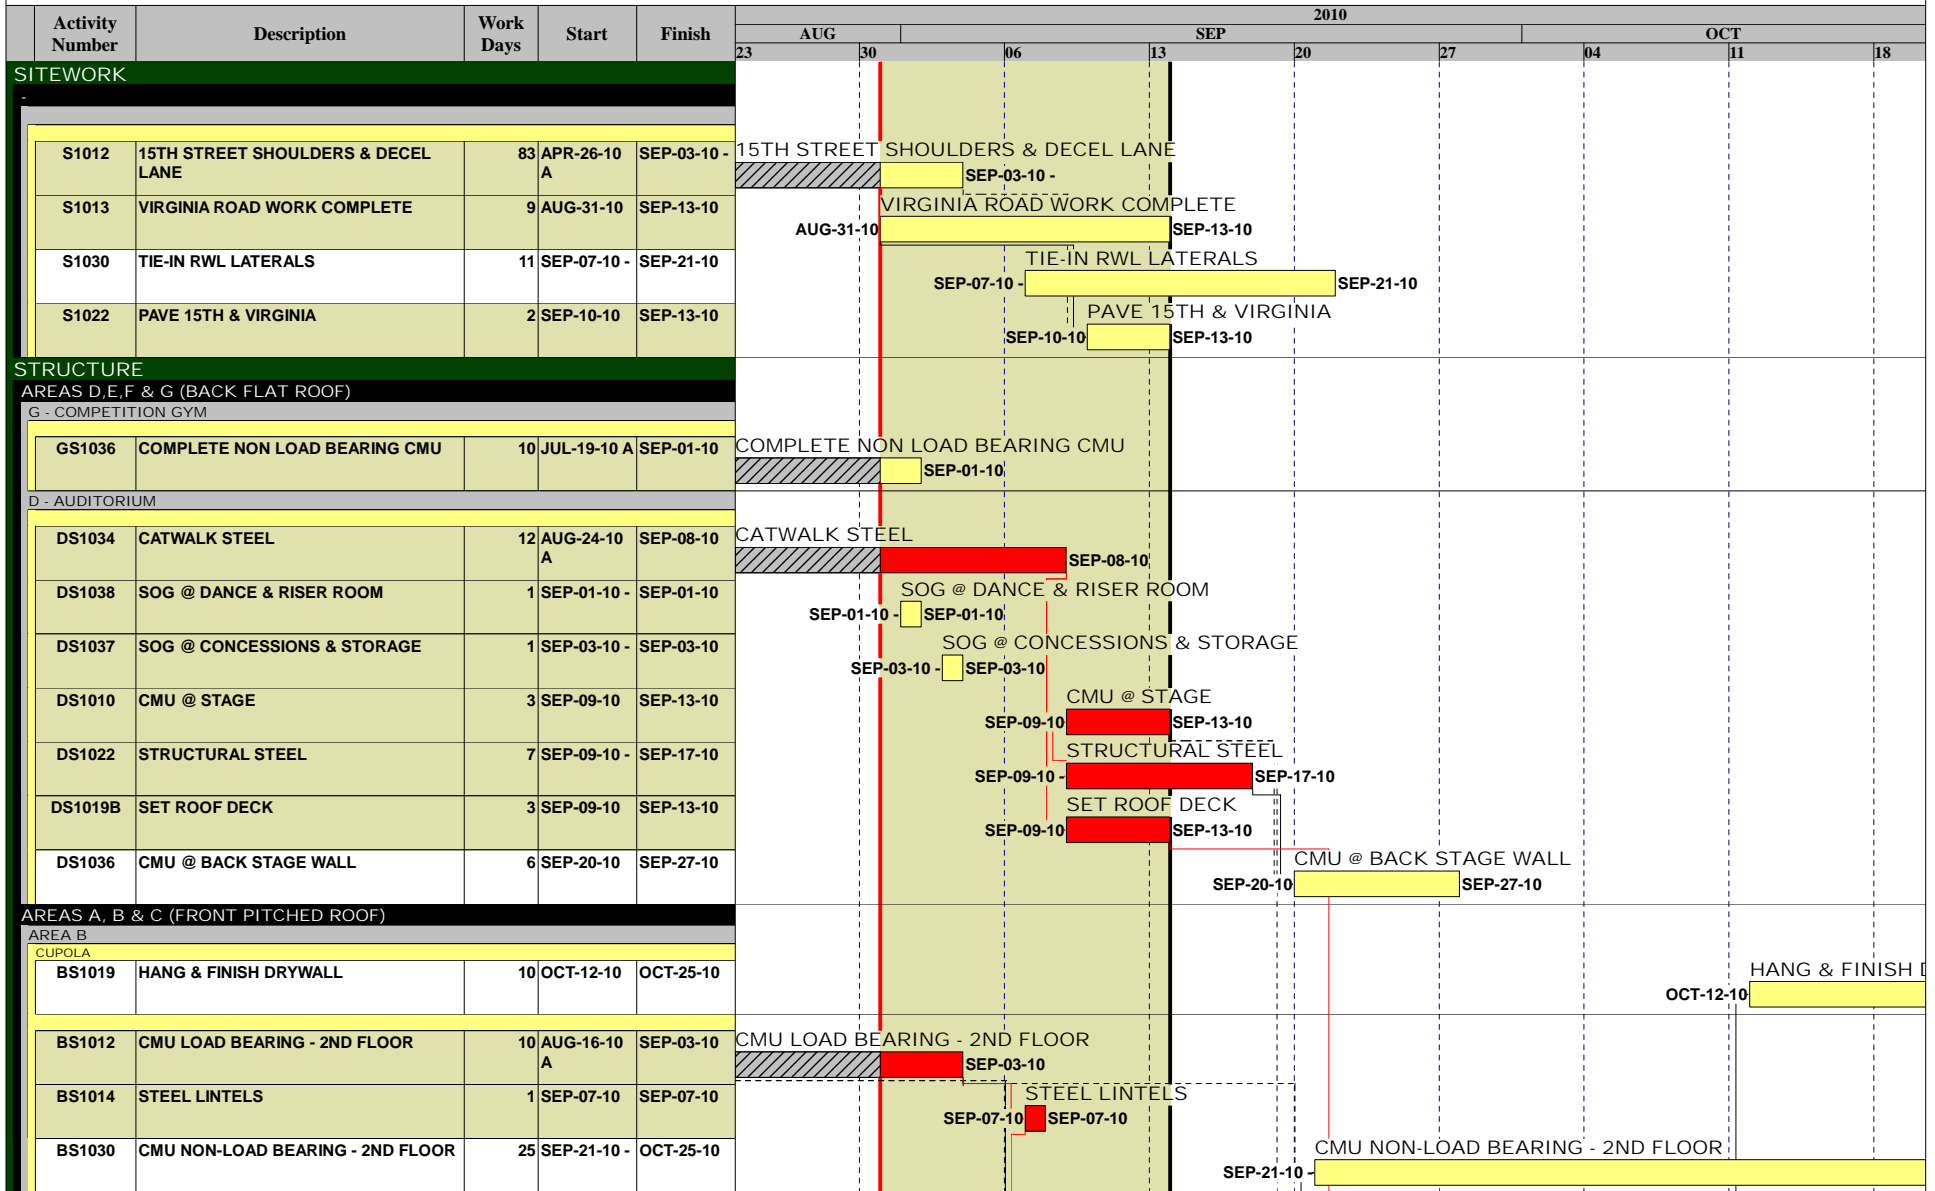


HUEYTOWN HIGH SCHOOL

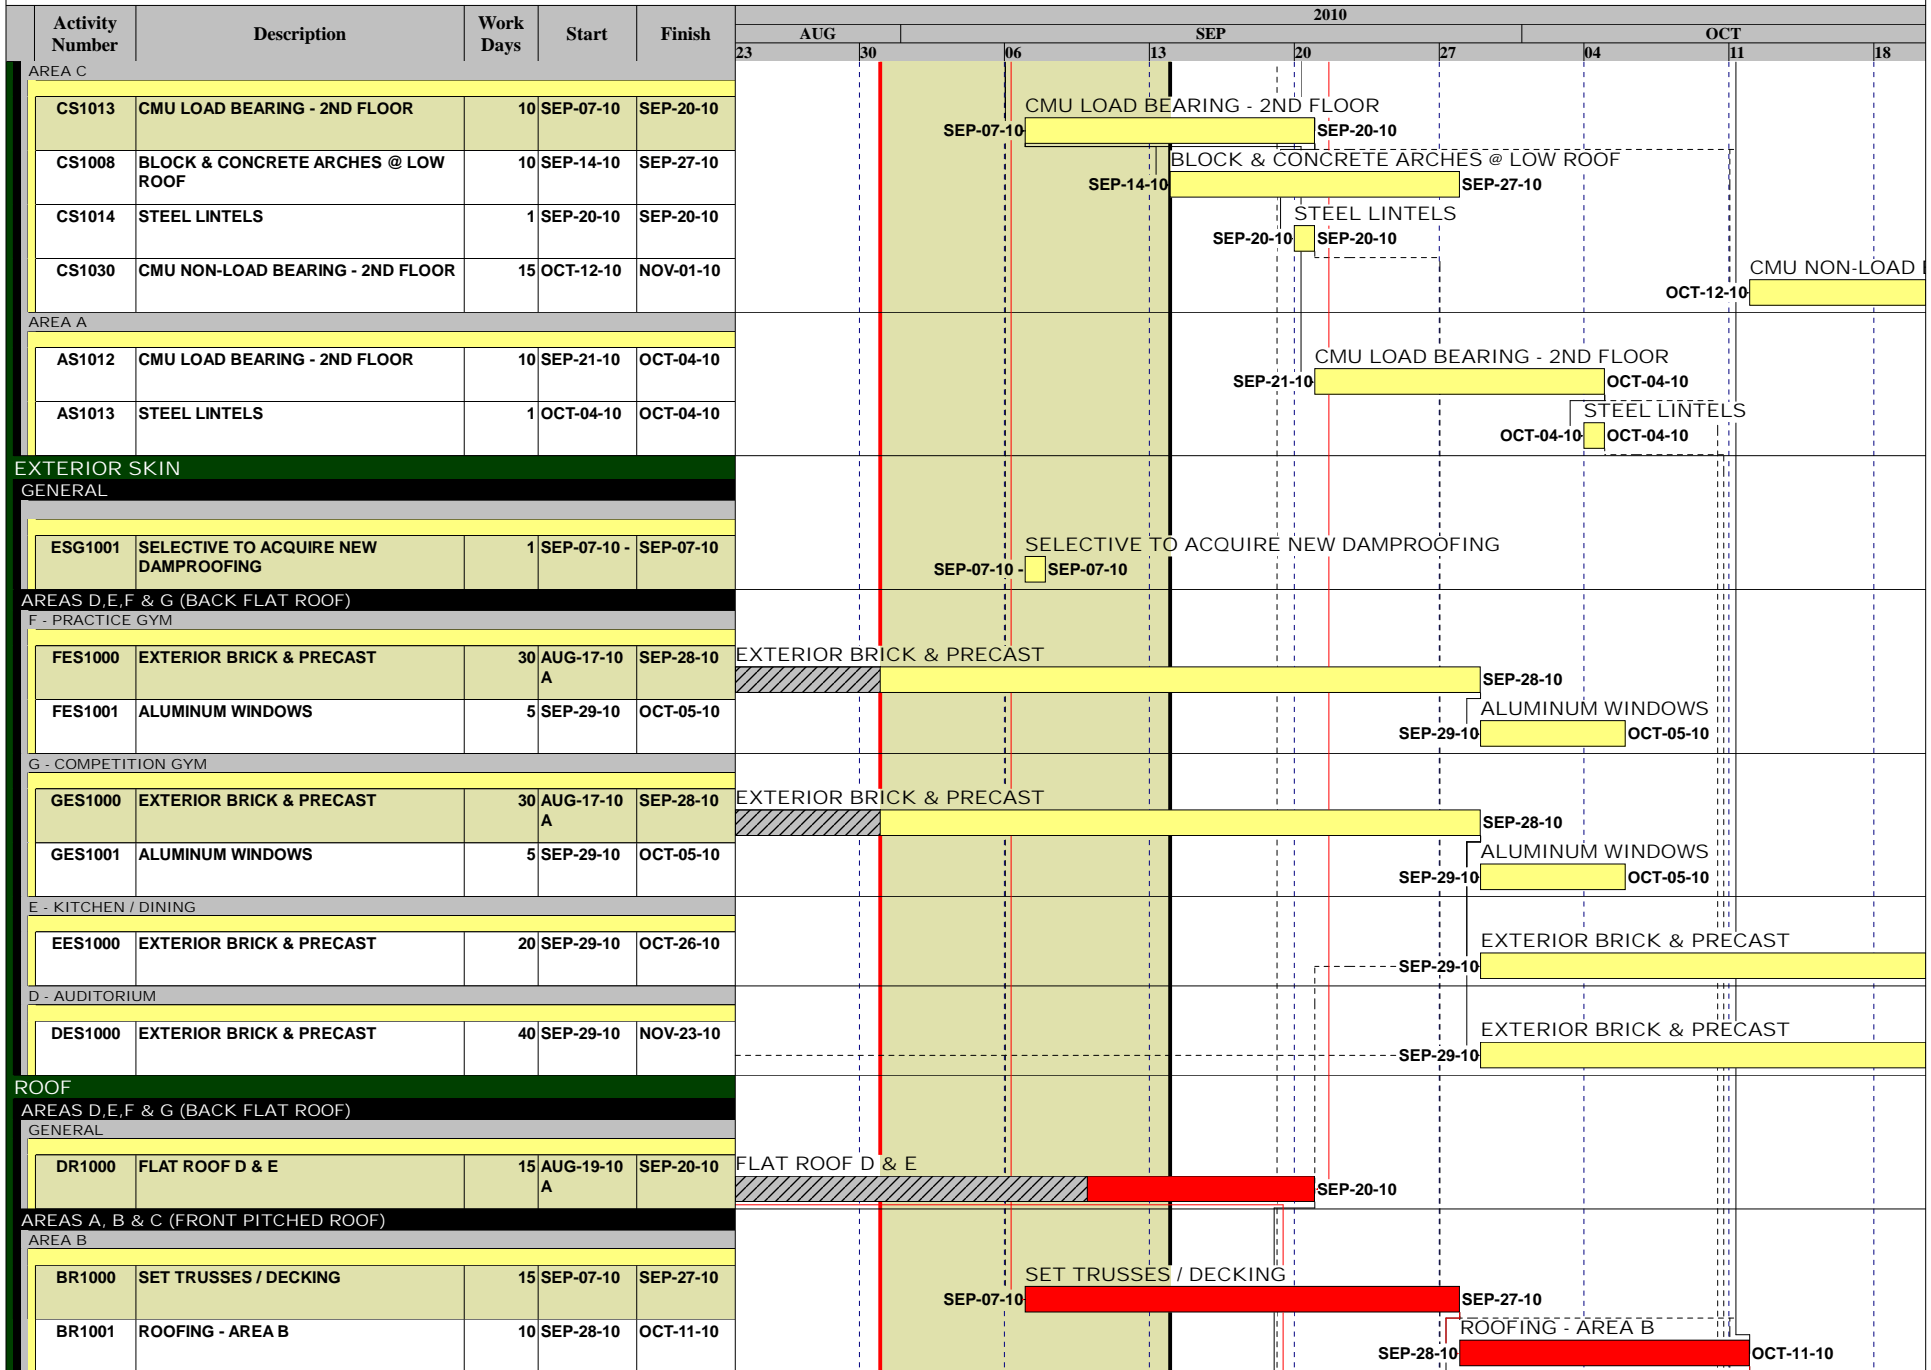


HUEYTOWN HIGH SCHOOL

Activity Number	Description	Work Days	Start	Finish	2010																		
					AUG			SEP						OCT									
					23	30	06	13	20	27	04	11	18										
BR1002	FIRE PROOF STEEL	3	OCT-12-10	OCT-14-10																			
AREA C																							
CR1000	SET TRUSSES / DECKING	10	SEP-28-10	OCT-11-10																			
CR1001	ROOFING - AREA C	10	OCT-12-10	OCT-25-10																			
AREA A																							
AR1000	SET TRUSSES / METAL DECKING	10	OCT-12-10	OCT-25-10																			


HUEYTOWN HIGH SCHOOL

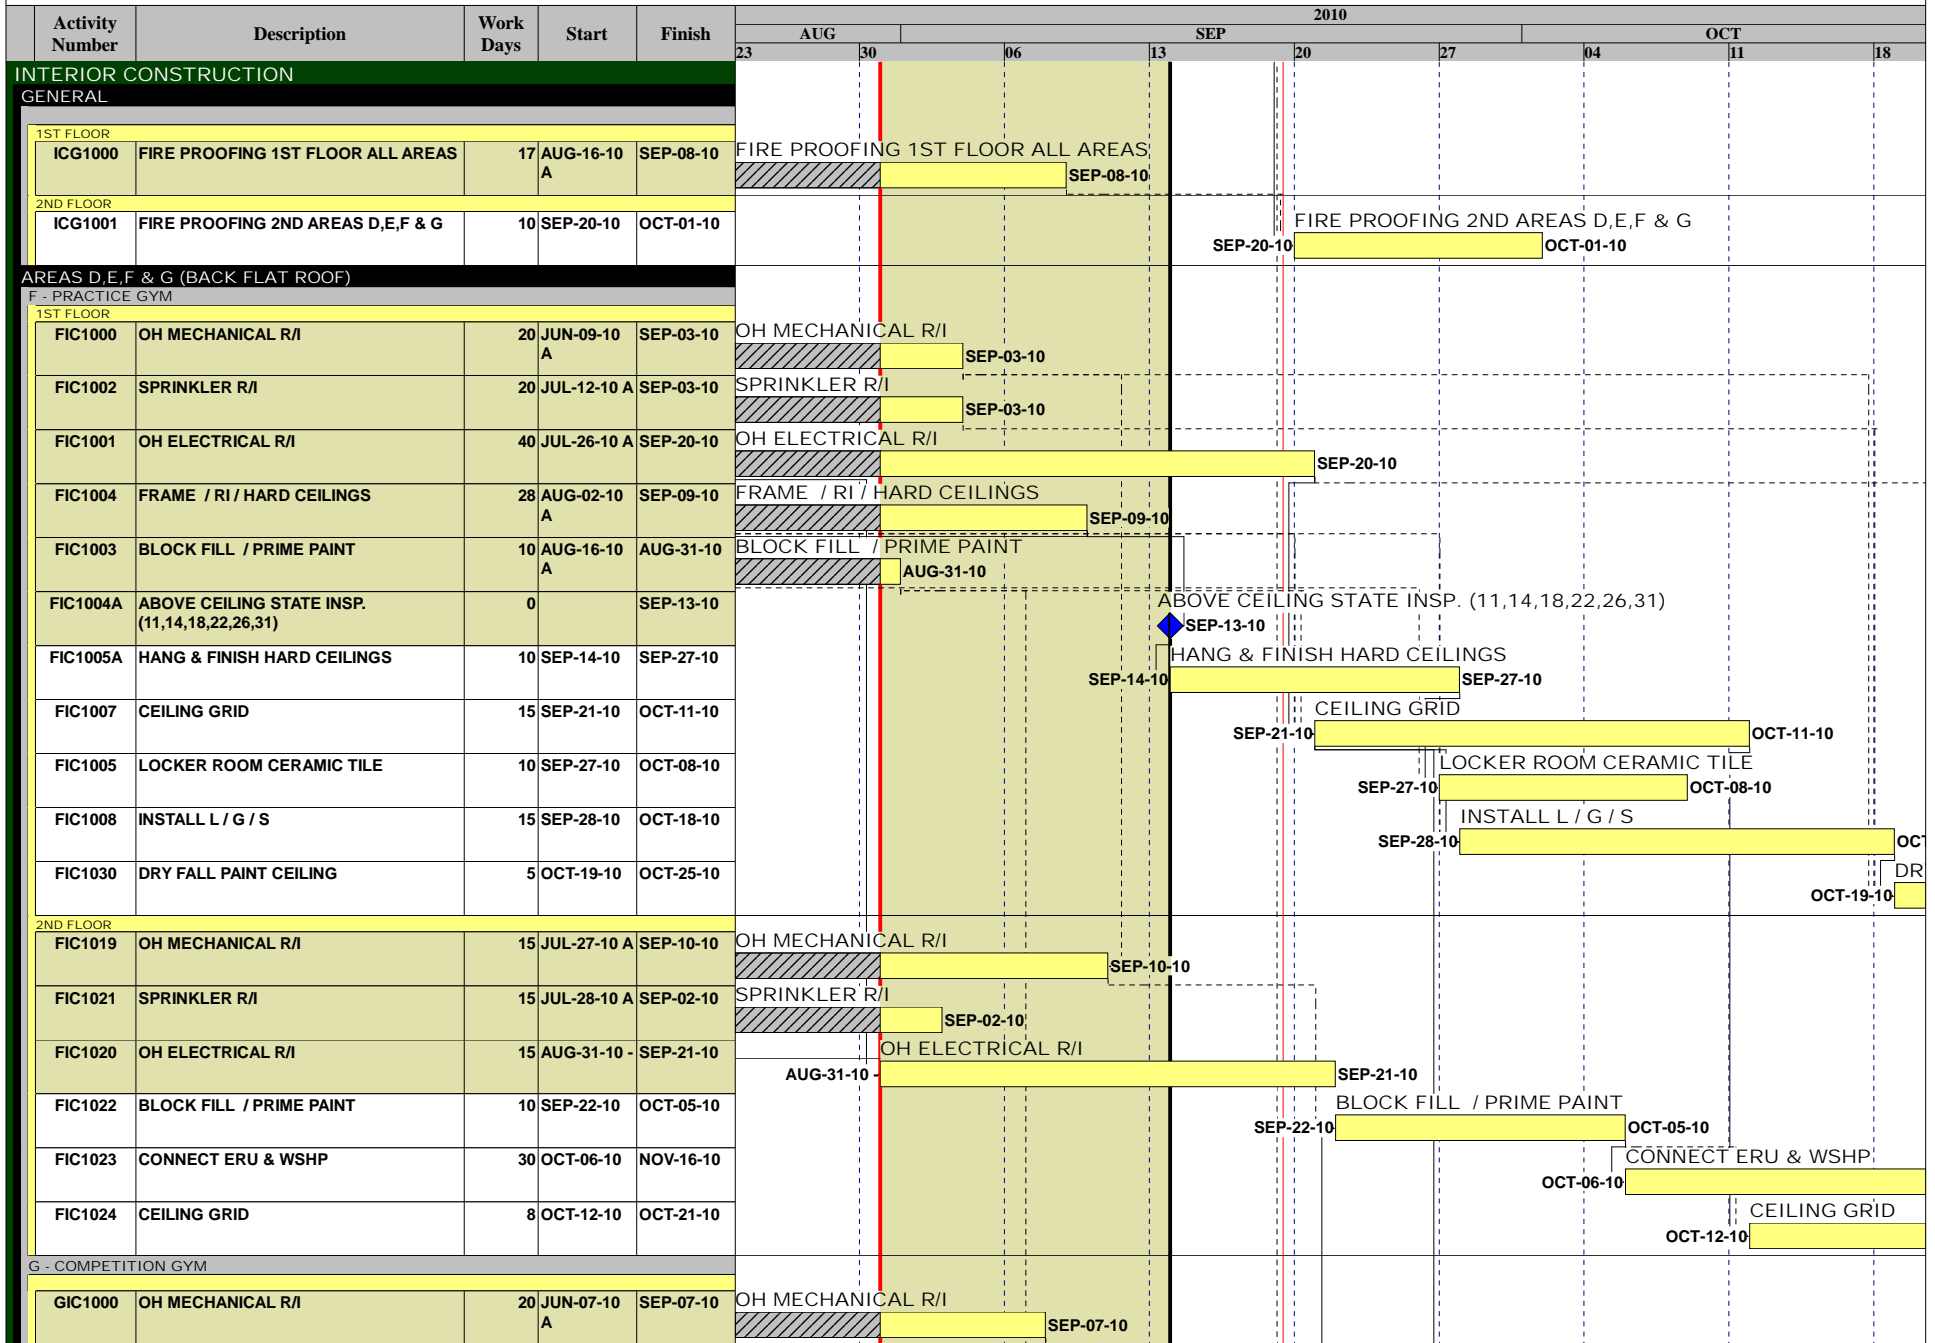

HUEYTOWN HIGH SCHOOL

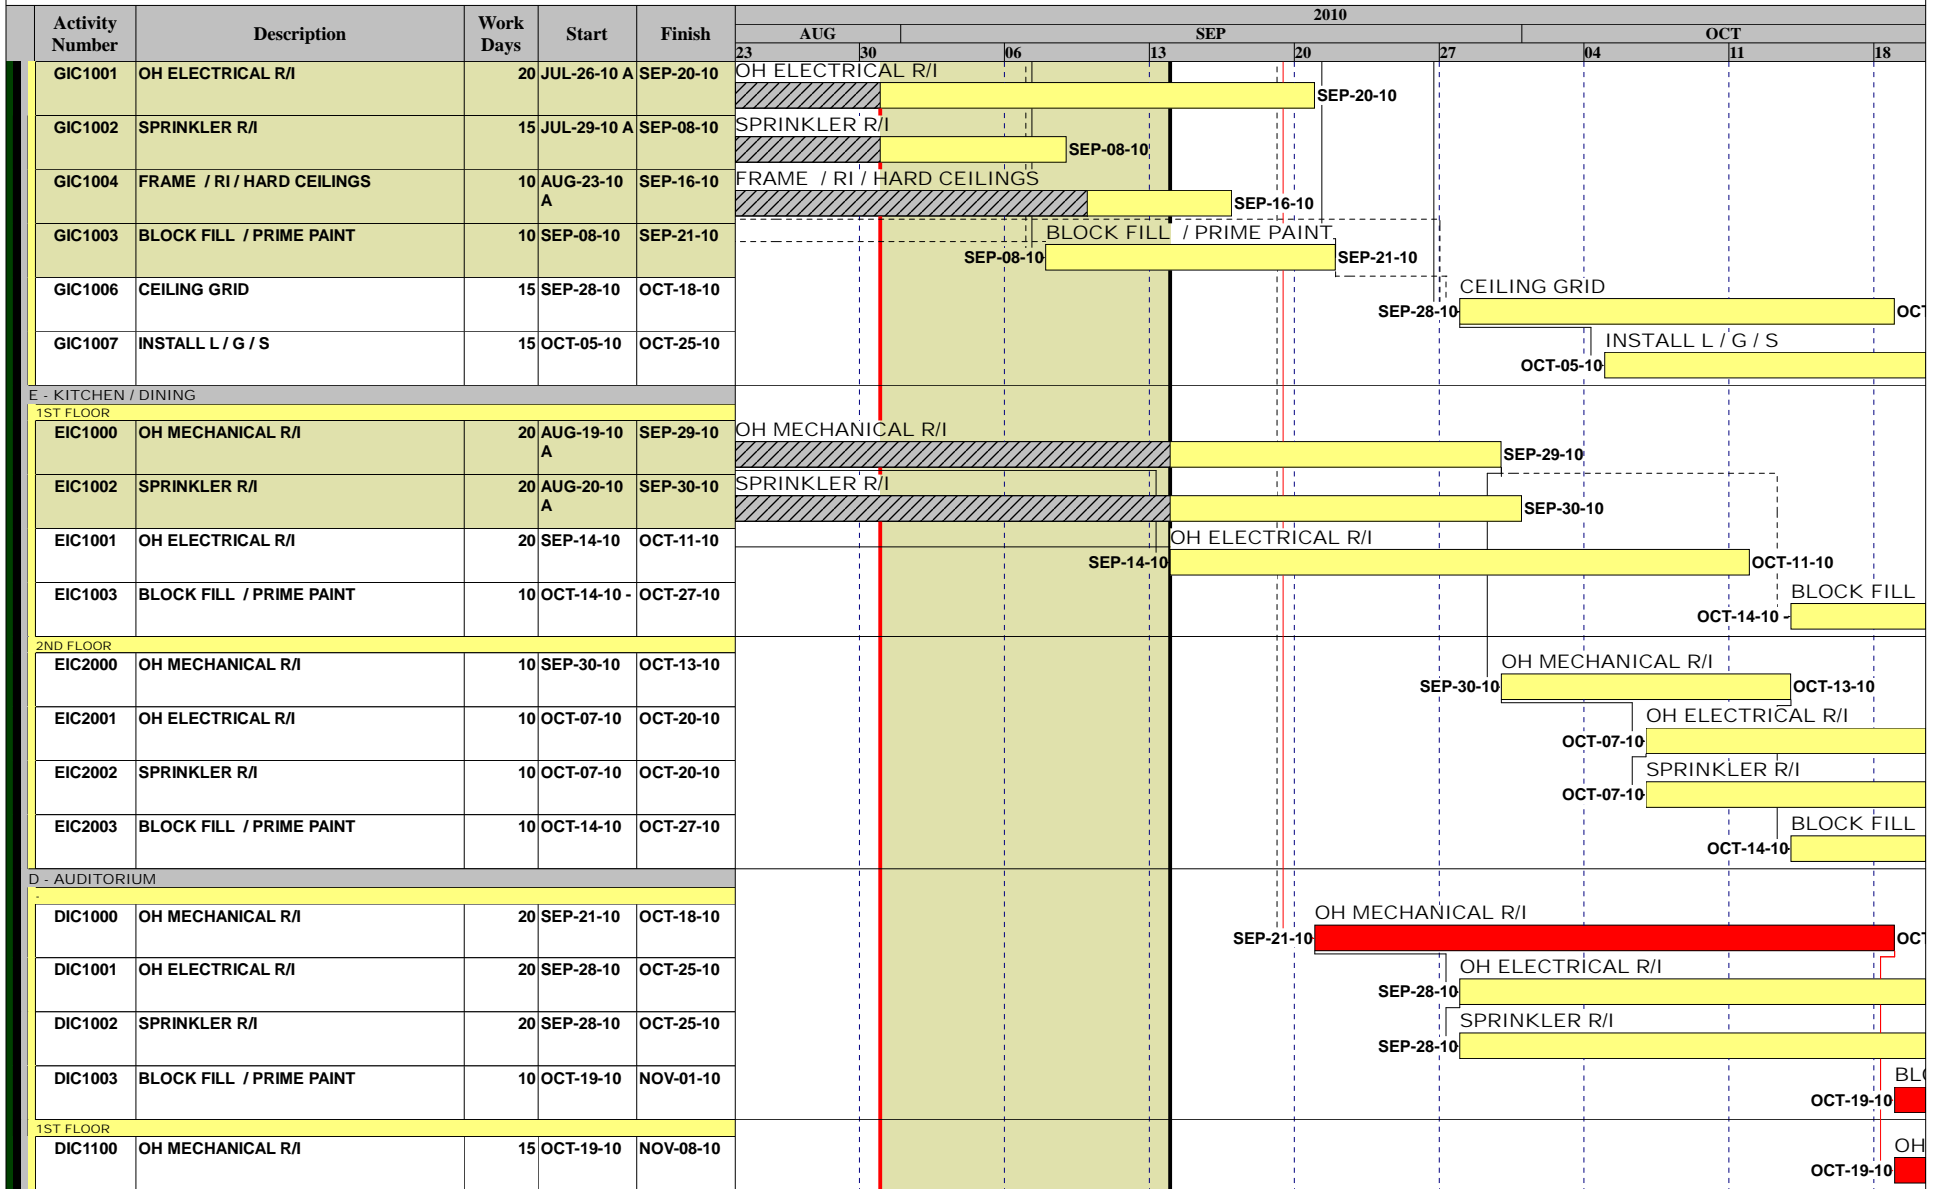

HUEYTOWN HIGH SCHOOL

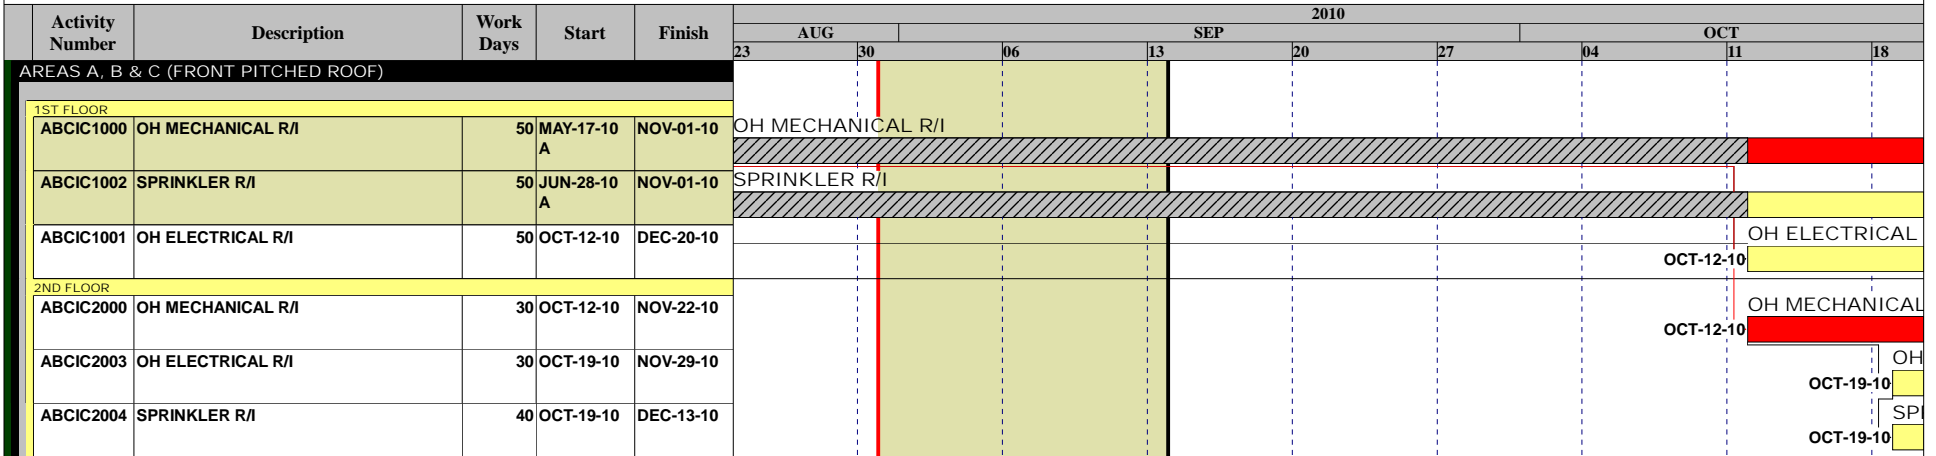

-

Distribution List Name: 29082 - Hueytown High School

Bo Hamilton	bhamilton@dunnconstruction.com
Brian Korfant	brian.korfant@roofusa.com
Donnie Hall	dhallnsons@aol.com
Elsie Cowart	ecowart@rpainc.biz
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Justin Petty	jpetty@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Mike Jones	mike.jones@roofusa.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Sue Cole	sue@dixiestorefixtures.com
Tim Robertson	trobertson@dosterconstruction.com
