

HUEYTOWN HIGH SCHOOL



PROGRESS UPDATE REPORT
August 3, 2010

DOSTER

BASELINE

CONSULTANTS, INC.

Please initial the **meeting** date to show that you were in attendance.



Hueytown High School #29082

8/17	ATTENDEES	CO. NAME	6/8	6/22	7/20	8/3
	Butch Henderson	Accurate Ele.				
	Steven Greeson	Automated Logic				
	Bob Cameron	Bama Concrete Inc.				
	Kyle Norwood	Bama Concrete Inc.				
	Larry Mackey	Bama Concrete Inc.				
	Stephen Franklin	BFS			XX	
	David Bullock	Bhate				
	Donnie Rigg	BSCO Inc.				
	Jessie Isom	BSCO Inc.				
	Cecil Smith	C.C.	XX	XX		
	Phil Sebring	Coreslab				
	Joe Kuhn	Doster Construction	XX	XX	XX	XX
	Josh Cronan	Doster Construction	XX	XX	XX	XX
	Justin Petty	Doster Construction	XX	XX	XX	XX
	Tim Robertson	Doster Construction	XX	XX	XX	XX
	Bo Hamilton	Dunn Construction				
	David Ginn	H2K	XX	XX	XX	XX
	Donnie Hall	Hall & Sons Plumbing				
	Jerry Fuller	Hall & Sons Plumbing	XX	XX	XX	
	Moe Garner	Hall & Sons Plumbing	XX	XX	XX	XX
	Don Davis	J & K Electric	XX	XX	XX	XX
	John Britton	J & K Electric	XX	XX		XX
	Wayne Skinner	J & K Electric			XX	
	Darryl White	J & Sons				
	Darrell Cole	P&M Mechanical	XX			
	Gary Psnell	P&M Mechanical				
	Jimmy Davis	P&M Mechanical		XX		
	Joe Manning	P&M Mechanical	XX	XX	XX	XX
	Micheal Isbell	P&M Mechanical				XX
	Michael B. Furniss	Reliance				XX
	Brian Korfant	Roof Craft	XX	XX	XX	
	Mike Jones	Roof Craft Systems		XX		
	Charles Johnson	Selective Masonry	XX	XX	XX	XX
	Jonathan Watts	Selective Masonry				
	Wes Smith	Selective Masonry		XX	XX	XX
	Mark Smith	Simpson Plastering			XX	
	Mike Kennedy	Simpson Plastering			XX	
	Jay Poole	SMI	XX			
	Jesse Kelley	Southwest Water		XX		
	Willy Shepard	Southwest Water		XX		
	P. E.	Stankunas Construction			XX	
	Gregg Baker	T&K Construction				
	Lanny Nelson	T&K Construction	XX	XX		
	Nathaniel Hutchinson	T&K Construction			XX	
	Steve Giddens	T&K Construction				
	Mell Gage Smith	The Mell Group		XX		
	Joseph Dodson	United States Sprinkler				
	Lee Edmonds	Baseline Consultants, Inc.	XX	XX	XX	XX

If you do not see your name, please print your name and company name in available space.

PROGRESS SUMMARY

**Hueytown High School
August 3, 2010**

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, August 3, 2010, at the Doster Construction Company jobsite trailer.

The next Progress Update Meeting will be held at 10:00 a.m. on Tuesday, August 17, 2010, at Doster Construction Company jobsite trailer.

Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.

The following summary is assumed to be a true and factual account of events that transpired in the August 3, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.



AREA G

GENERAL NOTES

Tim Robertson of Doster Construction Company reviewed general safety items and cleanup. Mr. Robertson also reviewed protection of concrete floors. Handrails at the 2nd Floor areas must stay in place and be monitored during material loading to the 2nd Floor. Tie-off must occur in all lifts.

SITWORK

The 15th Street shoulder and decel lane work is continuing. The water connection will be completed by the end of the week. The 15th Street work will be complete August 9 and the Virginia Road work will follow and complete the week of August 23, 2010.



AREA D

STRUCTURE

The non-load bearing CMU in the Area F will complete following the electrical rough-in. Electrical rough-in will be complete by Monday, August 9, 2010. The remaining 7 days of CMU wall work will complete the week of August 16, 2010. CMU work in Area G will be complete in conjunction with Area F. Area E, Kitchen and Dining, joist and deck will be complete by the end of the day. CMU at parapet decking is underway and will complete by Wednesday, August 4, 2010. Roof curbs are now targeted to be set August 9, 2010. Roofing activities in this area need to begin immediately.

Area D, Auditorium, CMU will be complete except for stage area by August 11, 2010. Forming and pouring of the orchestra pit walls is

complete and structural steel in this area will now begin being set Monday, August 16, 2010. Roof truss and decking will begin on Tuesday, August 17, 2010. CMU at the stage will follow the structural steel, roof joist and decking. Pouring of the Auditorium slab-on-grade will occur after the roof decking is complete.

The target date to have Areas F and G 100% dry, with air handling unit curbs tied in complete is August 20, 2010.

The flat roof at Areas F and G is substantially complete. Setting of the air handling units and energy recovery units will occur the week of August 16, 2010. Complete installation of the roof curb details for the units will complete the week of August 9, 2010.



AREA B

Flat roof at Areas D and E will begin installation August 11, 2010, provided that roofing materials are available on the jobsite. It is noted that the decking in Area E is available for roofing to begin.

The topping slab at the 2nd Floor of Area B has begun installation. Load bearing CMU will not be installed prior to the topping slab. The topping slab at Area B will be poured complete today; the topping slab at Area C will be poured by August 10; and the topping slab at Area A will be poured by August 17, 2010. Load bearing CMU installation at the 2nd Floor of Area B will begin on August 10, 2010.

Setting of roof trusses and decking at Area B will begin August 30, 2010, and are targeted to be substantially complete through Areas C and A by mid- October 2010.

EXTERIOR SKIN

Exterior brick is onsite and installation of brick and precast is now targeted to begin August 16, 2010, provided that precast material is available at this time.

INTERIOR CONSTRUCTION

Grouting of plates ahead of the fireproofing has not occurred. This grouting work will be complete by the end of the week. Fireproofing at the 1st Floor in all areas that are available for fireproofing will begin installation August 9, 2010.



AREA C

In Area F, the over head mechanical rough-in has had no progress over the past two weeks. The 2nd Floor mechanical rough-in is underway with piping activities. Overhead electrical rough-in is underway. Sprinkler rough-in is continuing at the 1st Floor. Framing of hard ceilings in the Locker Room has begun. Block fill and prime paint in this area is now targeted to begin August 23, and Locker Room ceramic tile August 30, 2010.

Overhead mechanical rough-in at Area G is continuing. Electrical rough-in and sprinkler rough-in in this area are underway.

Overhead mechanical and sprinkler rough-ins are continuing at the 1st Floor of Areas A, B, and C.


Electrical fixture deliveries were reviewed during today's meeting and light fixtures for Areas G, E, and F need to be released today and are targeted for a 6 to 8 week delivery. Delivery should be between mid-September and early- October 2010. Release of lay-in fixtures for Areas A, B, C and D will need to be released no later than September 20, and a 6 to 8 week delivery forecast material being onsite between early - and mid- November 2010.

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated August 3, 2010.


Hueytown High School

ACTION ITEM LIST						MEETING DATE: August 3, 2010
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	4.	Brick Color Boards	SMI	03/18/10	08/16/10	Build final mock-up on building in place
01/05/10	5.	Water Meter C.O.R.	Lathan	01/06/10	?	Issue change order (Final pricing to A/E 4/13/10)
03/02/10	9.	Settlement Plate	T&K	03/05/10	06/14/10	Install and monitor (at ball field)
06/22/10	13.	South West Water Company	SWWC	06/22/10	08/04/10	Issue install schedule


HUEYTOWN HIGH SCHOOL

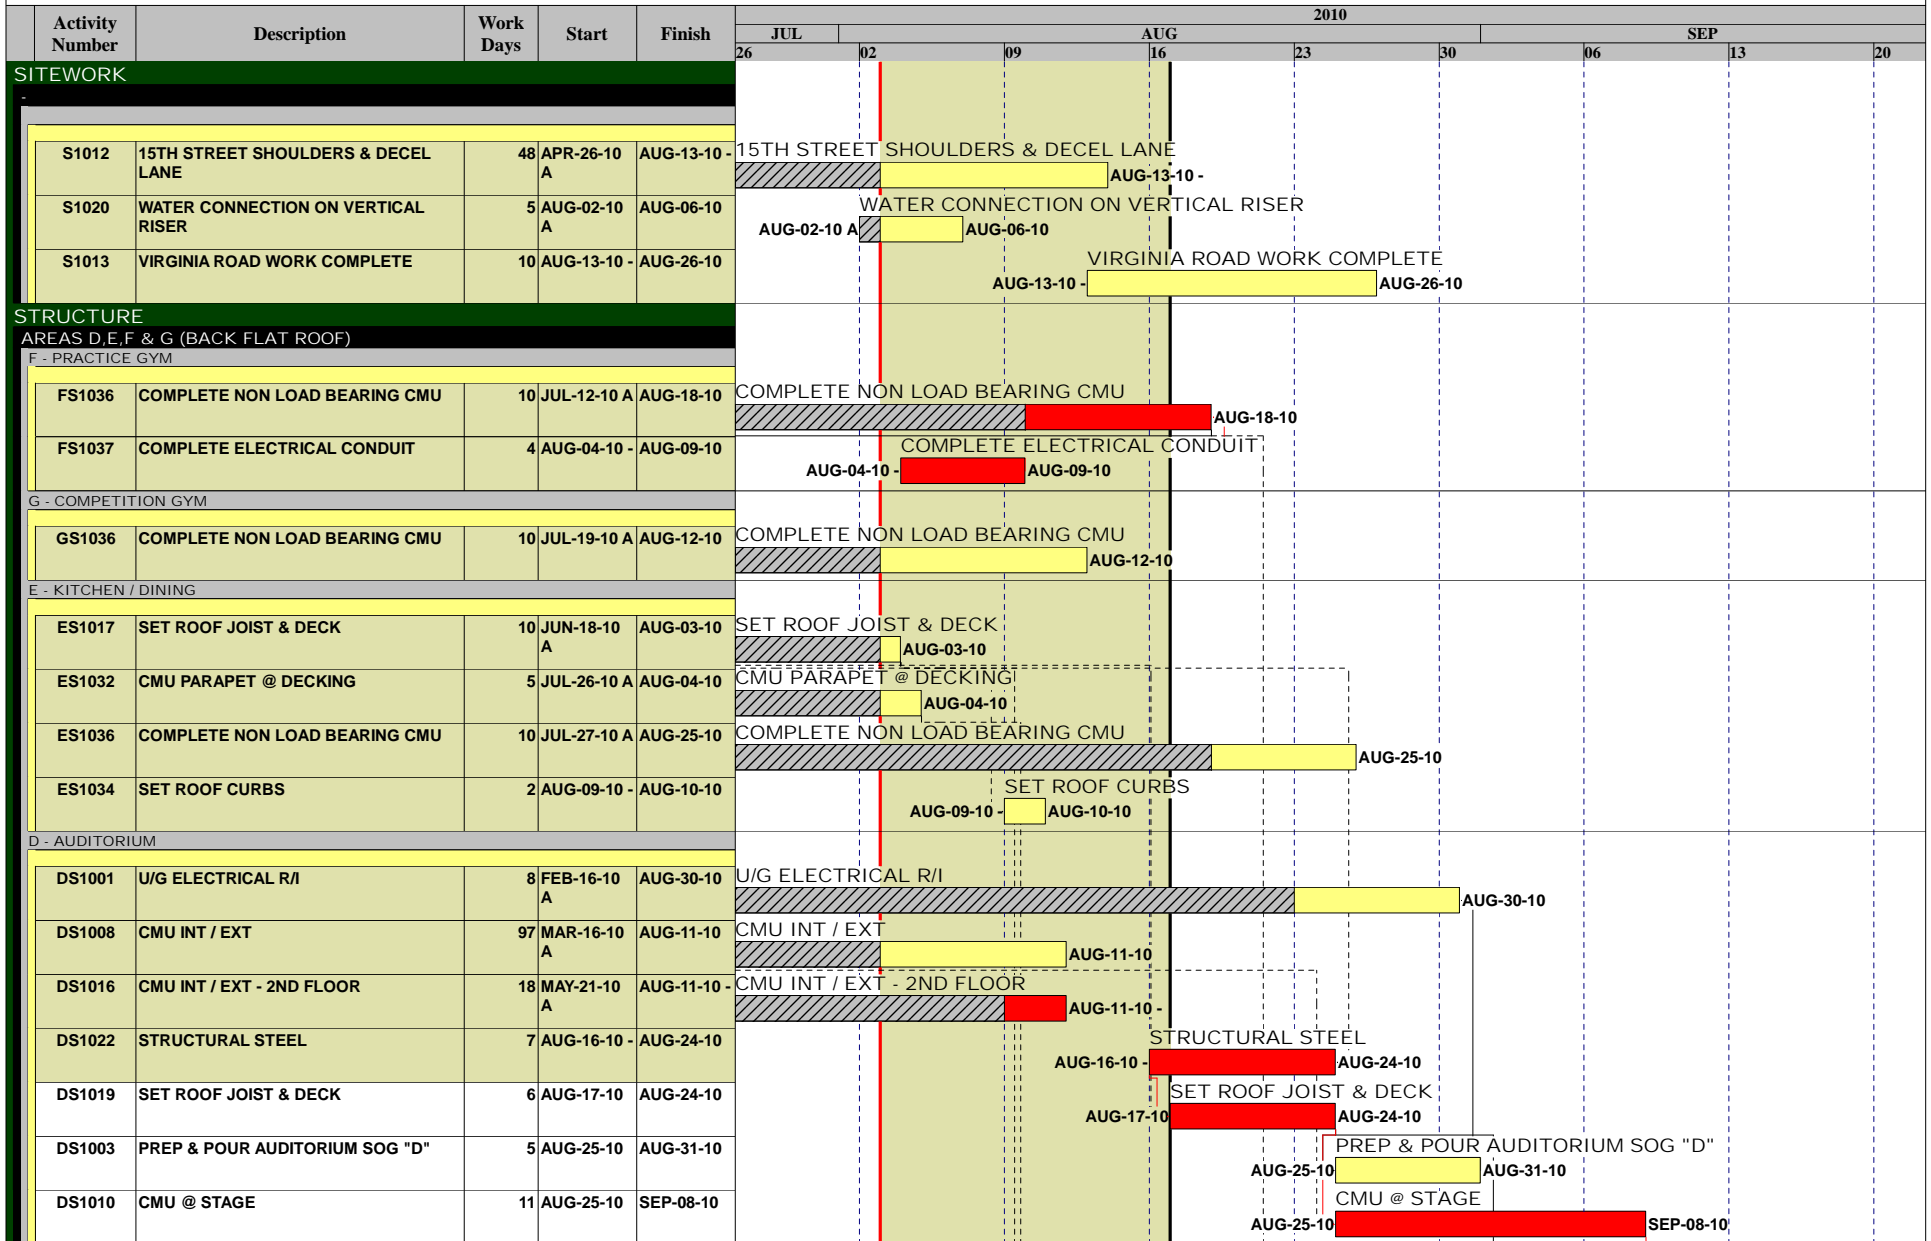


HUEYTOWN HIGH SCHOOL

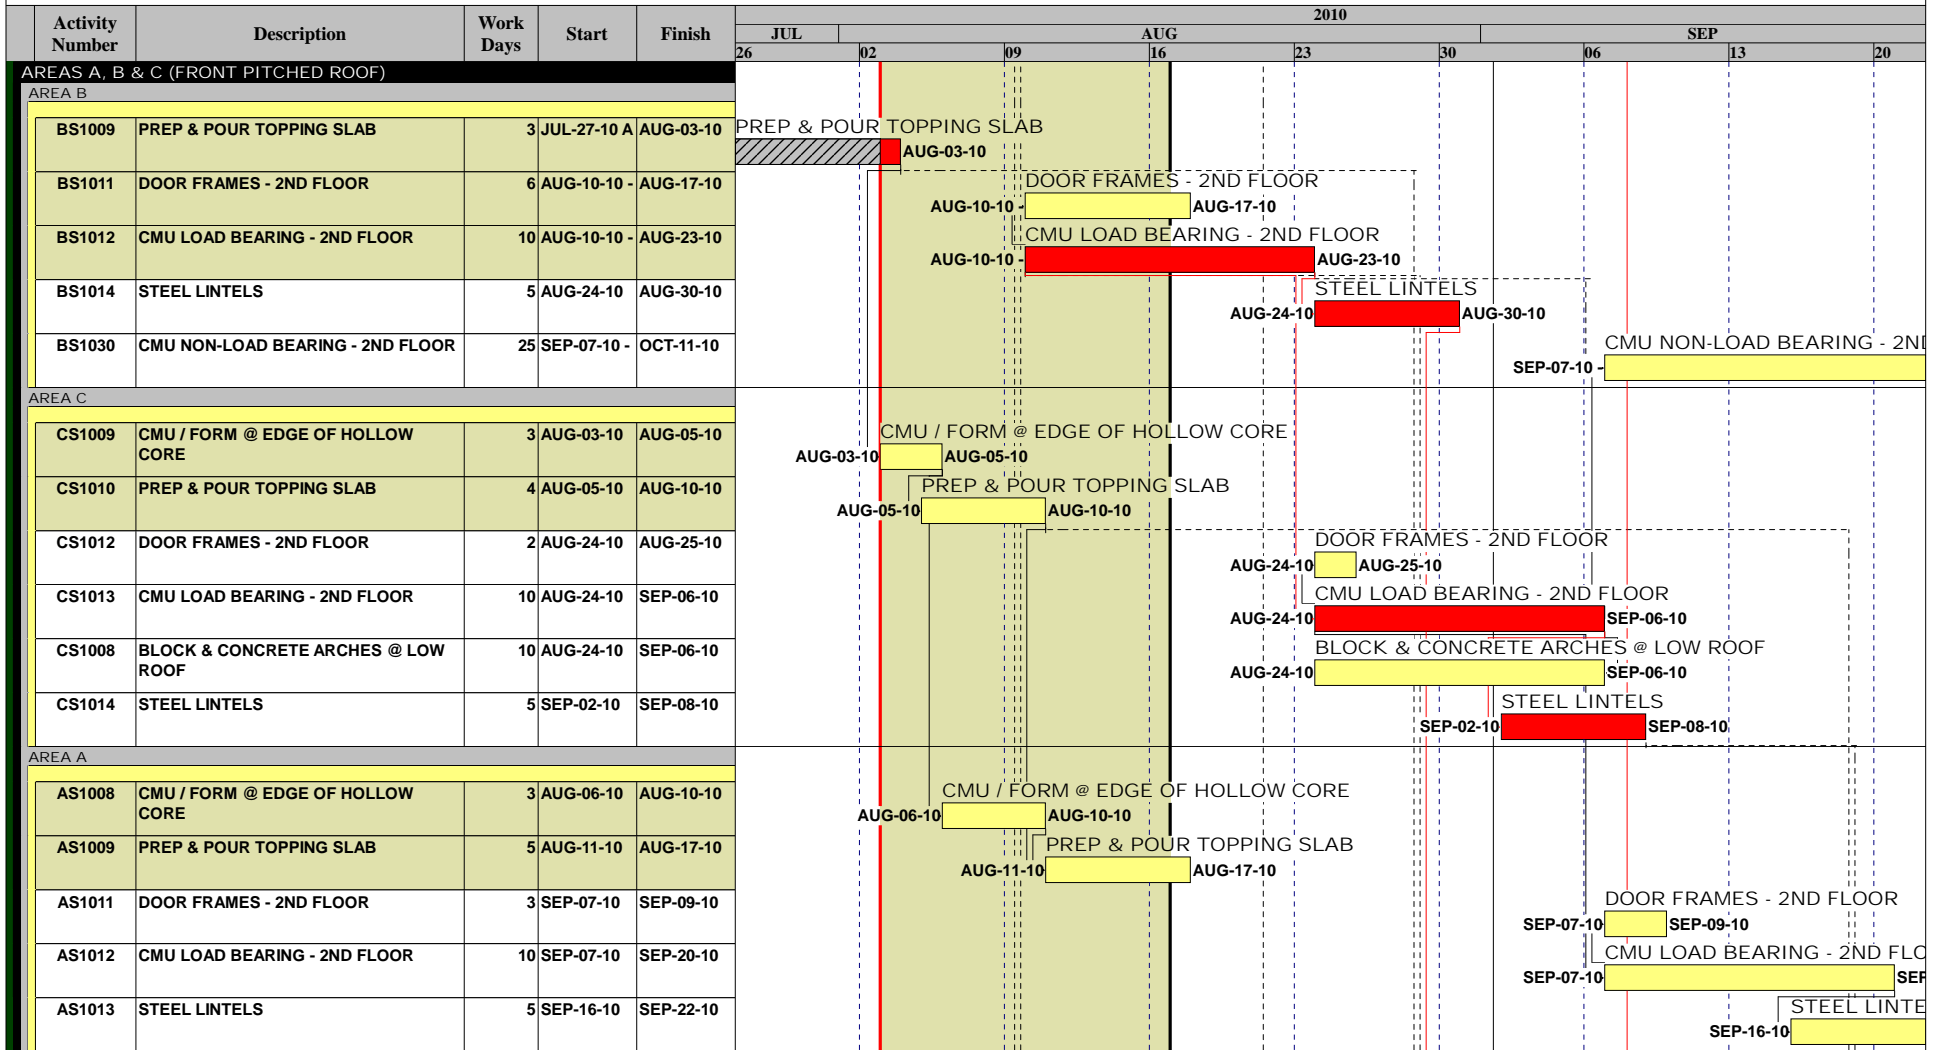


HUEYTOWN HIGH SCHOOL

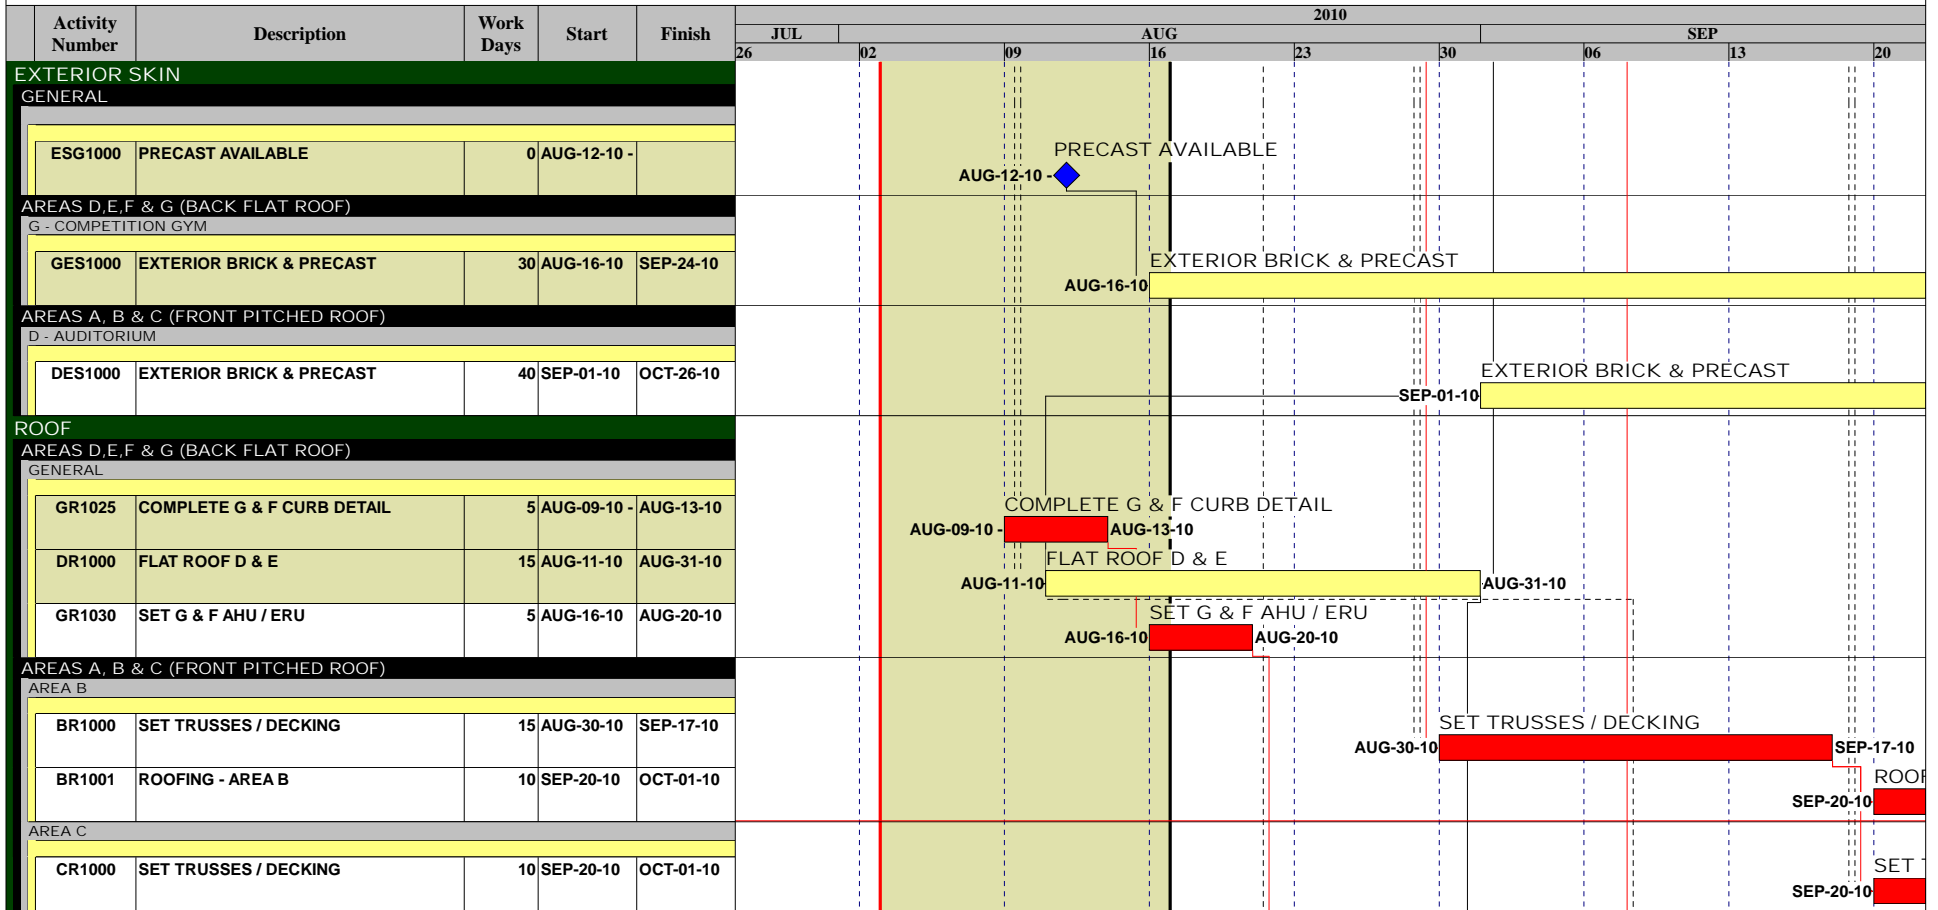

HUEYTOWN HIGH SCHOOL

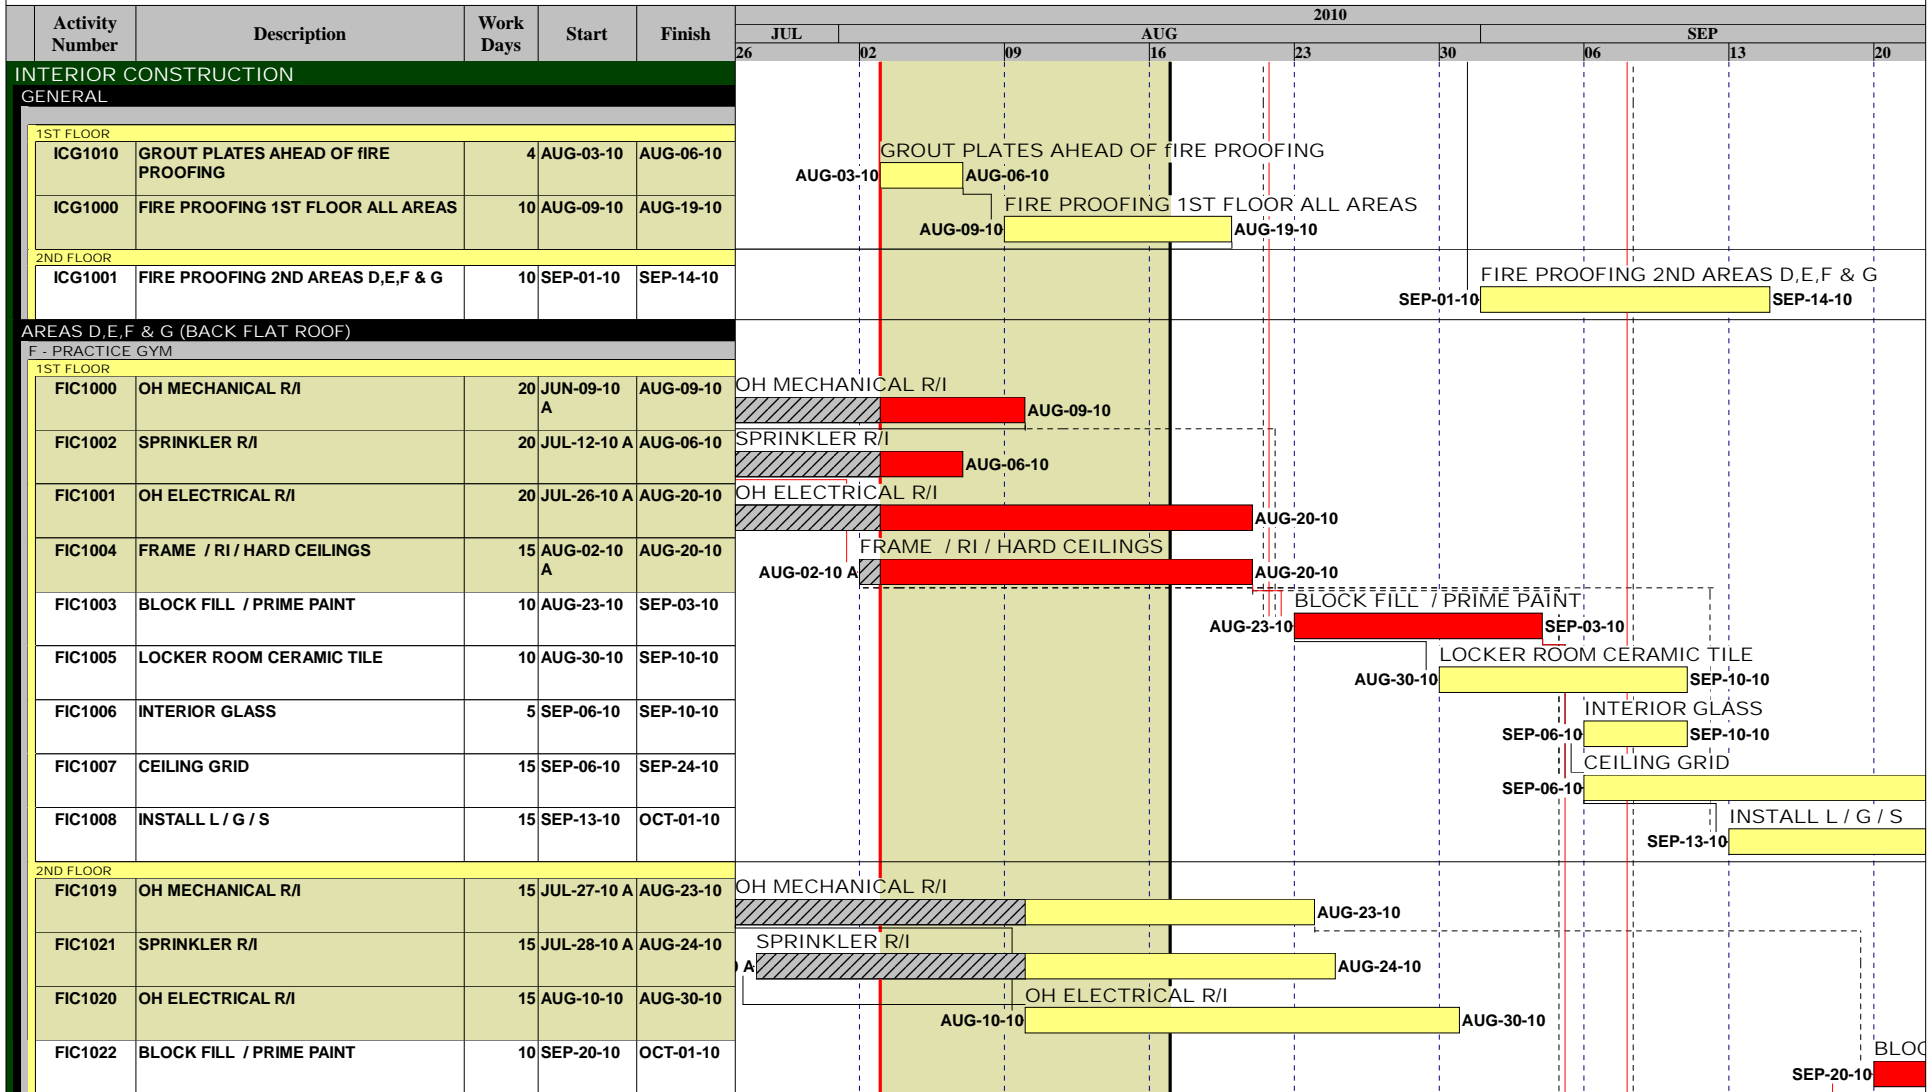

HUEYTOWN HIGH SCHOOL

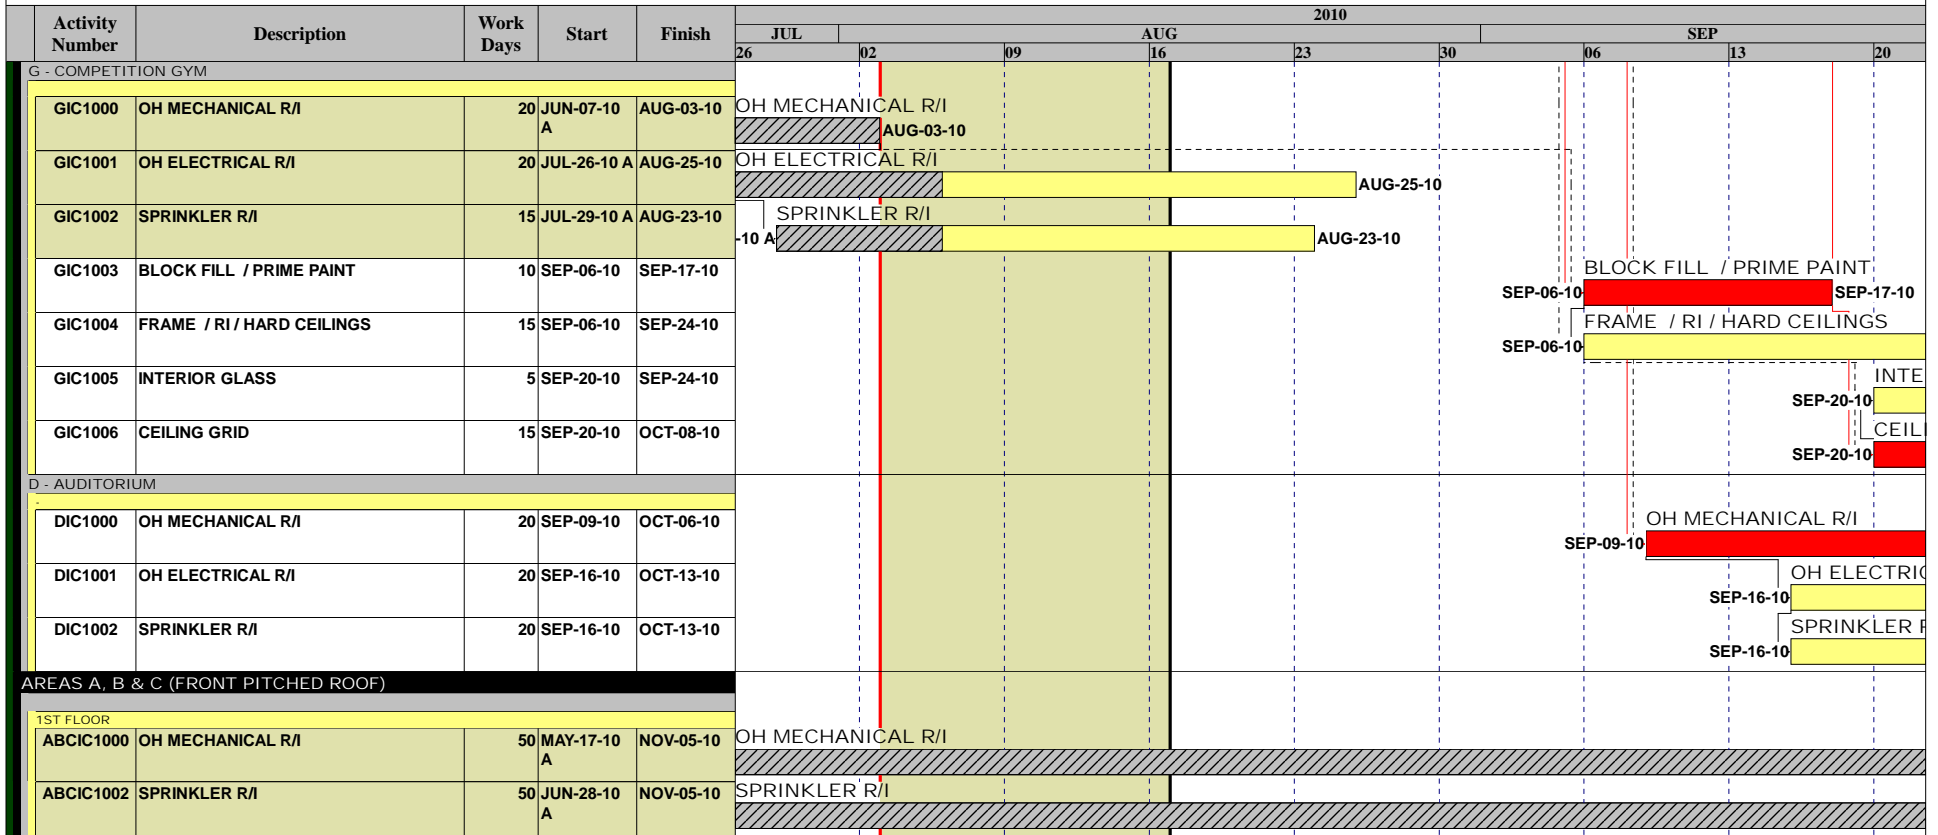

-

Distribution List Name: 29082 - Hueytown High School

Bo Hamilton	bhamilton@dunnconstruction.com
Brian Korfant	brian.korfant@roofusa.com
Donnie Hall	dhallnsons@aol.com
Elsie Cowart	ecowart@rpainc.biz
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Justin Petty	jpetty@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Mike Jones	mike.jones@roofusa.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Sue Cole	sue@dixiestorefixtures.com
Tim Robertson	trobertson@dosterconstruction.com
