

HUEYTOWN HIGH SCHOOL



PROGRESS UPDATE REPORT
September 28, 2010

DOSTER

BASELINE

CONSULTANTS, INC.

Please initial the **meeting** date to show that you were in attendance.

Hueytown High School #29082

10/12	ATTENDEES	CO. NAME	8/17	8/31	9/14	9/28
	Butch Henderson	Accurate Ele.	XX		XX	
	Steven Greeson	Automated Logic				
	Stephen Franklin	BFS		XX		
	David Bullock	Bhate				
	Cecil Smith	C.C.	XX			XX
	Jim Hacker	C.C.		XX		
	Phil Sebring	Coreslab				
	Joe Kuhn	Doster Construction	XX		XX	XX
	Josh Cronan	Doster Construction	XX	XX	XX	XX
	Justin Petty	Doster Construction	XX	XX	XX	XX
	Tim Robertson	Doster Construction	XX	XX	XX	
	Bo Hamilton	Dunn Construction				
	Jason Greene	Green Bldg		XX		XX
	A. Castillo	Green Bldg		XX		
	David Ginn	H2K	XX	XX	XX	XX
	Donnie Hall	Hall & Sons Plumbing		XX		
	Jerry Fuller	Hall & Sons Plumbing	XX		XX	
	Moe Garner	Hall & Sons Plumbing	XX	XX	XX	XX
	Don Davis	J & K Electric	XX	XX	XX	XX
	John Britton	J & K Electric	XX	XX	XX	XX
	Wayne Skinner	J & K Electric				
	Darrell Cole	P&M Mechanical				
	Jimmy Davis	P&M Mechanical				
	Joe Manning	P&M Mechanical	XX	XX	XX	XX
	Micheal Isbell	P&M Mechanical				
	Ed B.	Reliance	XX			
	Michael B. Furniss	Reliance	XX			
	David Torres	Reliance	XX			
	Brian Korfant	Roof Craft	XX		XX	
	Mike Jones	Roof Craft Systems				
	Charles Johnson	Selective Masonry	XX	XX		XX
	Jonathan Watts	Selective Masonry				XX
	Wes Smith	Selective Masonry	XX	XX	XX	XX
	Mark Smith	Simpson Plastering			XX	
	Mike Kennedy	Simpson Plastering				
	Jay Poole	SMI				
	Jesse Kelley	Southwest Water				
	Willy Shepard	Southwest Water				
	P. E.	Stankunas Construction	XX			
	Gregg Baker	T&K Construction				
	Lanny Nelson	T&K Construction				XX
	Nathaniel Hutchinson	T&K Construction				
	Steve Giddens	T&K Construction				
	Mell Gage Smith	The Mell Group				
	Joseph Dodson	United States Sprinkler	XX			
	Lee Edmonds	Baseline Consultants, Inc.	XX	XX	XX	XX

If you do not see your name, please print your name and company name in available space.

PROGRESS SUMMARY

**Hueytown High School
September 28, 2010**

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, September 28, 2010, at the Doster Construction Company jobsite trailer.

The next Progress Update Meeting will be held at 10:00 a.m. on Tuesday, October 12, 2010, at Doster Construction Company jobsite trailer.

Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.



AREAS G and F

The following summary is assumed to be a true and factual account of events that transpired in the September 28, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.

GENERAL NOTES

Justin Petty reviewed general safety issues. Mr. Petty also stated that no parking can occur outside of authorized areas unless permission is granted by Doster Construction.

SITWORK

The 15th Street and Virginia Road work has not completed. The activities prior paving are scheduled to complete by October 8, and Dunn is scheduled for paving activities to begin October 11, 2010.

Tie-in of the rain water leader laterals began installation September 20, 2010. These activities were to complete September 29, 2010. It was reported in today's meeting that rain water leaders will not be tied in complete until October 8, 2010.



AREA F

STRUCTURE

Non-load bearing CMU in Area G at the columns on the 2nd Floor is underway and will complete by September 29, 2010.

The catwalk steel at the Auditorium has been installed as far as it can go. Structural steel in this area will resume September 28, 2010. Decking in this area needs to begin on or before October 4, 2010.

The last remaining hollow core pieces at the front section of Area B will be set Monday, October 4, 2010.

CMU at the 2nd Floor of Areas A, B, and C is continuing. The CMU non-load bearing at the

2nd Floor of Area B is underway, as well as in Area C. Load bearing CMU at Area A is ongoing and is targeted to complete the week of October 4, 2010.

EXTERIOR SKIN

Installation of masonry at Areas F and G is continuing and targeted to complete October 22, 2010. Exterior masonry at Areas E and D will begin the week of October 11, 2010.

ROOF

Area D flat roof is continuing below the roof line of the high roof at the Auditorium. The Auditorium roof will begin once decking activities have progressed far enough. It is anticipated that the Area D Auditorium roof will be roofed as far as it can be by October 8, 2010.

Setting of roof trusses in Area B is complete; however, decking activities are not. Decking activities will begin October 4 and all pitched roof areas will be decked complete by October 25, 2010. Setting of trusses at Area C has begun, and trusses at Area A are to begin October 12, 2010.

Roofing activities in Area B will now begin October 11, 2010. Roofing activities for Areas A, B, and C are to be complete by mid- November 2010.

INTERIOR CONSTRUCTION

Provided roofing in Area B is installed substantially complete by October 25, 2010, overhead rough-ins in the 2nd Floor Section B will begin at that time.

Rough-ins at the 1st Floor of Areas A, B, and C have made minimal progress over the past two weeks. Ductwork and sprinkler rough-ins in this area are tracking ahead of schedule. Overhead electrical rough-ins in this area are underway.

Area F practice gym overhead rough-ins are targeted to be complete by the week of October 11, 2010. Dry-fall painting in this area is scheduled to begin the week of October 18, 2010. Hanging of hard ceilings in the locker room areas will now begin Monday, October 4, 2010. Ceramic tile is scheduled to start the week of October 11, 2010.



AREA A—2nd FLOOR



AREA D—AUDITORIUM

Block fill activities in Area G will be available to start Friday, October 8, 2010. Block fill activities at the 2nd Floor of Area F will begin by the end of the week.

In Area E, the kitchen hood was not installed. This hood needs to be installed so that mechanical and sprinkler rough-ins above ceiling in this area can be completed.


No progress with overhead rough-in in Area D/ Auditorium has occurred and will not until the deck at the Auditorium roof is installed.

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated September 28, 2010.


Hueytown High School

ACTION ITEM LIST						MEETING DATE: September 28, 2010
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	4.	Brick Color Boards	SMI	03/18/10		Build final mock-up on building in place
06/22/10	13.	South West Water Company	SWWC	06/22/10	project end date	Issue install schedule - work ongoing


HUEYTOWN HIGH SCHOOL

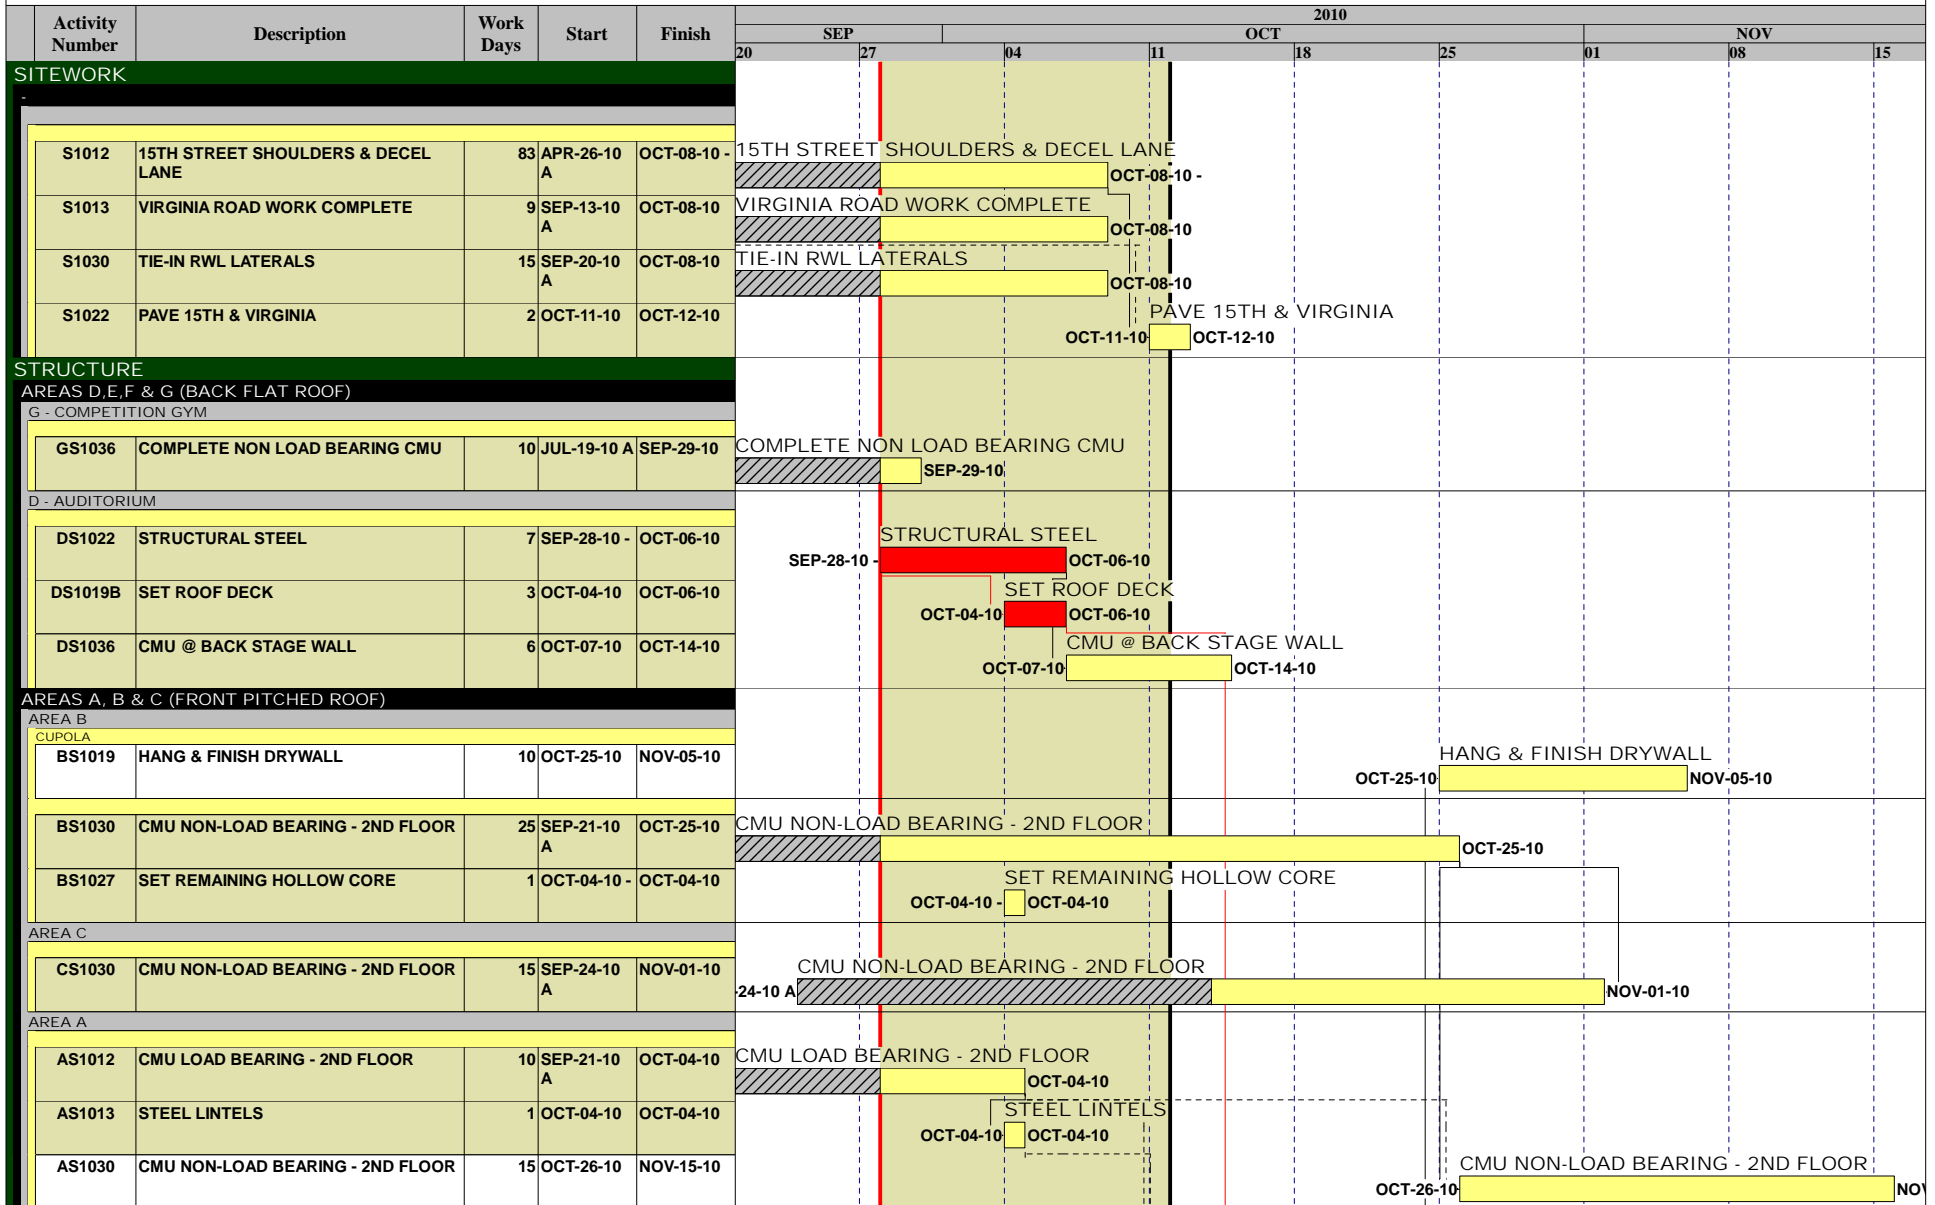


HUEYTOWN HIGH SCHOOL

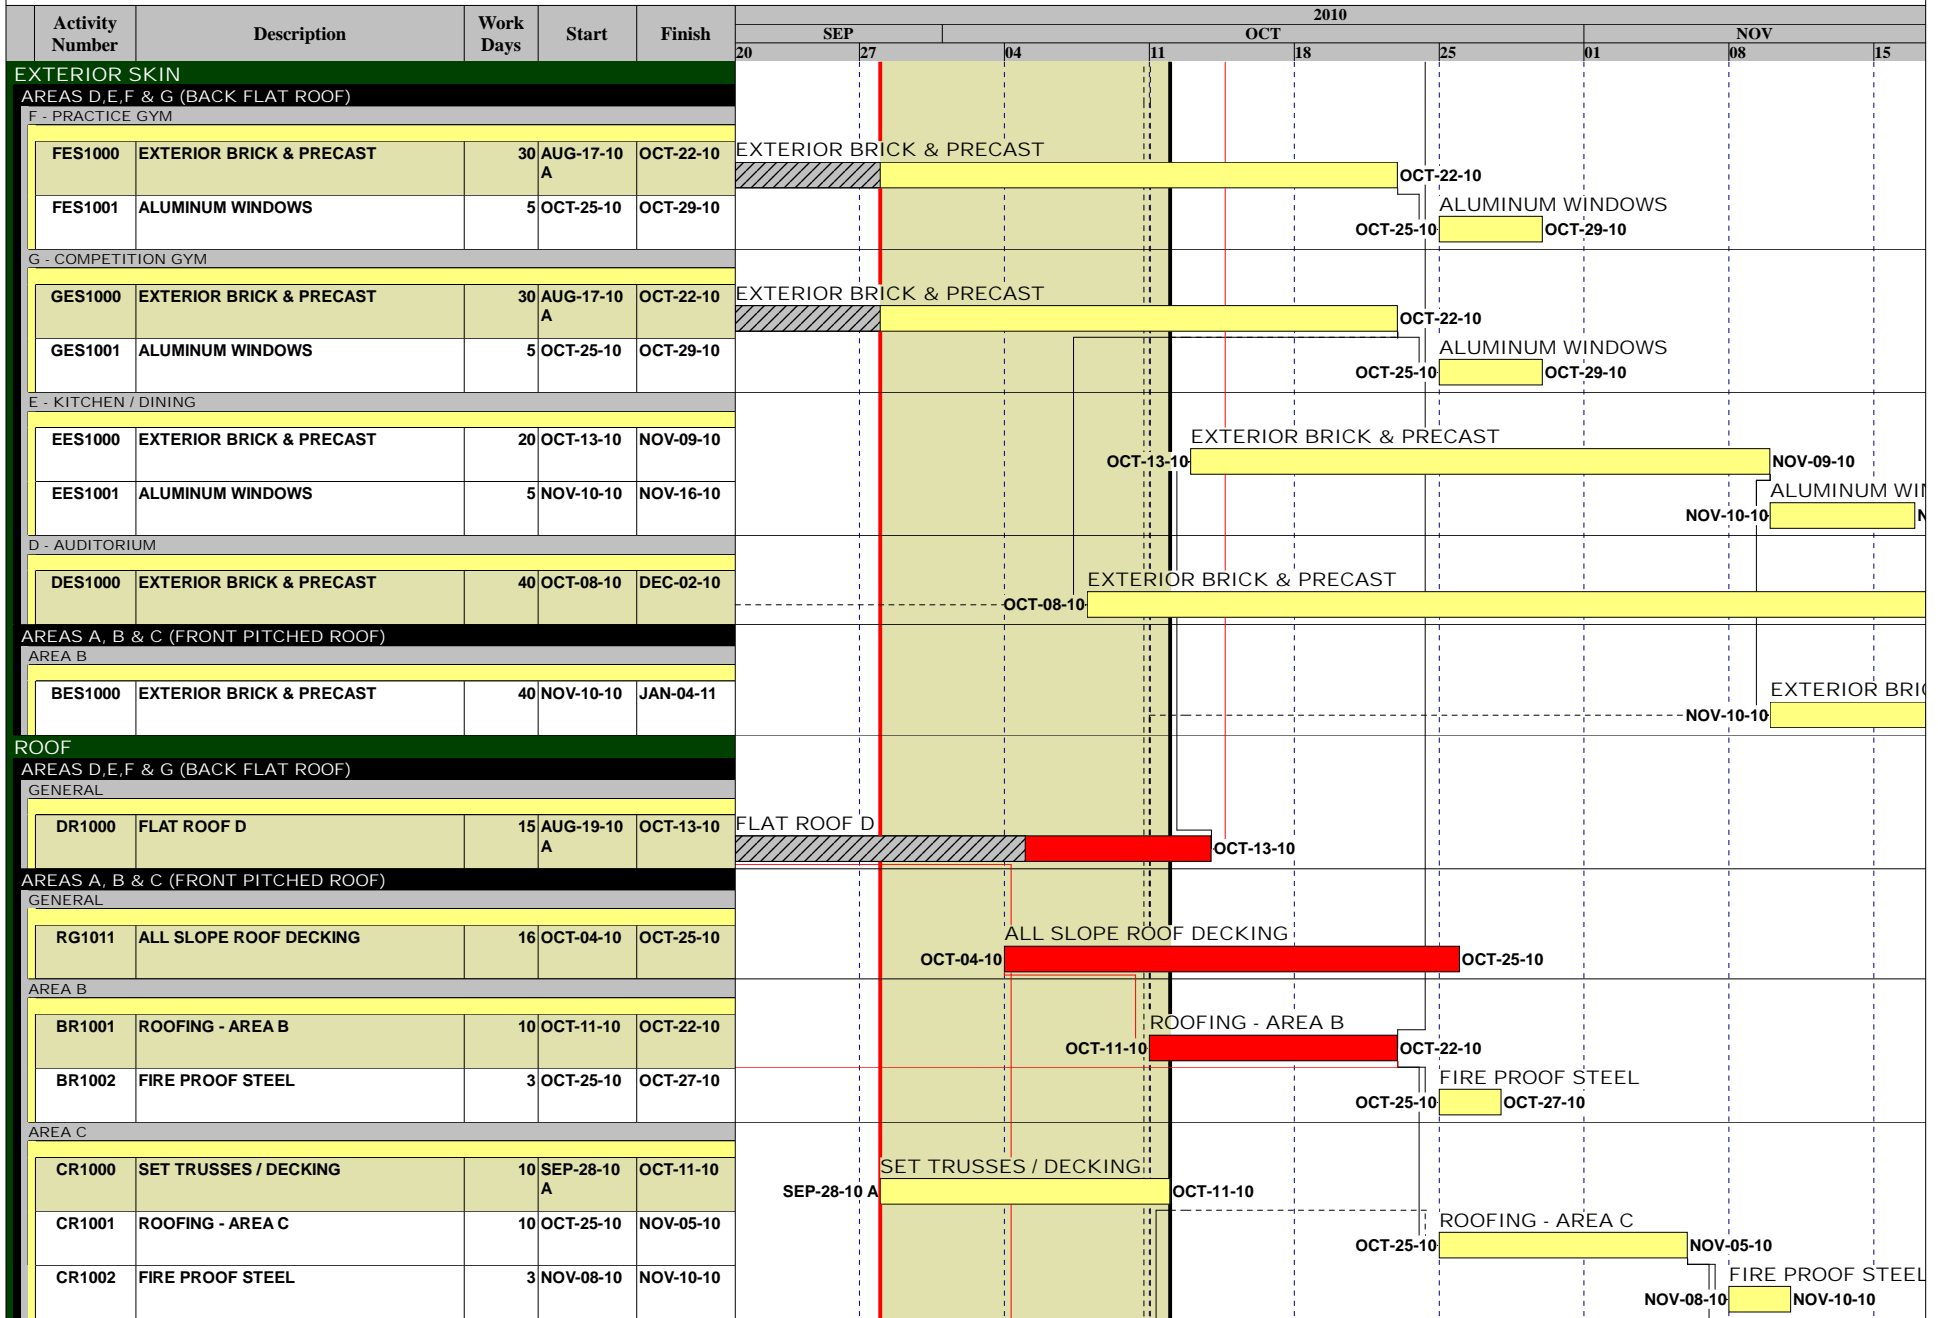


HUEYTOWN HIGH SCHOOL

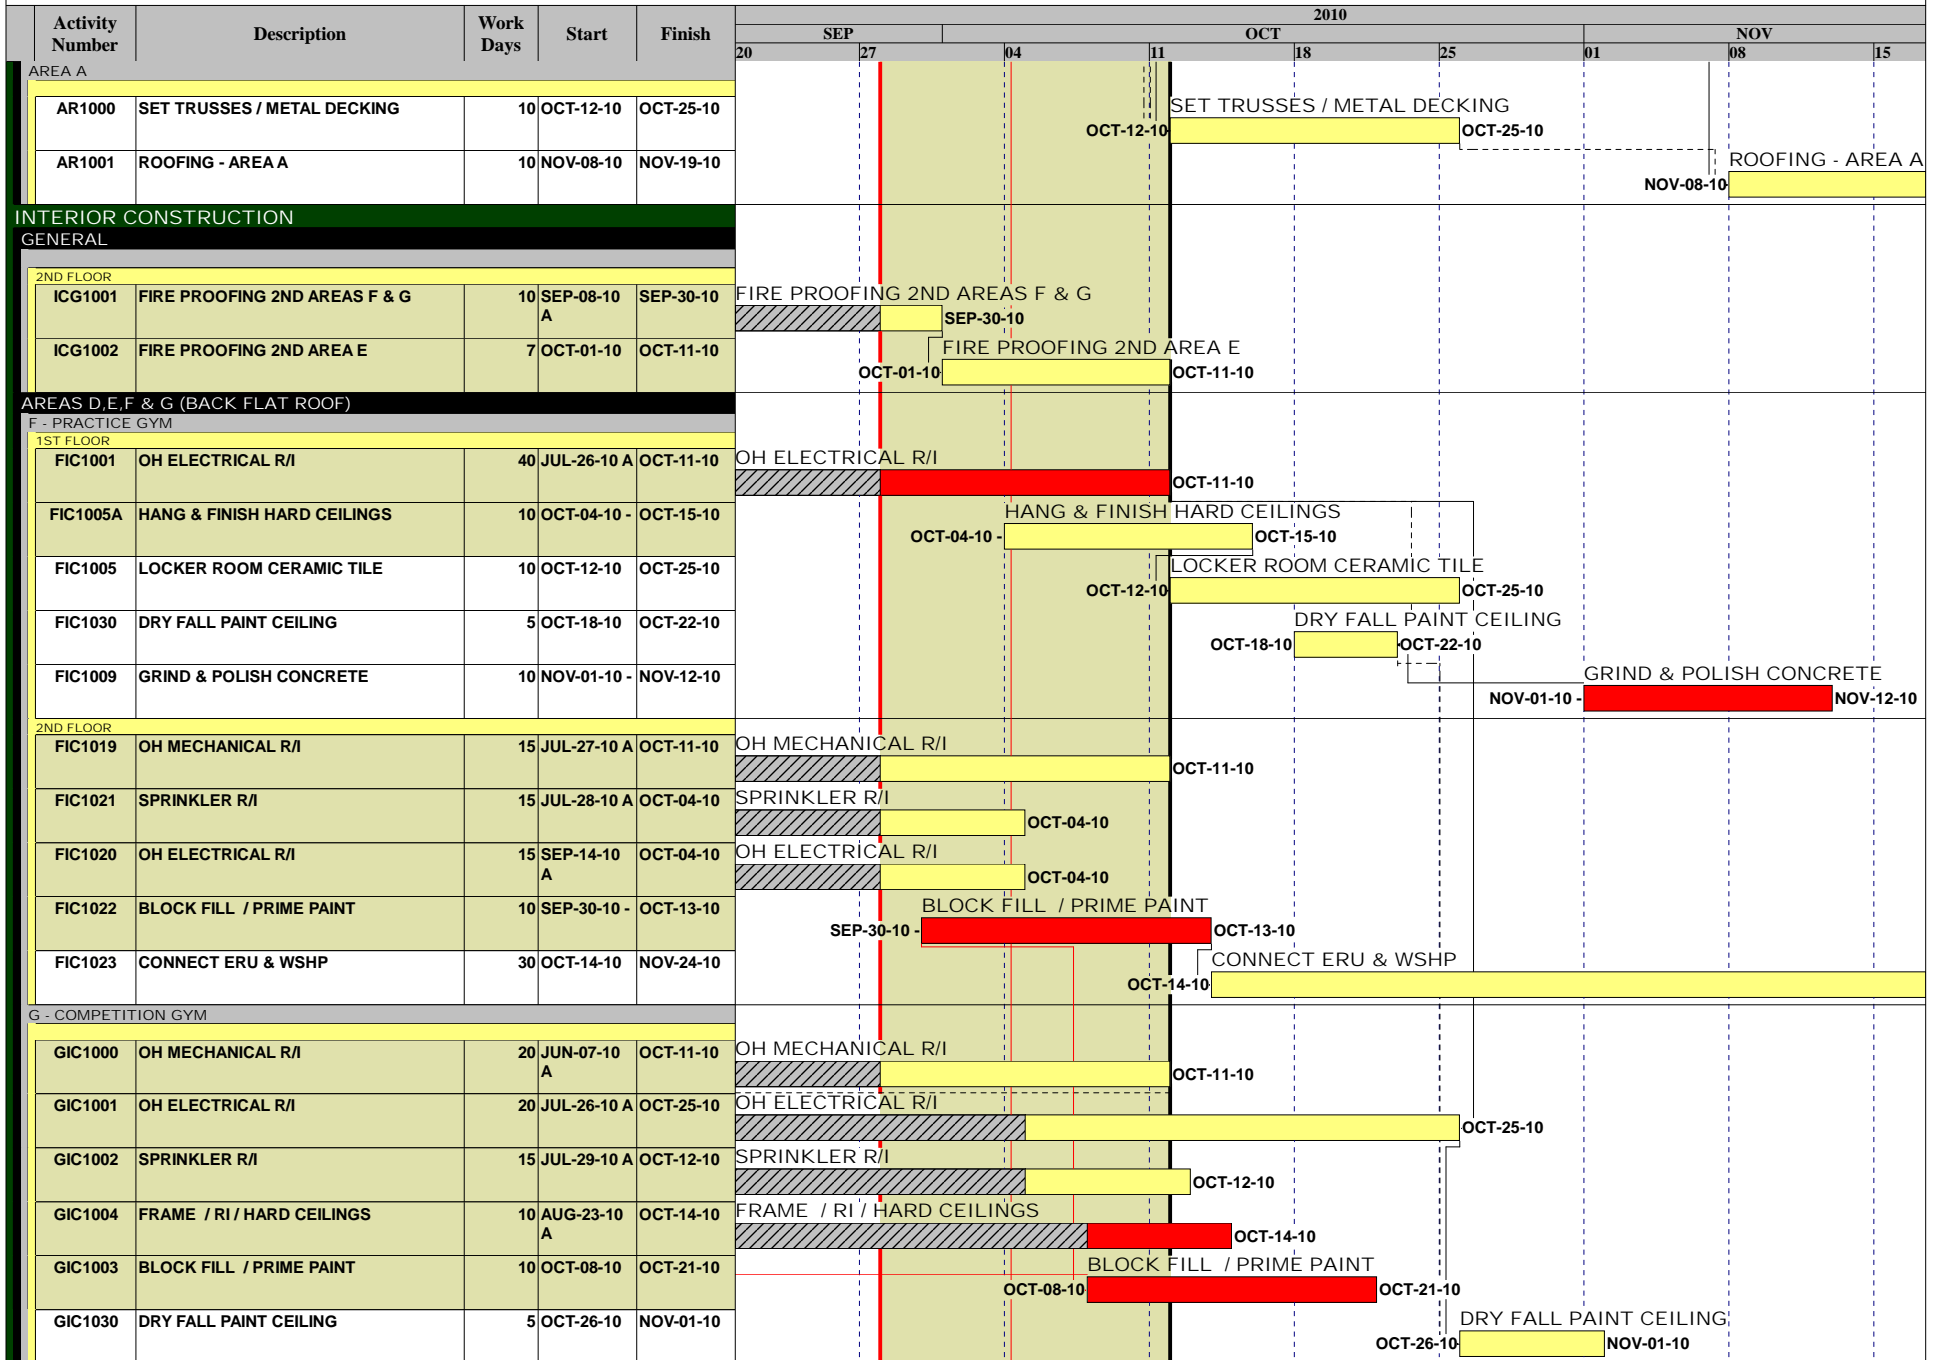

HUEYTOWN HIGH SCHOOL

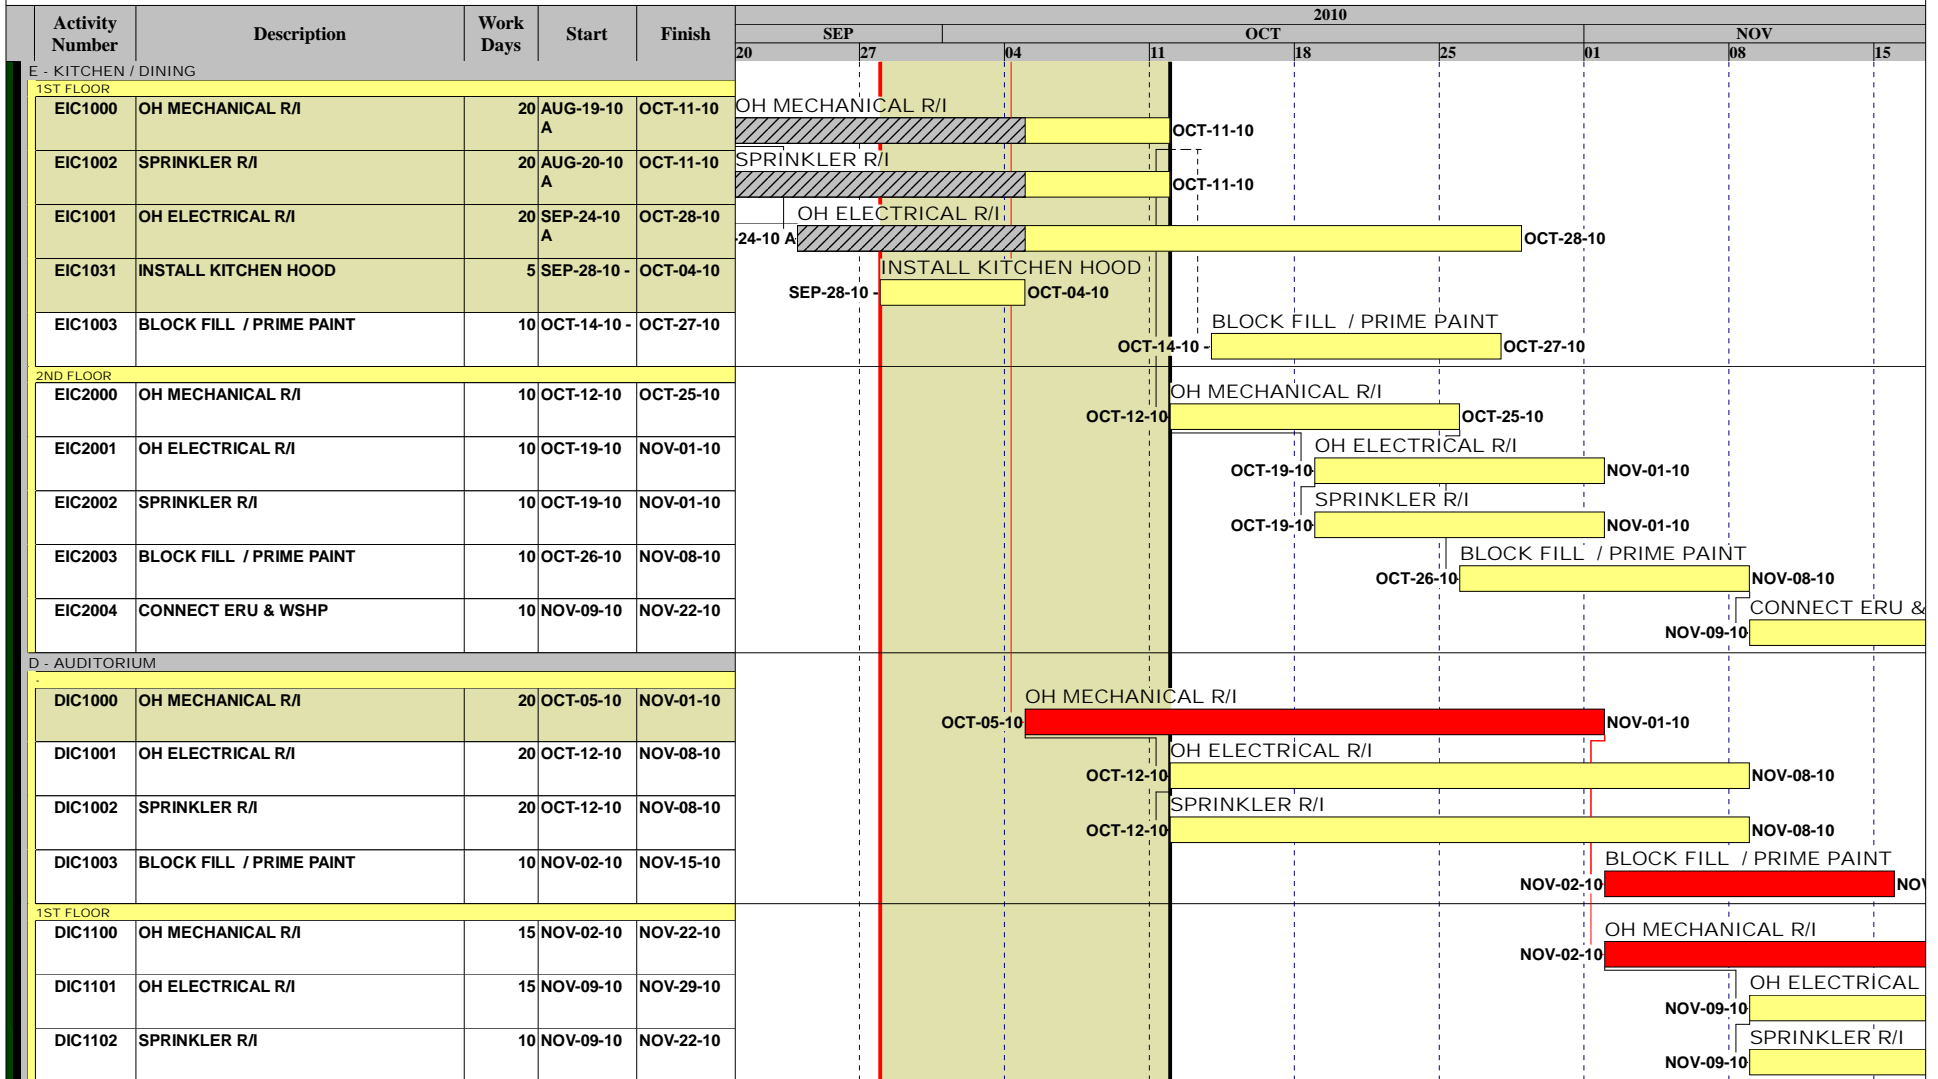

HUEYTOWN HIGH SCHOOL

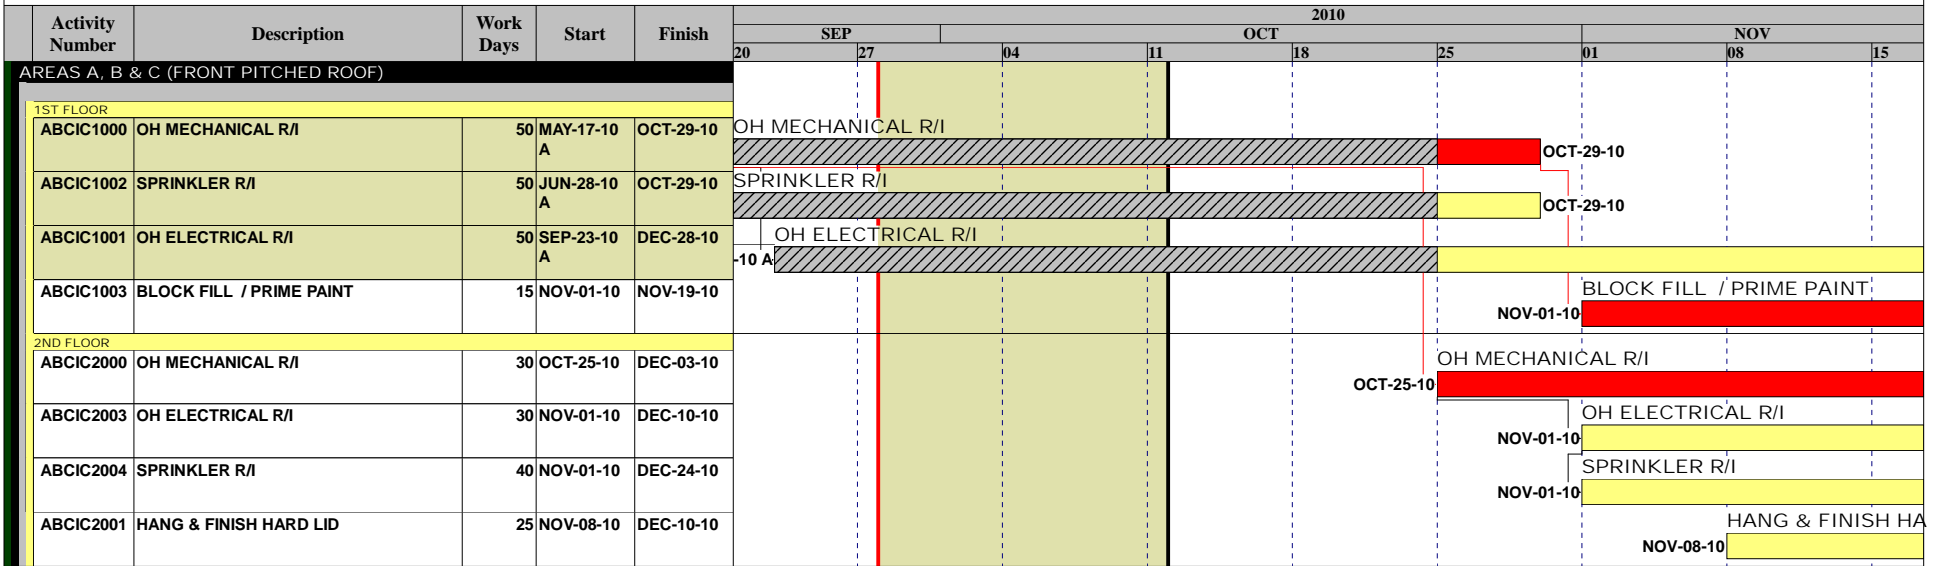

Distribution List Name: 29082 - Hueytown High School

Bo Hamilton	bhamilton@dunnconstruction.com
Brian Korfant	brian.korfant@roofusa.com
Donnie Hall	dhallnsons@aol.com
Elsie Cowart	ecowart@rpainc.biz
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Justin Petty	jpetty@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Mike Jones	mike.jones@roofusa.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Sue Cole	sue@dixiestorefixtures.com
Tim Robertson	trobertson@dosterconstruction.com
