

# HUEYTOWN HIGH SCHOOL



**PROGRESS UPDATE REPORT**  
**March 16, 2010**

---

**DOSTER**

**BASELINE**  
  
**CONSULTANTS, INC.**



## PROGRESS SUMMARY

Hueytown High School  
March 16, 2010

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, March 16, 2010, at the Doster Construction Company jobsite trailer.

**The next Progress Update Meeting will be held at 1:30 p.m. on Tuesday, March 30, 2010, at Doster Construction Company jobsite trailer.**

**Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.**

**The following summary is assumed to be a true and factual account of events that transpired in the March 16, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.**



**AREA F—PRACTICE GYM**

### **GENERAL NOTES**

Tim Robertson of Doster Construction Company reiterated safety issues that were addressed during the weekly safety meeting held at 9:00 a.m. every Tuesday morning. Mr. Robertson stated that all scaffold must be checked daily. All personnel must have personal protection equipment to work on the project.

### **SITWORK**

The asphalt base at the north lot did not begin due to curbing activities not being completed. These activities will complete so that asphalt base in this area can begin March 22, 2010. Asphalt base at the south loop road is scheduled to be installed the same week as the north lot. Asphalt base at the remaining loop road will follow.



**AREA G—COMPETITION GYM**

Cooling towers are scheduled to be on site March 17, 2010. Joe Manning with P&M Mechanical will follow-up with the cooling tower vendor to insure an on-schedule delivery.

### **STRUCTURE**

The slab-on-grade for Area D building has not been prepped for pour as previously scheduled. This pour is now targeted for April 2, 2010. Foundation CMU and orchestra pit work will need to be installed over the next two weeks in conjunction with the electrical rough-ins, so that Area D can be poured by April 2, 2010. The hollow core at Areas F and G has been set, grouted, and the topping slab placed. CMU work at the 2nd Floor of Area F building will

begin today. Setting of the low roof trusses at Area F building will occur by Tuesday, March 23, 2010. Pre-roof conference will be held at 10:00 a.m. on March 30, 2010. Following this conference, installation of the low roof above the switchgear will need to begin.

The CMU stairwells for 2nd Floor access will be complete by Friday, March 19, 2010. Installation of the stairs will begin March 22, 2010. CMU at the 2nd Floor of Area G will begin the week of March 22, 2010.

The forming and pouring of the concrete columns and elevated slab at the cupola will now complete March 17, 2010. Cupola steel erection is ongoing at the ground level and will be clad and constructed as far as possible until it is set on the cupola concrete structure. It is anticipated that the cupola will be set March 29, 2010.



**AREA E—KITCHEN/DINING**

Foundations in Area B that were to complete on March 5, 2010, have been hampered due to weather. These foundations will now complete March 26, 2010. The slab in Area B will begin prep work April 19, 2010, and be poured just ahead of setting of hollow core.

The slabs in Areas C and A will follow and be installed just prior to setting of hollow core for the 2nd Floors. Underground plumbing work in Area C is ongoing and foundation work has not started. Foundation work in this area will begin on or before March 29, 2010. Foundation work in Area A will follow Area C.

#### **ACTION ITEMS**

Settlement plate #3 was not installed by Friday, March 5, 2010. This settlement plate is now scheduled to be installed by March 17, 2010. Settlement plate #3 is at the ball field.

The brick color boards have been identified. A final mock-up is to be built as soon as possible and brick color range and design is to be issued immediately following construction and review of the mock-up.

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated March 16, 2010.




**AREA D—AUDITORIUM**


## Hueytown High School

ACTION ITEM LIST						MEETING DATE: March 16, 2010
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	3.	Precast Shop Drawings	Watts	02/22/10	03/18/10	Issue remaining precast shop drawings
12/16/09	4.	Brick Color Boards	SMI Bryant	03/18/10 03/18/10		Build final mock-up Issue brick color design
01/05/10	5.	Water Meter C.O.R.	Lathan	01/06/10	03/18/10	Issue change order (who furnishes meter?)
02/02/10	7.	Temporary Construction & Primary Power	Britton APCO	03/15/10 03/05/10		Install power Issue design
02/02/10	8.	Stage Lighting & Equipment	Stage Light	02/23/10	03/17/10	Issue submittals to team
03/02/10	9.	Settlement Plate	T&K	03/05/10	03/17/10	Install and monitor (at ball field)


# HUEYTOWN HIGH SCHOOL

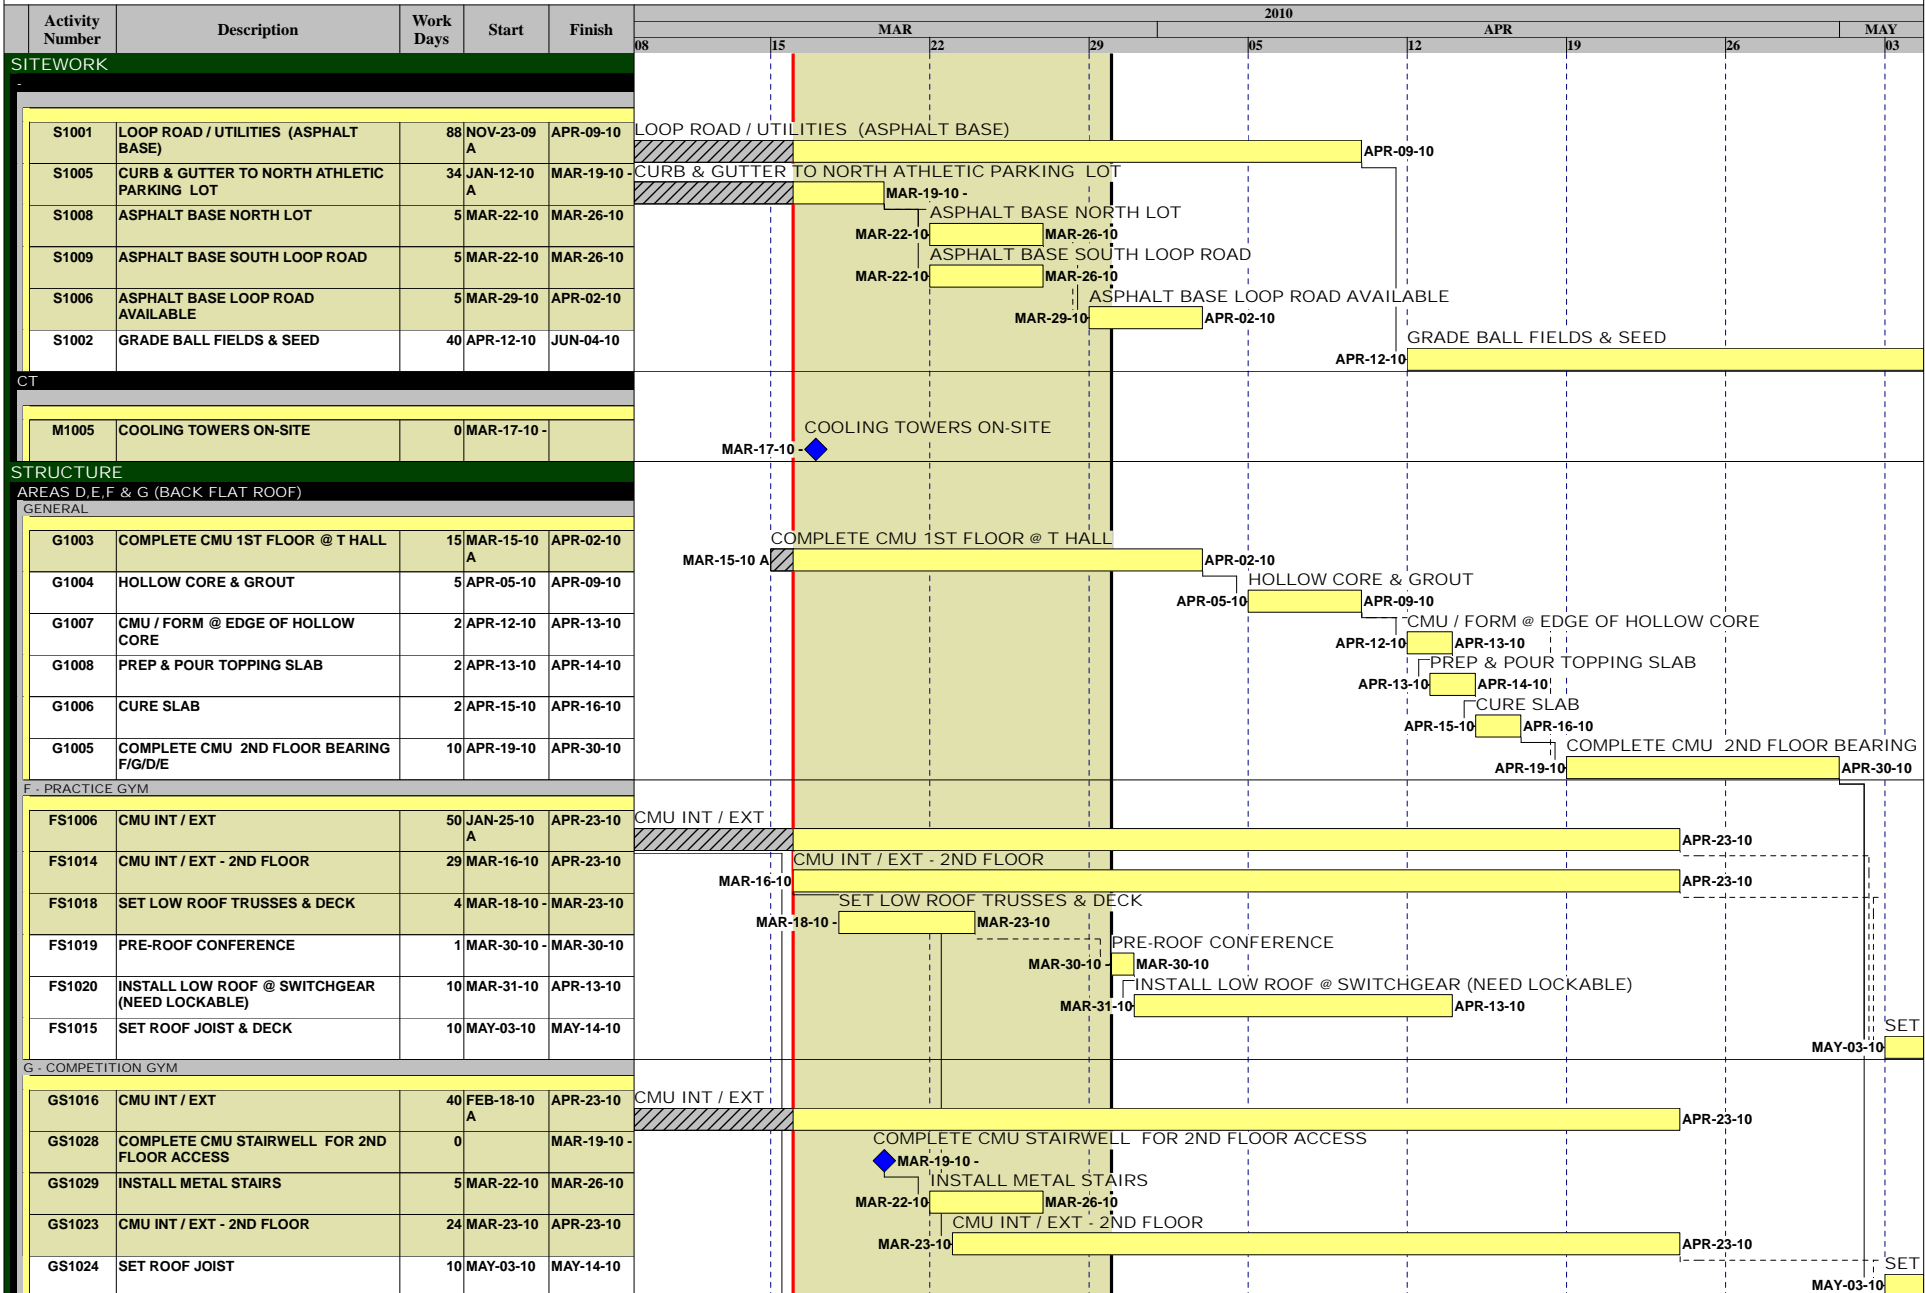


# HUEYTOWN HIGH SCHOOL

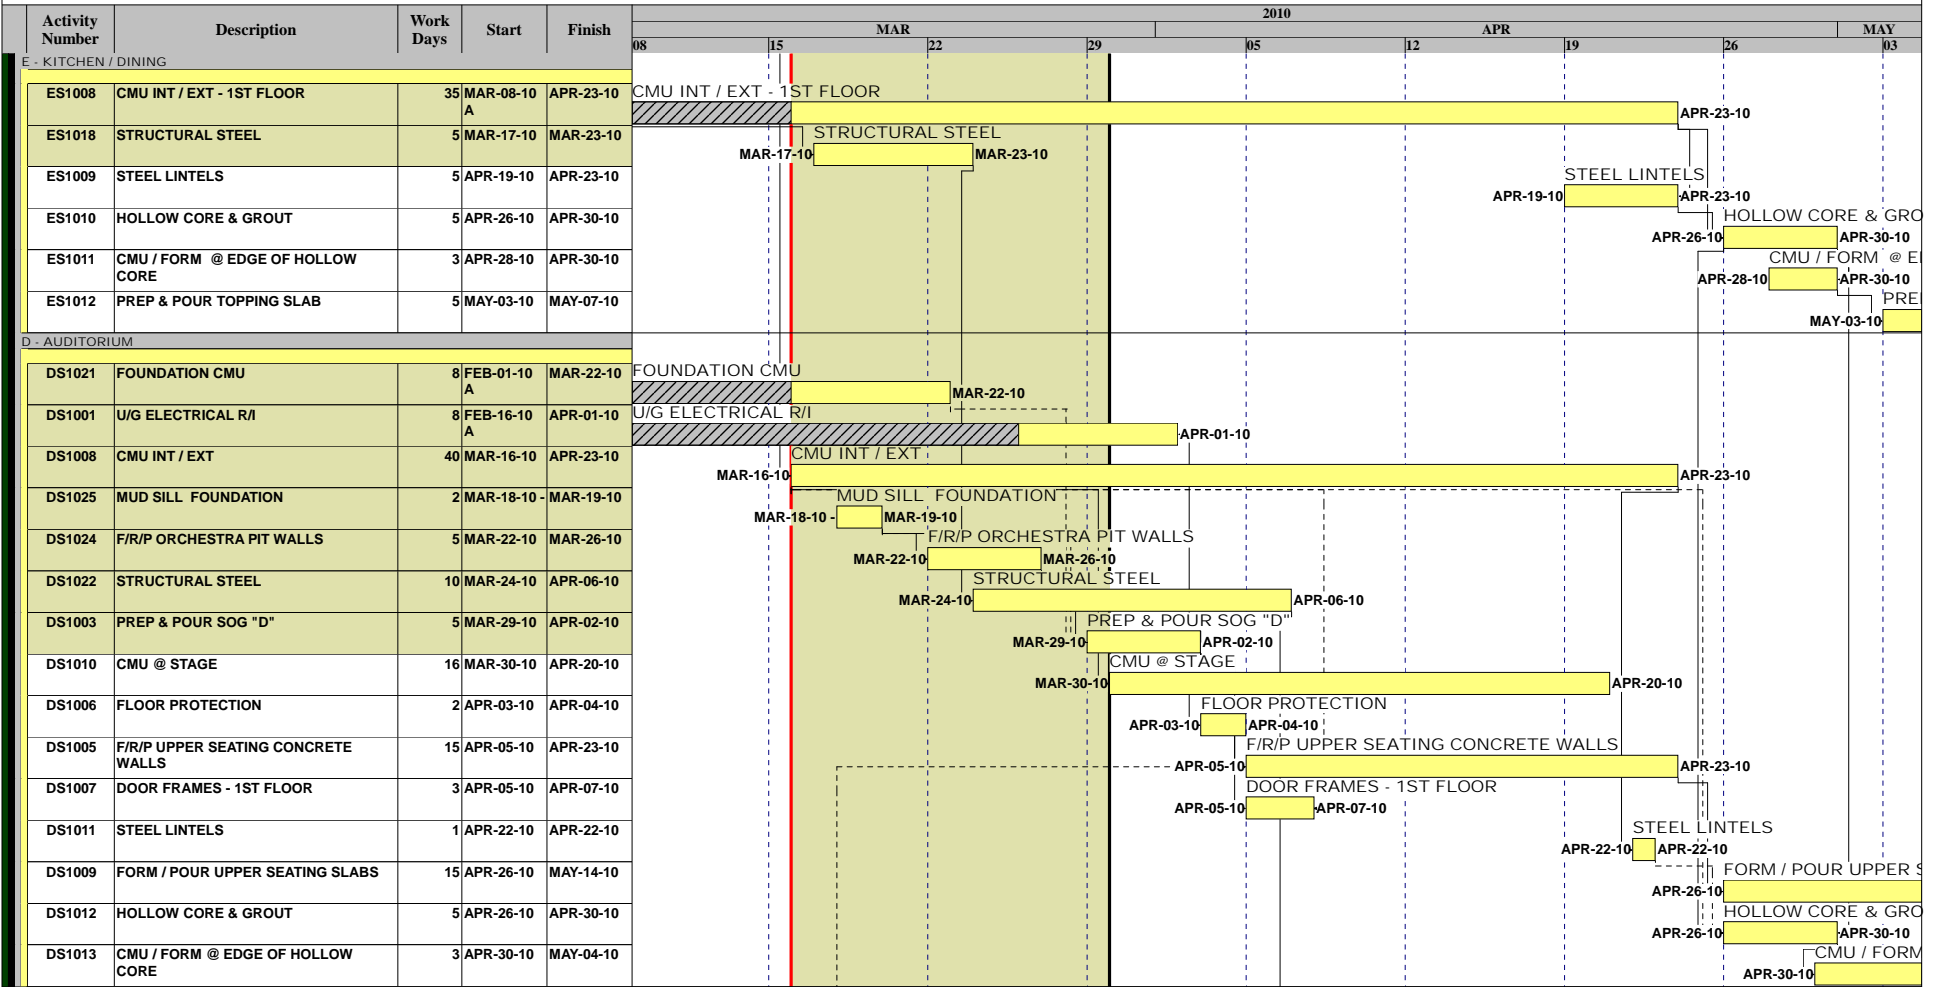

# HUEYTOWN HIGH SCHOOL

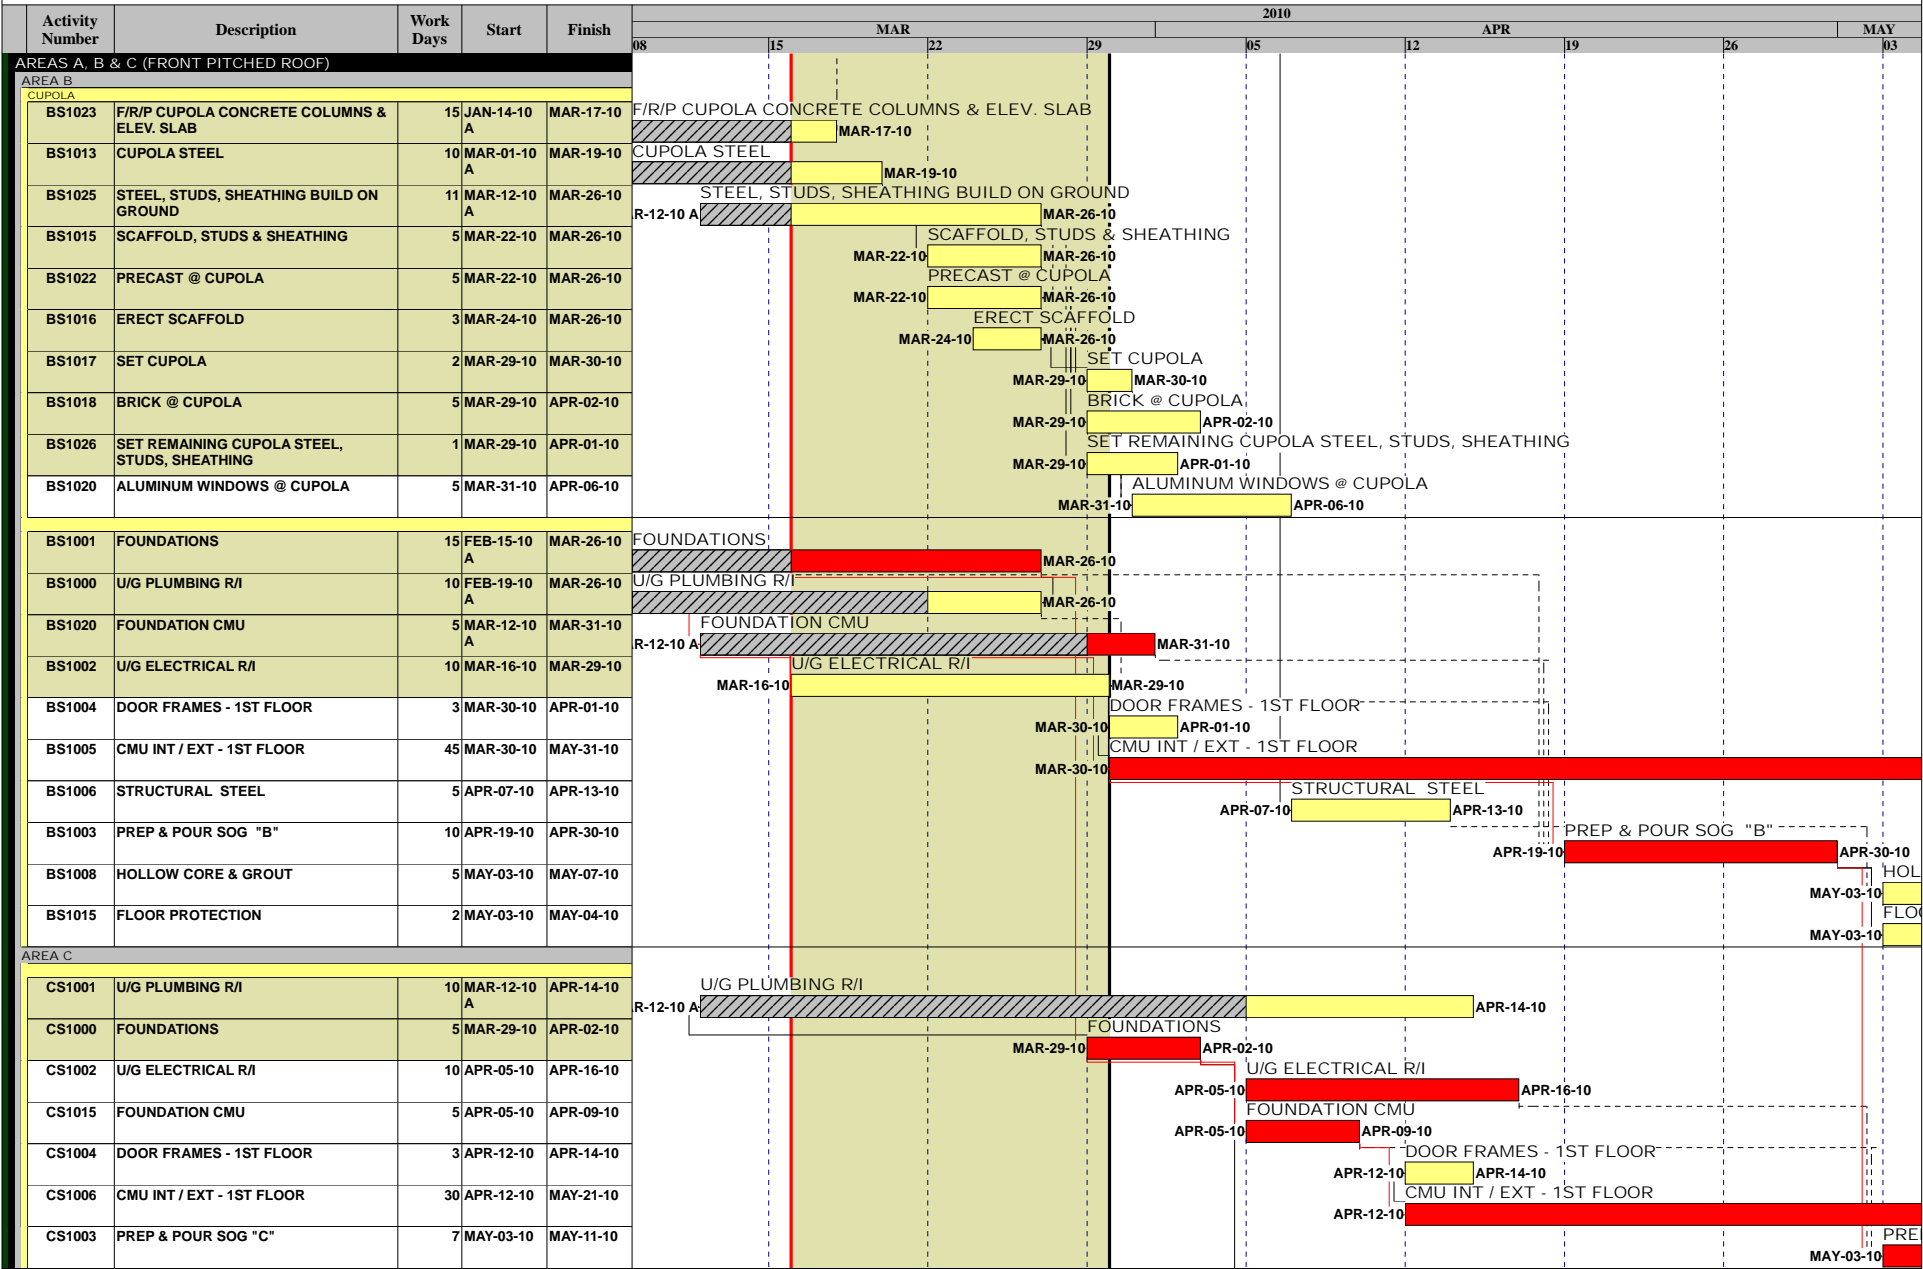

# HUEYTOWN HIGH SCHOOL

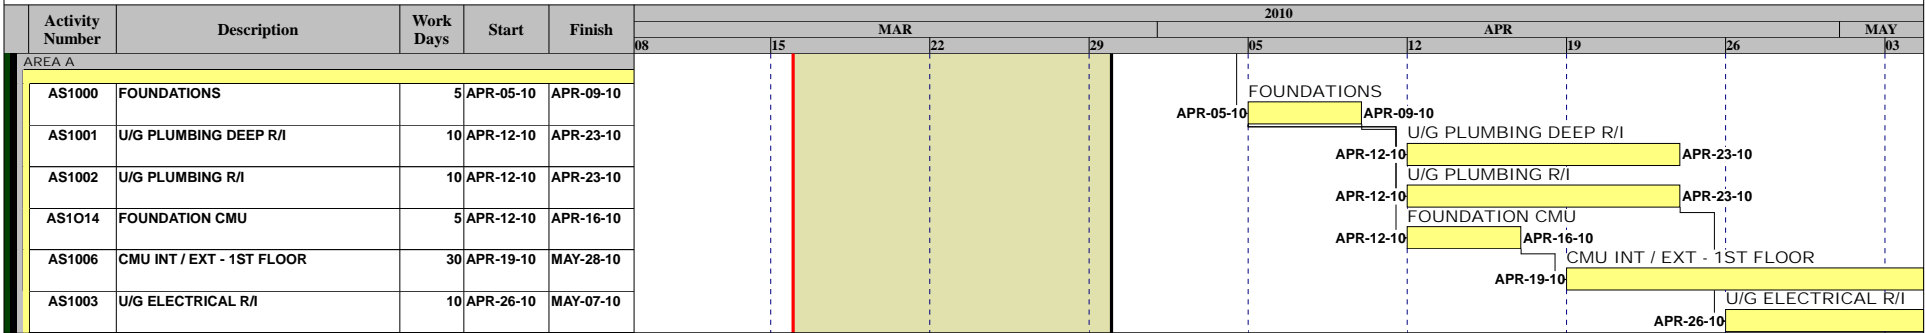

-

**Distribution List Name: 29082 - Hueytown High School**

Bo Hamilton	bhamilton@dunnconstruction.com
Donnie Hall	dhallnsons@aol.com
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Tim Robertson	troberson@dosterconstruction.com
