

HUEYTOWN HIGH SCHOOL



PROGRESS UPDATE REPORT
March 2, 2010

DOSTER

BASELINE

CONSULTANTS, INC.

PROGRESS SUMMARY

**Hueytown High School
March 2, 2010**

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, March 2, 2010, at the Doster Construction Company jobsite trailer.

The next Progress Update Meeting will be held at 10:00 a.m. on Tuesday, March 16, 2010, at Doster Construction Company jobsite trailer.

Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.

The following summary is assumed to be a true and factual account of events that transpired in the March 2, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.



AREA F—1st FLOOR

SITWORK

Loop road grading is continuing. The asphalt base and first coarse paving has been installed at the east parking lot. The next area for asphalt base and first coarse paving will be installed at the north parking area the week of March 19, 2010. Following this area, loop road asphalt base will be installed.

Cooling tower work has been completed and cooling towers are scheduled to be on site March 17, 2010.

STRUCTURE

The balance of Areas D and E structural steel has been delivered, as well as the joist steel for Areas F and G.



AREA E—KITCHEN/DINING

CMU work is continuing in Area F practice gym and hollow core installation has begun. Hollow core setting and grouting is to be complete this week and edge forming at the hollow core and CMU will begin March 3, 2010. The topping slab for this area is targeted to be poured by March 8, 2010. Work in Area F and Area G will be ongoing concurrent relative to hollow core and topping slab work.

Area E kitchen slab-on-grade has been poured. Flooring protection has not been installed as scheduled. Mr. Robertson stated that delaying of floor protection is impacting the ability of CMU to start in this area. Provided that floor protection is installed this week, CMU installation will begin Monday, March 8, 2010.

Area D—Auditorium CMU foundation work will be complete by the end of the week. Mud seal slab work will be poured between Friday, March 5 and Monday, March 8, 2010. The remainder of the slab will be poured following the installation of the orchestra pit walls. Upper concrete seating walls are targeted to begin forming after the slab-on-grade is installed.

The cupola steel has been installed at the lower elevation. The remaining cupola steel is scheduled to be erected on the ground with studs and sheathing set the week of March 15, 2010. Final studs and sheathing and brickwork will follow.



AREA D—AUDITORIUM

Foundations in Area B will complete by the end of the week and foundation CMU will follow. Underground plumbing is ongoing in Area B.

Foundations in Area C will begin the week of March 15 and Area A foundations are scheduled to begin March 22, 2010.

ACTION ITEMS

The remaining precast shops drawings will be submitted by Selective Masonry on or before March 10, 2010. As of today's meeting no precast color has been identified. The color will be finalized after the brick has been finalized.

Settlement plate #3 will be installed by T&K Construction no later than Friday March the 5th.

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated March 2, 2010.




AREA C


Hueytown High School

ACTION ITEM LIST						MEETING DATE: March 2, 2010
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	3.	Precast Shop Drawings	Watts	02/22/10	03/10/10	Issue remaining precast shop drawings
12/16/09	4.	Brick Color Boards	SMI Owner	03/05/10 03/08/10		Build additional mock-up Review mock-up
01/05/10	5.	Water Meter C.O.R.	Lathan	01/06/10	03/04/10	Issue direction
02/02/10	7.	Temporary Construction & Primary Power	Britton APCO	03/15/10 03/05/10		Install power Issue design
02/02/10	8.	Stage Lighting & Equipment	Stage Light	02/23/10	03/15/10	Issue submittals to team
03/02/10	9.	Settlement Plate	T&K	03/05/10		Install and monitor


HUEYTOWN HIGH SCHOOL

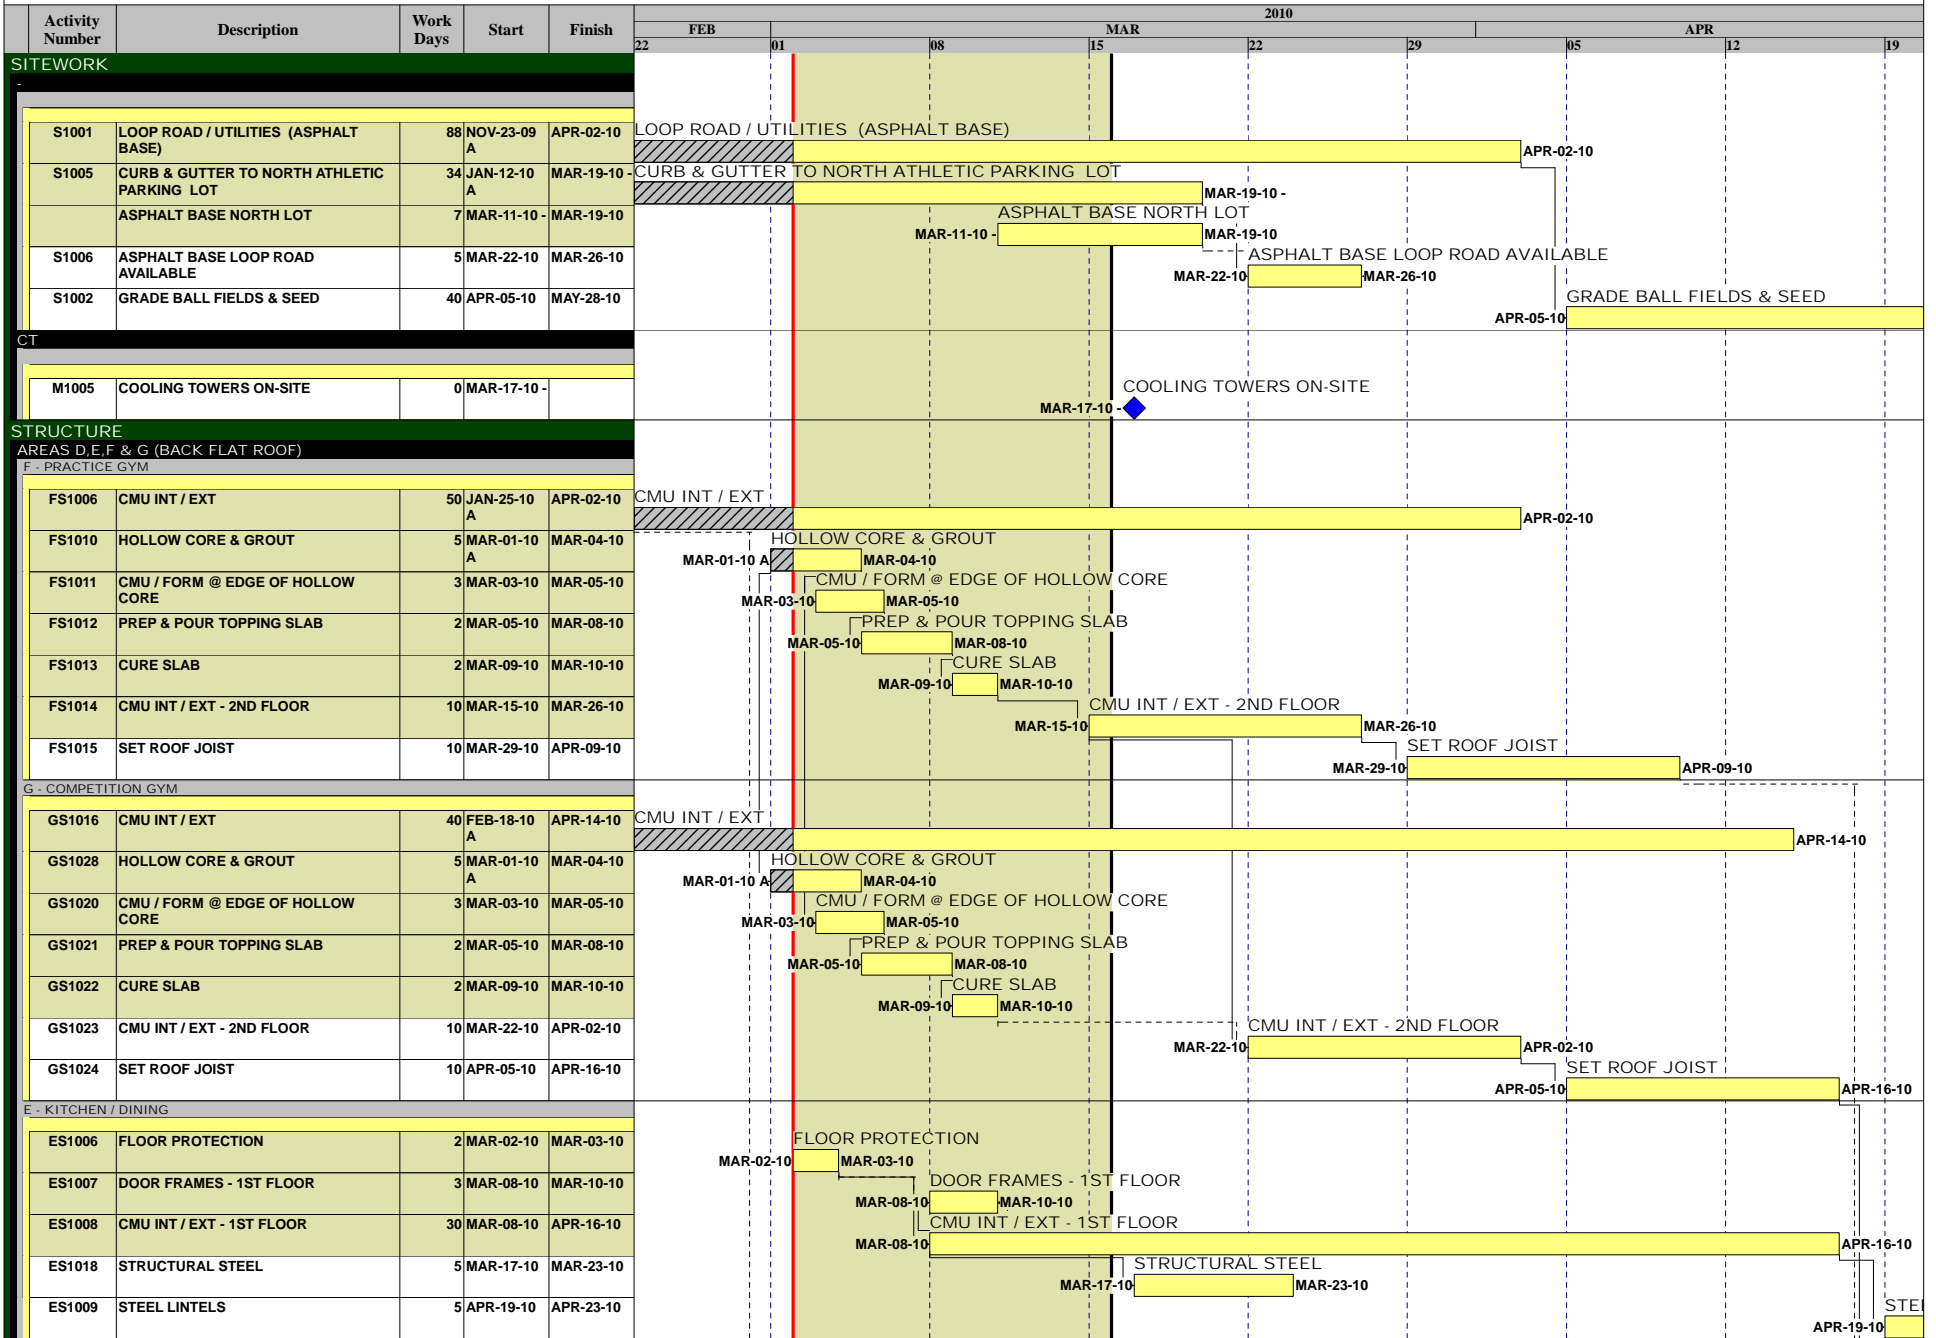

HUEYTOWN HIGH SCHOOL

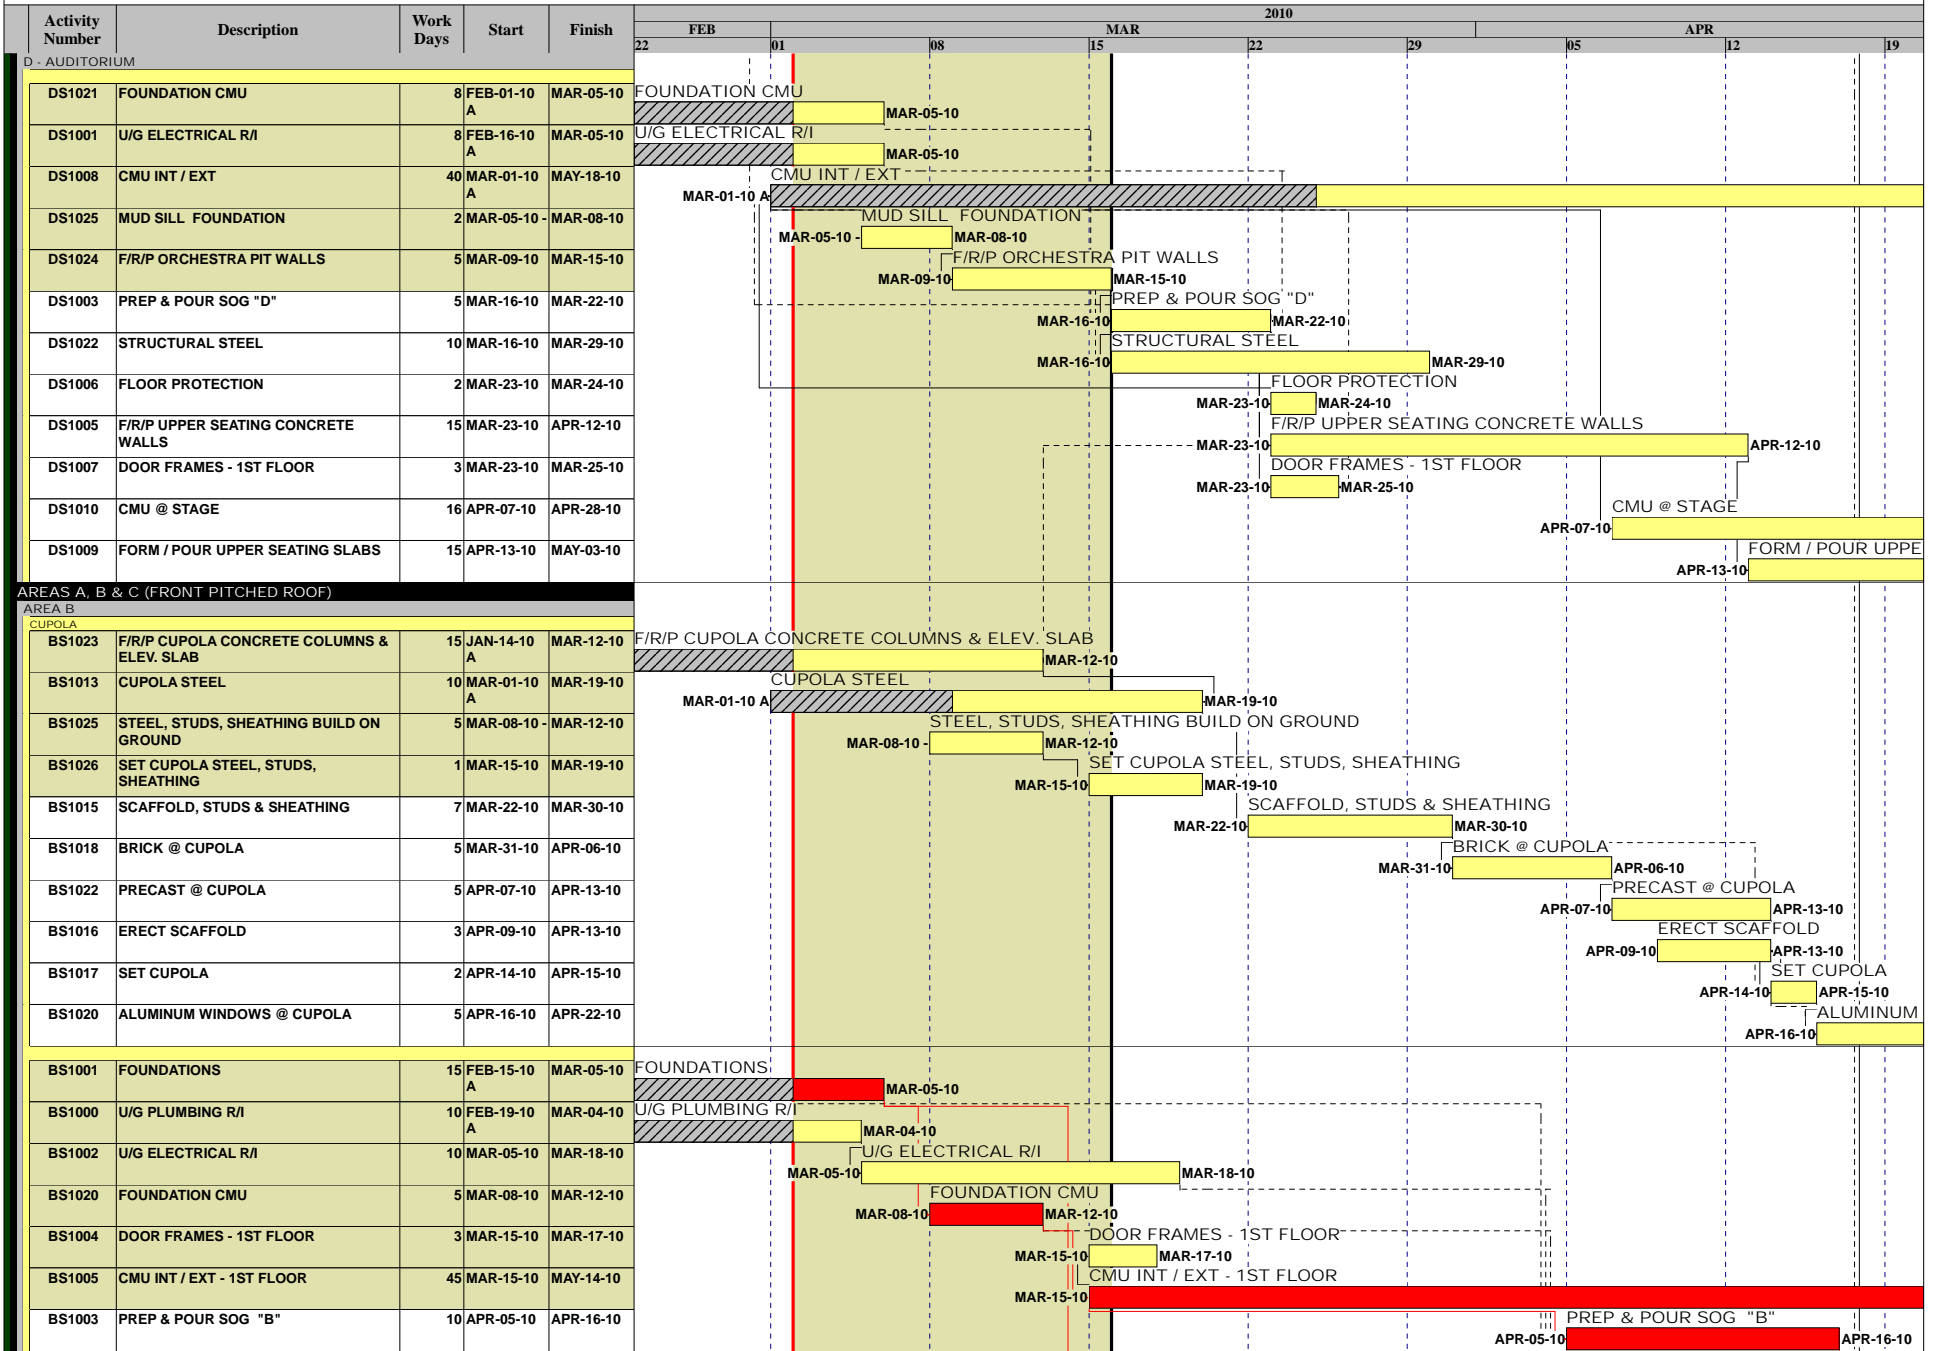

HUEYTOWN HIGH SCHOOL

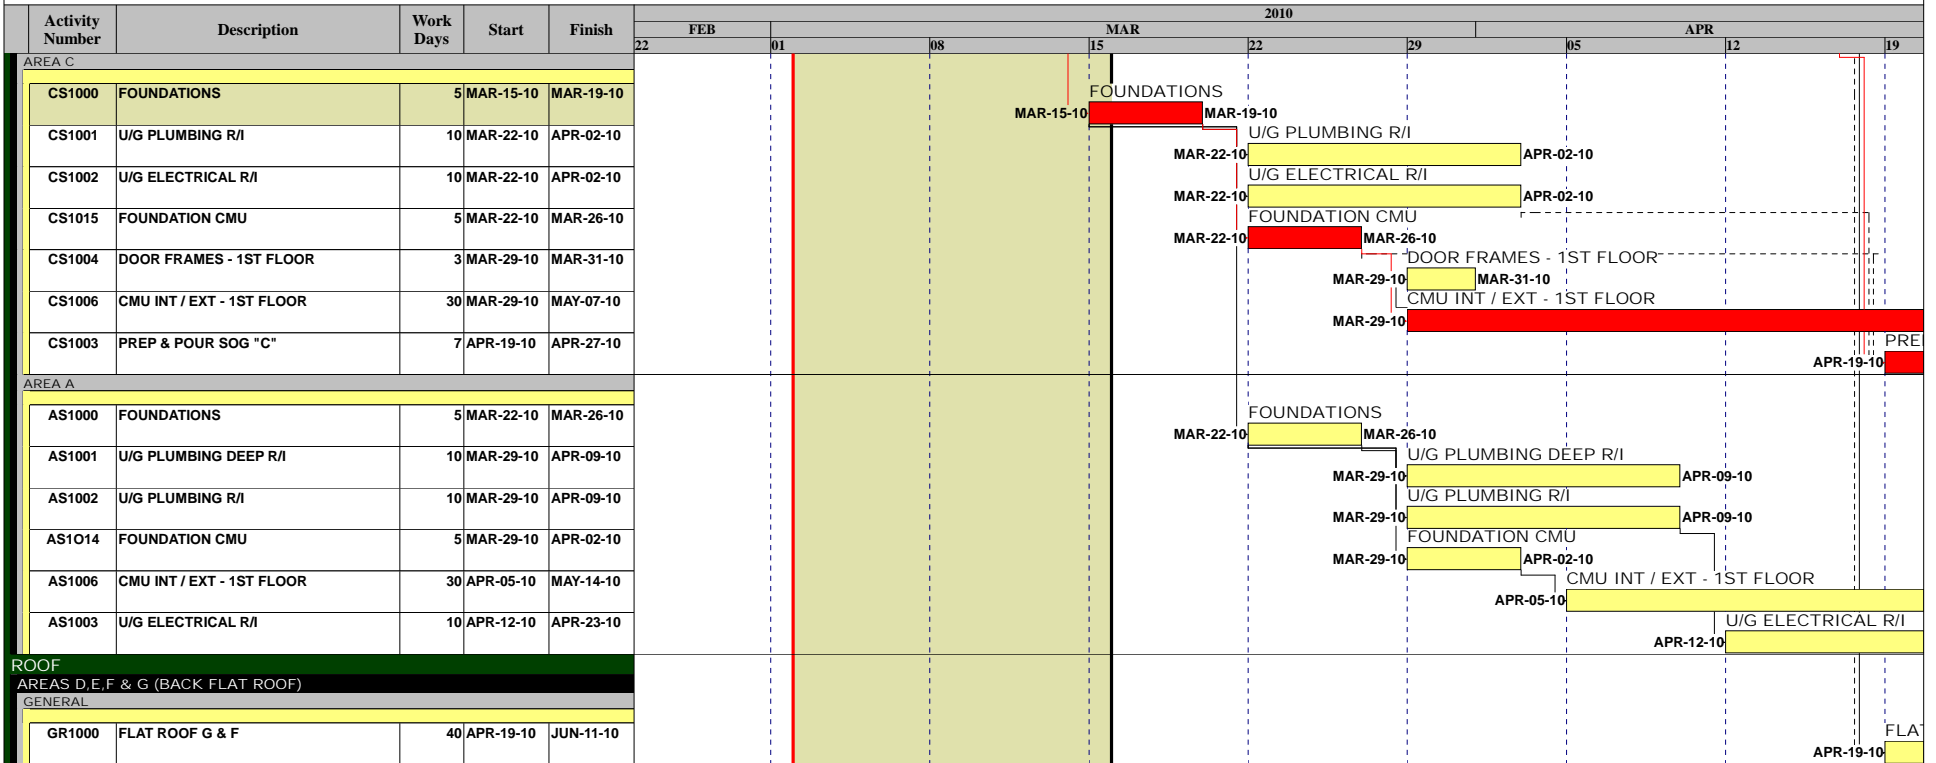

-

Distribution List Name: 29082 - Hueytown High School

Bo Hamilton	bhamilton@dunnconstruction.com
Donnie Hall	dhallnsons@aol.com
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Tim Robertson	troberson@dosterconstruction.com
