

# **HUEYTOWN HIGH SCHOOL**



**PROGRESS UPDATE REPORT**  
**July 20, 2010**

---

**DOSTER**

**BASELINE**  
  
**CONSULTANTS, INC.**

Please initial the **meeting** date to show that you were in attendance.



Hueytown High School #29082

8/3	ATTENDEES	CO. NAME	5/25	6/8	6/22	7/20
	Butch Henderson	Accurate Ele.				
	Steven Greeson	Automated Logic				
	Bob Cameron	Bama Concrete Inc.				
	Kyle Norwood	Bama Concrete Inc.				
	Larry Mackey	Bama Concrete Inc.				
	Stephen Franklin	BFS				XX
	David Bullock	Bhate				
	Donnie Rigg	BSCO Inc.				
	Jessie Isom	BSCO Inc.				
	Cecil Smith	C.C.	XX	XX	XX	
	Phil Sebring	Coreslab				
	Joe Kuhn	Doster Construction	XX	XX	XX	XX
	Josh Cronan	Doster Construction	XX	XX	XX	XX
	Justin Petty	Doster Construction	XX	XX	XX	XX
	Tim Robertson	Doster Construction	XX	XX	XX	XX
	Bo Hamilton	Dunn Construction	XX			
	David Ginn	H2K		XX	XX	XX
	Donnie Hall	Hall & Sons Plumbing				
	Jerry Fuller	Hall & Sons Plumbing	XX	XX	XX	XX
	Moe Garner	Hall & Sons Plumbing	XX	XX	XX	XX
	Don Davis	J & K Electric	XX	XX	XX	XX
	John Britton	J & K Electric	XX	XX	XX	
	Wayne Skinner	J & K Electric				XX
	Darryl White	J & Sons				
	Darrell Cole	P&M Mechanical		XX		
	Gary Psnell	P&M Mechanical				
	Jimmy Davis	P&M Mechanical			XX	
	Joe Manning	P&M Mechanical	XX	XX	XX	XX
	Micheal Isbell	P&M Mechanical				
	Brian Korfant	Roof Craft	XX	XX	XX	XX
	Mike Jones	Roof Craft Systems			XX	
	Charles Johnson	Selective Masonry	XX	XX	XX	XX
	Jonathan Watts	Selective Masonry				
	Wes Smith	Selective Masonry	XX		XX	XX
	Mark Smith	Simpson Plastering				XX
	Mike Kennedy	Simpson Plastering				XX
	Jay Poole	SMI		XX		
	Jesse Kelley	Southwest Water			XX	
	Willy Shepard	Southwest Water			XX	
	P. E.	Stankunas Construction	XX			XX
	Gregg Baker	T&K Construction				
	Lanny Nelson	T&K Construction	XX	XX	XX	
	Nathaniel Hutchinson	T&K Construction				XX
	Steve Giddens	T&K Construction				
	Mell Gage Smith	The Mell Group			XX	
	Joseph Dodson	United States Sprinkler				
	<b>Lee Edmonds</b>	<b>Baseline Consultants, Inc.</b>	XX	XX	XX	XX

If you do not see your name, please print your name and company name in available space.

## PROGRESS SUMMARY

**Hueytown High School  
July 20, 2010**

The Progress Update Meeting was held at 10:00 a.m. on Tuesday, July 20, 2010, at the Doster Construction Company jobsite trailer.

**The next Progress Update Meeting will be held at 10:00 a.m. on Tuesday, August 3, 2010, at Doster Construction Company jobsite trailer.**

**Any subcontractor scheduled to perform work during the next few weeks should have a representative present at that meeting. This person should be able and prepared to discuss current manpower and material deliveries, and make commitments concerning that subcontractor's work over the following few weeks.**

**The following summary is assumed to be a true and factual account of events that transpired in the July 20, 2010 Progress Update Meeting. If you feel there are any discrepancies in this report, these will be addressed at the next meeting.**



**AREA G**

### **GENERAL NOTES**

Tim Robertson of Doster Construction Company reviewed general safety items. Mr. Robertson reviewed in detail dumpster protocol, scaffold procedures, and floor protection.

### **SITework**

The grading of the ball fields and temporary seating is substantially complete except for the football field. Asphalt base to close the loop road and at the north and south lots is complete. The 15th Street shoulder and decel lane has had no progress over the past month. This work is anticipated to resume August 2, 2010. Virginia roadwork will not be complete by July 30, 2010. It is anticipated that this work will finish with the 15th Street shoulder work.



**AREA D**

### **STRUCTURE**

The decking activities at the practice gym and competition gym are complete. Roof curbs have been set in both areas. CMU parapet at the roofs of these areas is complete and roof installation at Area G is underway.

Installation of the roof joist and deck at the kitchen/dining area has not completed. This work will finish the week of July 26, 2010. CMU parapet decking, as well as roof curbs, will need to be set by July 30, 2010. Roofing activities at Area E will begin August 2, 2010.

Area D auditorium seating areas have been poured and upper seating slab work is ongoing and will be complete the week of July 26, 2010.

Orchestra pit wall work is continuing and will complete by July 23, 2010. Prepping and pouring of the auditorium slab-on-grade is scheduled to complete July 29, 2010. CMU in this area and structural steel will need to be complete by August 9, so that roof joist and deck activities can begin August 10, 2010. Roofing activities in Area D will follow Area E.



**AREA C—2nd FLOOR**

The front pitched roof area, which encompasses Areas A, B, and C, has had all hollow core set; and CMU at the 2nd Floor has not begun as of today's meeting. A change order is in review by the A/E team to minimize possible damage to the 2nd Floor concrete polished floors by erecting the CMU ahead of pouring topping slabs. A decision needs to be issued as soon as possible in order to begin 2nd Floor CMU or pour the topping slabs. Work in this area is on the critical path and this issue needs to be resolved immediately.

### **EXTERIOR SKIN**

Precast is not on the project and will not be on site until mid- August 2010. Exterior brick can begin ahead of precast. The schedule currently reflects brick starting August 2, 2010 this will occur pending Selective masonry manpower

### **INTERIOR CONSTRUCTION**

Fireproofing at the 1st Floor will begin in areas that are available on August 2, 2010. Grouting of all openings prior to fireproofing will need to be complete the week of July 26, 2010. All overhead systems installed ahead of fireproofing must be protected by each discipline.

Ceiling framing activities in Area F were reviewed during today's meeting and ceiling framing will begin August 2, 2010. Block-fill activities are now targeted to begin August 10 and concrete polishing activities in Area F are scheduled to begin October 1, 2010.

Enclosed for review following the Summary section are the Action Items and the Near Term Schedule dated July 20, 2010.




**AREA E**


## Hueytown High School

<b>ACTION ITEM LIST</b>						<b>MEETING DATE: July 20, 2010</b>
Origination Date	No.	Item	Who	Original Need Date	Revised Date	Comment
12/16/09	3.	Precast Shop Drawings	Watts	05/10/10	05/26/10	Submit interior precast shop drawings (at gym)
12/16/09	4.	Brick Color Boards	SMI	03/18/10	08/02/10	Build final mock-up on building in place
01/05/10	5.	Water Meter C.O.R.	Lathan	01/06/10	06/25/10	Issue change order (Final pricing to A/E 4/13/10)
03/02/10	9.	Settlement Plate	T&K	03/05/10	06/14/10	Install and monitor (at ball field)
06/22/10	13.	South West Water Company	SWWC	06/22/10	07/21/10	Issue install schedule


# HUEYTOWN HIGH SCHOOL

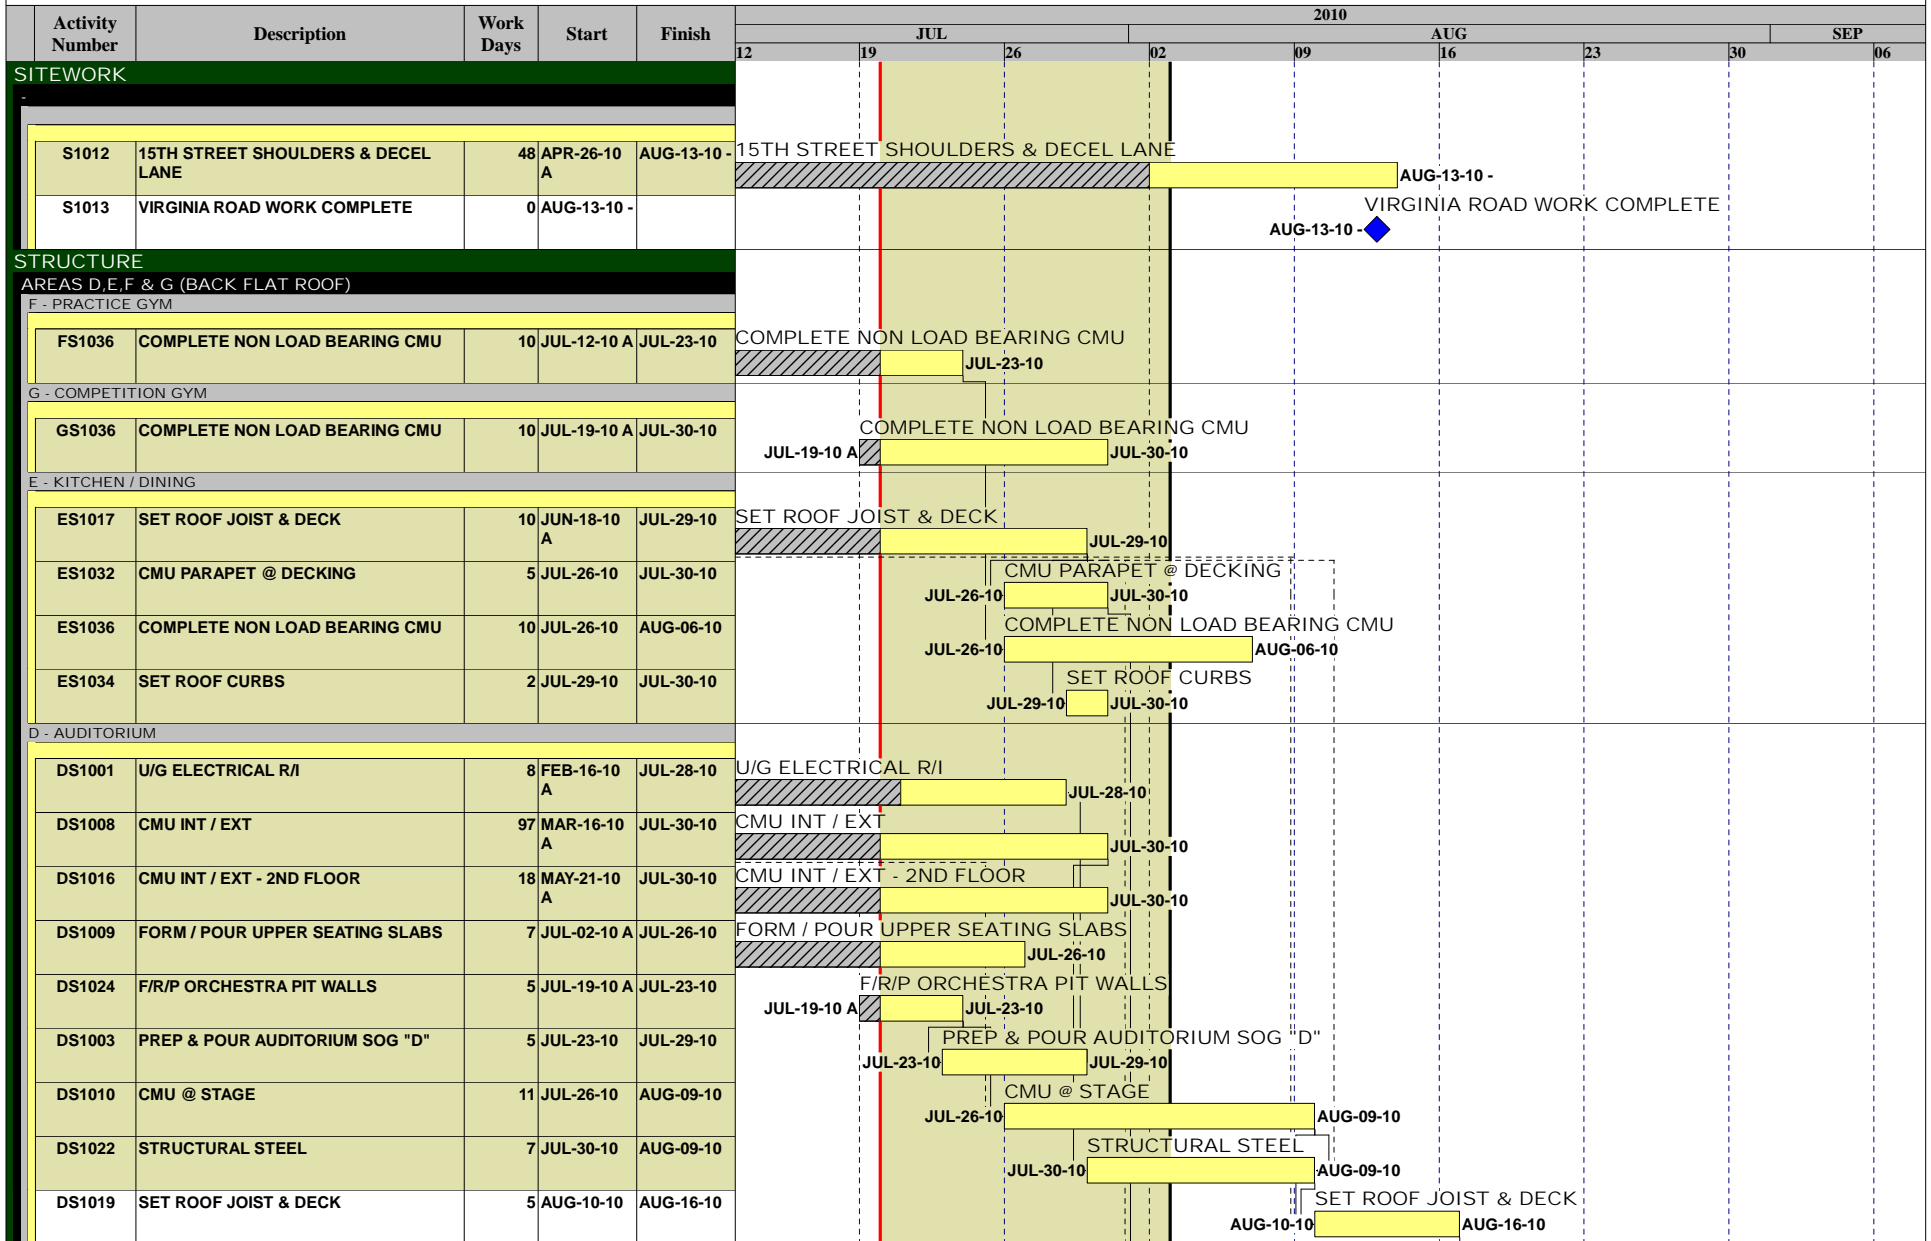


# HUEYTOWN HIGH SCHOOL

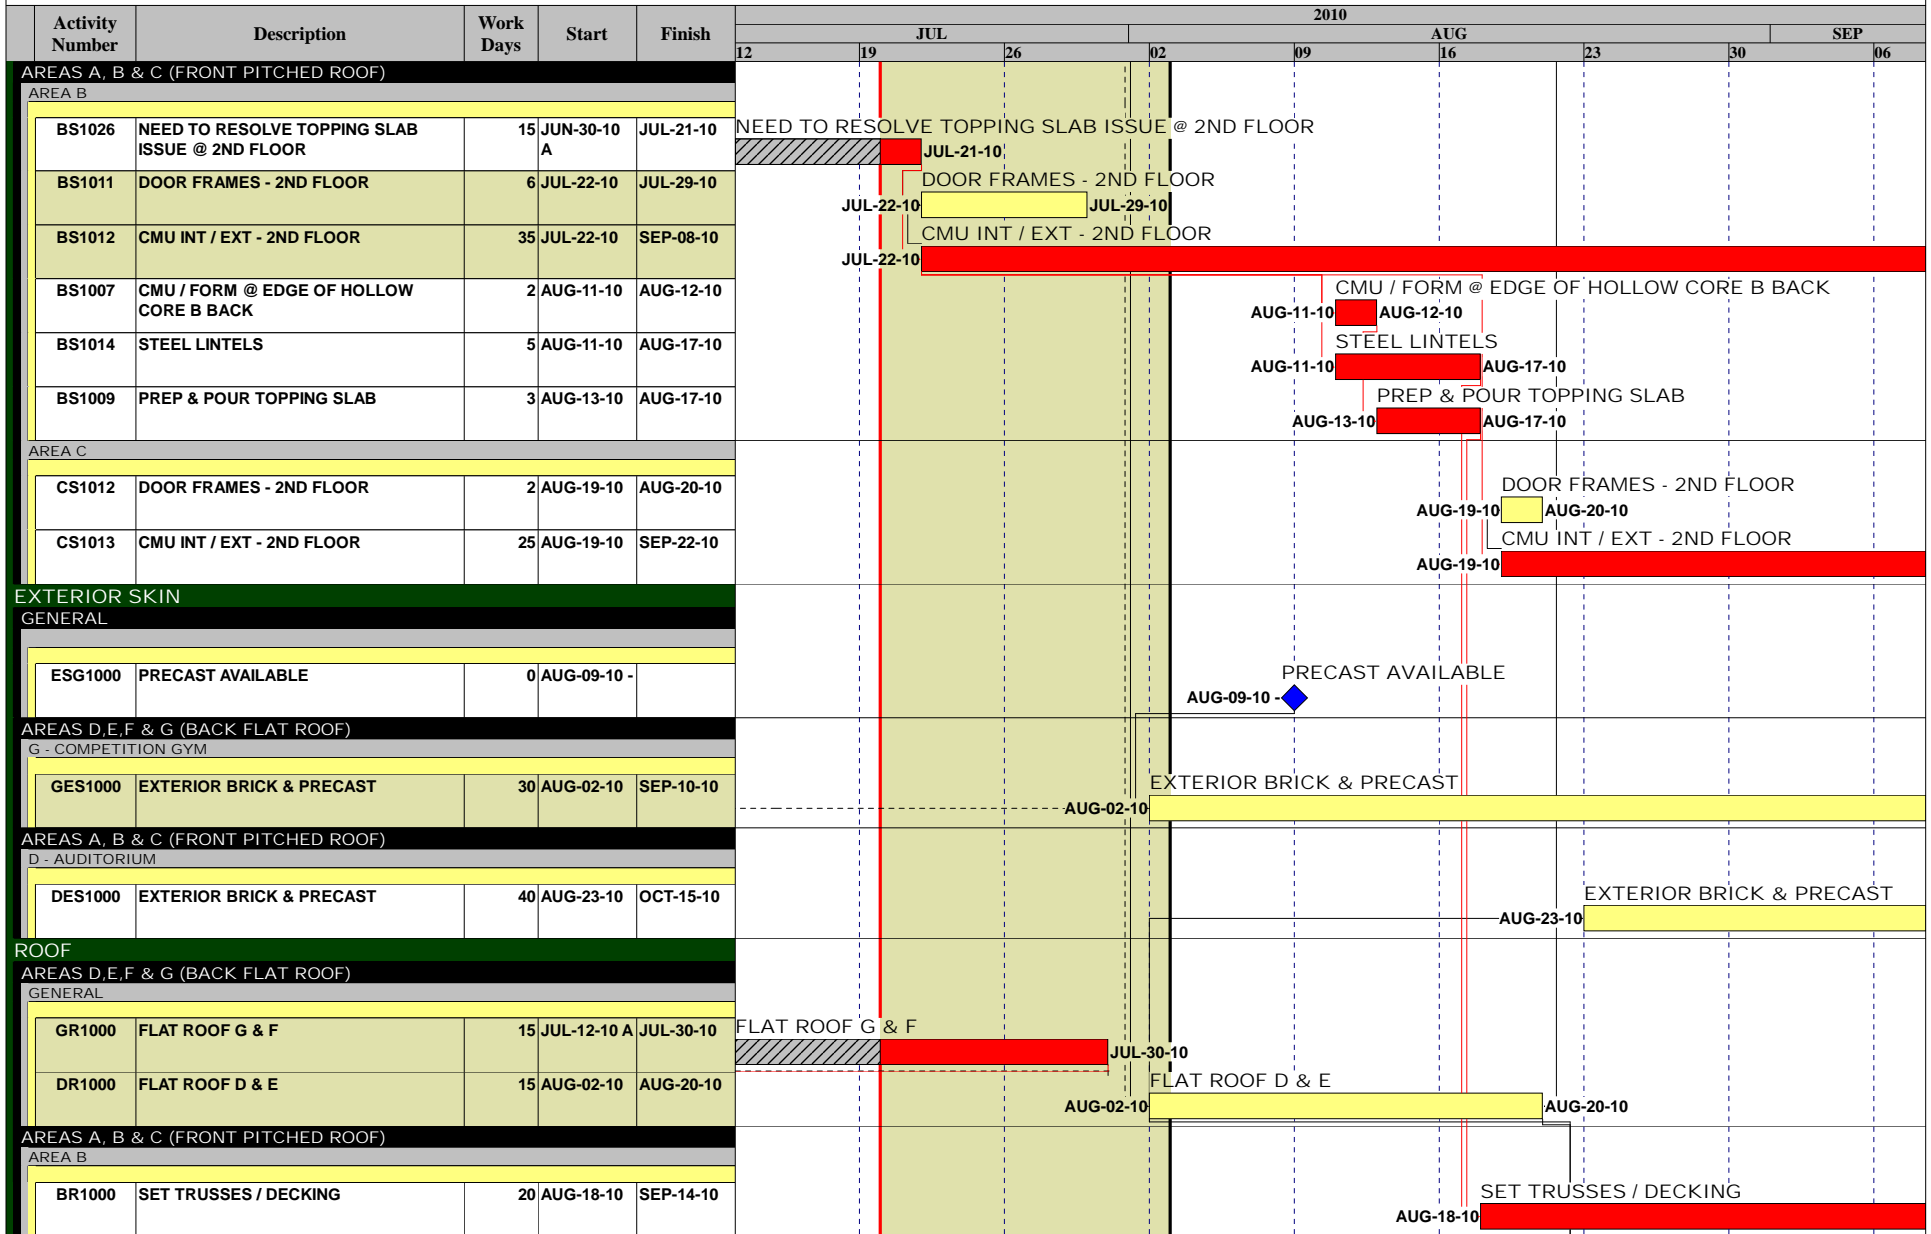

# HUEYTOWN HIGH SCHOOL

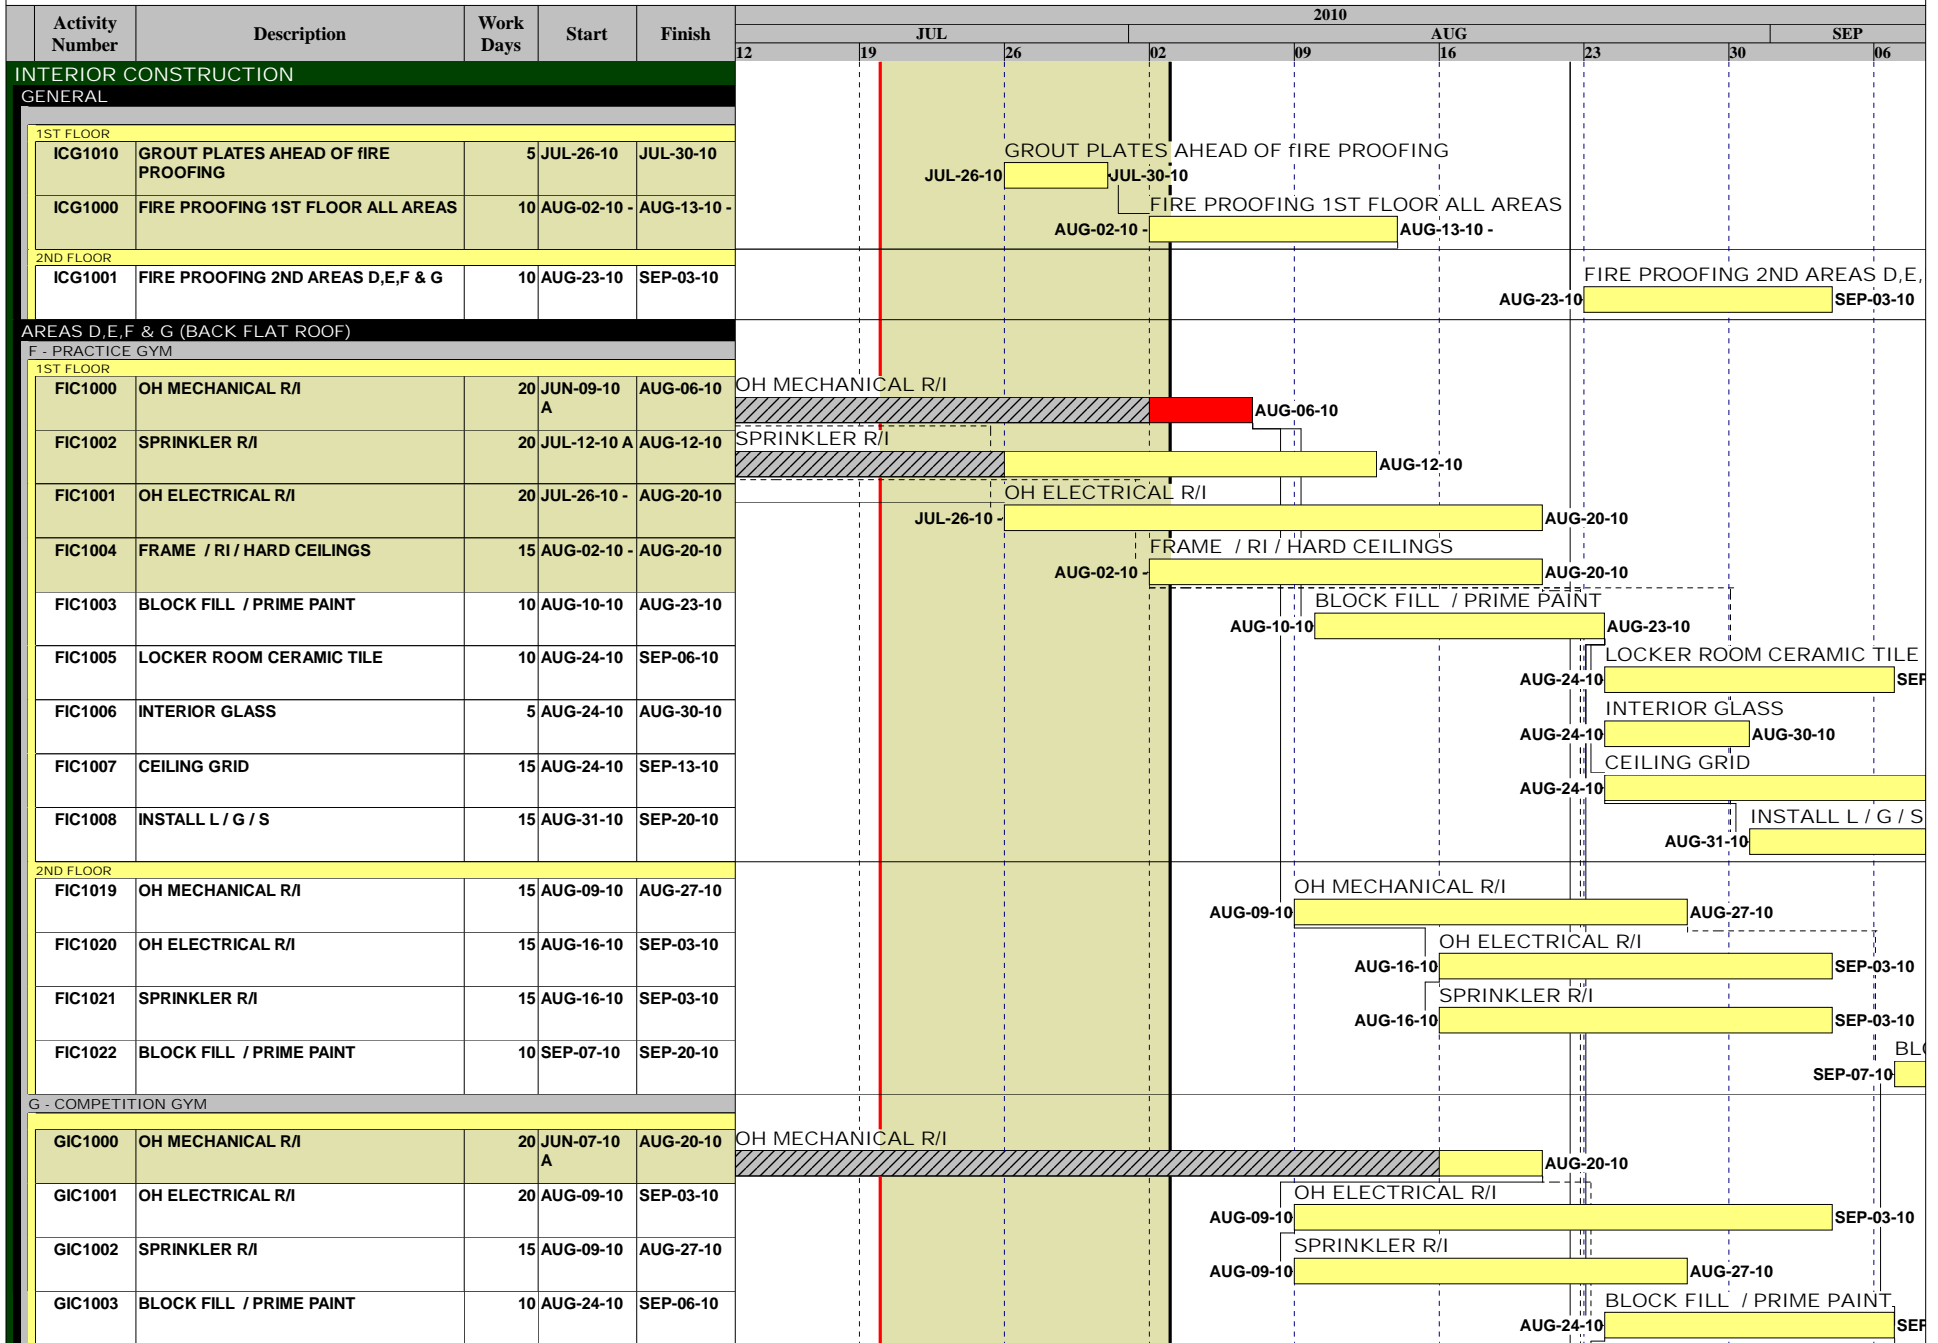

# HUEYTOWN HIGH SCHOOL

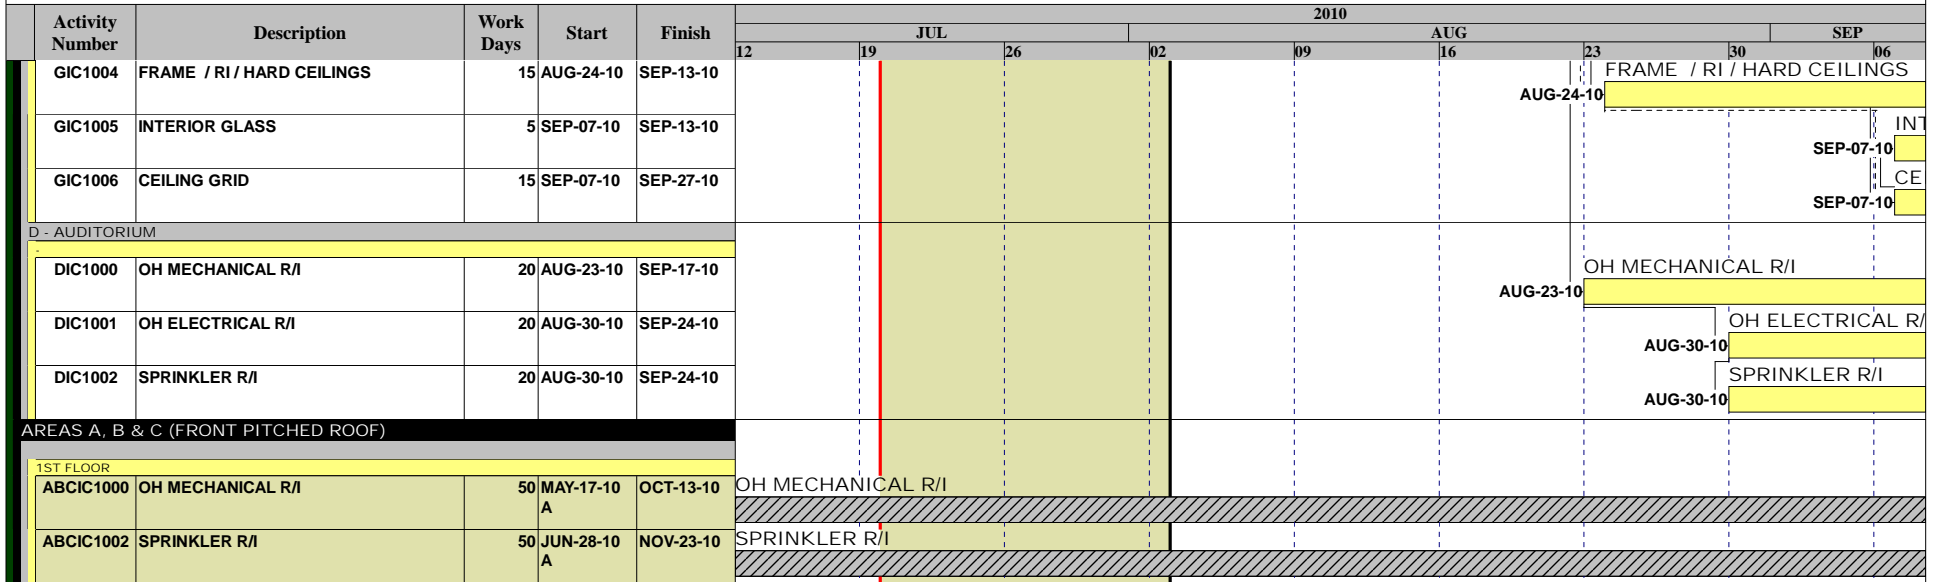

-

**Distribution List Name: 29082 - Hueytown High School**

Bo Hamilton	bhamilton@dunnconstruction.com
Brian Korfant	brian.korfant@roofusa.com
Donnie Hall	dhallnsons@aol.com
Jimmy Davis	jldpm@bellsouth.net
Joe Kuhn	jkuhn@dosterconstruction.com
John Britton	jkelectric@bellsouth.net
Jonathan Watts	jwatts@selind.com
Josh Cronan	jcronan@dosterconstruction.com
Justin Petty	jpetty@dosterconstruction.com
Lee Edmonds	lee@baselineconsultants.com
Michelle Best	mbest@jefcoed.com
Mike Jones	mike.jones@roofusa.com
Nathaniel Hutchinson	hutch@tandkconstruction.com
Sue Cole	sue@dixiestorefixtures.com
Tim Robertson	troberson@dosterconstruction.com
