

PLEASANT GROVE HIGH SCHOOL FOOTBALL STADIUM

PROGRESS MEETING
AUGUST 18, 2010



ATTENDEES / DISTRIBUTION LIST

18AUG10

MEETING ATTENDEES:

Steven Blalock	Blalock Building Company	Travis Moody	Knowles Con.
Brett Biel	Blalock Building Company	Duke Price	MSE Building Co.
Joey Bussey	Blalock Building Company	Keith Stewart	MSE Building Co.
Anthony Lutz	Blalock Building Company	Ray Calhoun	Montgomery Woodworks
Shane Lutz	Blalock Building Company	Charles Johnson	Selective Masonry
Billy Beardslee	B&B Painting	Arnold Bryant	Selective Masonry
Duane Beardslee	B&B Painting	Robby McCormick	Selective Masonry
Troy Ellison	E&E Acoustical	Jonathan Watts	Selective Masonry
Dave Coyte	Eagle Framing	James Boothe	Premier Service
Steve Early	J&K Electric	Derek Monk	Premier Service
Nick Stauder	J&K Electric	George Merchant	Victory Plumbing
John Britton	J&K Electric	David Shepherd	Victory Plumbing
Jeffrey McCool	Jeffco Concrete	A.J. Wolnski	Wolnski Scheduling Services


EMAIL DISTRIBUTION:

Michelle Best	Jefferson County BOE	Mike Wade	Joshco dba Butler Cont.
Dr. Rafael McDaniel	Jefferson County BOE	Linda Wright	Locker Pro
Lee Bryant	Lathan Associates	Todd Dunn	MC Precast
Joey Bussey	Blalock Building Company	WT Smith	MC Precast
Pam Garner	Blalock Building Company	Rodd Kindoll	MC Precast
Shane Lutz	Blalock Building Company	Ray Calhoun	Montgomery Woodworks
Bo Willis	ABG Caulking	Randy McDaniel	MSE Building Company
Keith Echols	Architectural Finishes	Mike Jones	MSE Building Company
Billy Beardslee	B&B Painting	Mike Schafer	Overhead Door Company
Jim Caradine	Building Specialties	Steven Stamps	Premier Service Company
Joe Cox	Covington Flooring	Jeremy Garrett	Schindler Elevator
Tommy Ellison	Covington Flooring	Jonathan Watts	Selective Masonry
Jimmy Isaminger	DMI Tile & Marble	Charles Johnson	Selective Masonry
Adam Easterling	E&E Acoustical & Drywall	Kirk Jones	Sizemore's Aluminum Prod.
C.J.	E&E Acoustical & Drywall	Frank Beaman	Steel Stadiums
Heith Comer	G&S Glass & Supply	George Merchant	Victory Plumbing
Jackie Keller	H2K Construction	A.J. Wolnski	Wolnski Scheduling
Karen Britton	J&K Electric	Susan Richardson	Wolnski Scheduling
George Henry	Jeffco Concrete		

HARD COPY DISTRIBUTION:

Brett Biel – 5 copies	Blalock Building Company		

PROJECT TIMELINE



NEXT MEETING: WEDNESDAY, SEPTEMBER 1ST AT 9:00AM

PROGRESS MEETING SUMMARY

18AUG10

JOB CONTACTS

Name	Title	Cell/Pager #	Nextel #	email
Brett Biel	Project Manager	205-281-9842	154*86951*11	bbiel@blalockbc.com
Shane Lutz	Superintendent	205-281-5279		shanel@blalockbc.com

JOBSITE ADDRESS

1301 4th Place Pleasant Grove, AL 35127

MEETING ATTENDANCE

The following subcontractors did not have anyone in attendance at today's progress meeting:

- Victory

Anyone with ongoing work or work scheduled to begin within the next 4 weeks is required to attend progress meetings. Anyone that is unable to attend a progress meeting should be sure to call Brett Biel or Shane Lutz before the meeting begins to give them the opportunity to ask any questions that would have come up at the meeting.

Below is a list of future meeting dates:

01SEP10 15SEP10 29SEP10

SAFETY

Blalock Building Company holds regular safety meetings every Tuesday morning at 9:00AM. Following is a list of key safety concerns:

- **Hard hats are required full time for everyone.**
- Step ladders – free standing, do not use top 2 steps, use proper height ladder.
- Competent person required on site during weekend work.
- Emergency phone numbers must be provided to all foremen.
- Fire extinguishers must be kept in place at all times.
- All subcontractors must attend safety meetings.
- Lull operators must wear a seatbelt during operation.
- Scaffolds must be erected in compliance with OSHA requirements.
- Interaction with students is strictly prohibited

CLEAN UP

All subcontractors are required to perform their own cleanup on a daily basis. Shane said that Blalock Building Company has been doing all of the cleanup. Consequently, a composite cleanup crew will be formed on Fridays to keep up with the work everyone is failing to do during the week. All subcontractors are required to contribute toward the composite cleanup crew. All subs agreed to contribute to the crew.

DAILY REPORTS

Daily reports are required to be turned in on a daily basis, not weekly. Shane said that he is only getting daily reports from the HVAC contractor.

PROGRESS MEETING SUMMARY (CONT.)

18AUG10

SUBMITTALS

Architect

There are currently no critical submittals out for approval.

REQUESTS FOR INFORMATION

27 RFI's have been issued to date. All of them have been answered.

PAYMENT APPLICATIONS

Payment applications for the entire month's work are to be sent to Blalock's main office by the 20th of each month. The faxed copy must be sent by the 20th in order to process the request on time. Daily Reports and Sub Safety Meeting Minutes must also be up to date in order to receive payment.

CHANGE ORDER REQUESTS

Following is a list of Change Order requests with the status of each noted:

- COR #1 – Lift station – approved
- COR #2 – Bermuda grass – approved
- COR #3 – Deduct for header brick – accepted
- COR #4 – Rain delays for March – awaiting architect approval
- COR #5 – VE for concrete stadiums

SCHEDULE


A.J. reviewed and updated the schedule of remaining work. A revised copy is included in this report.









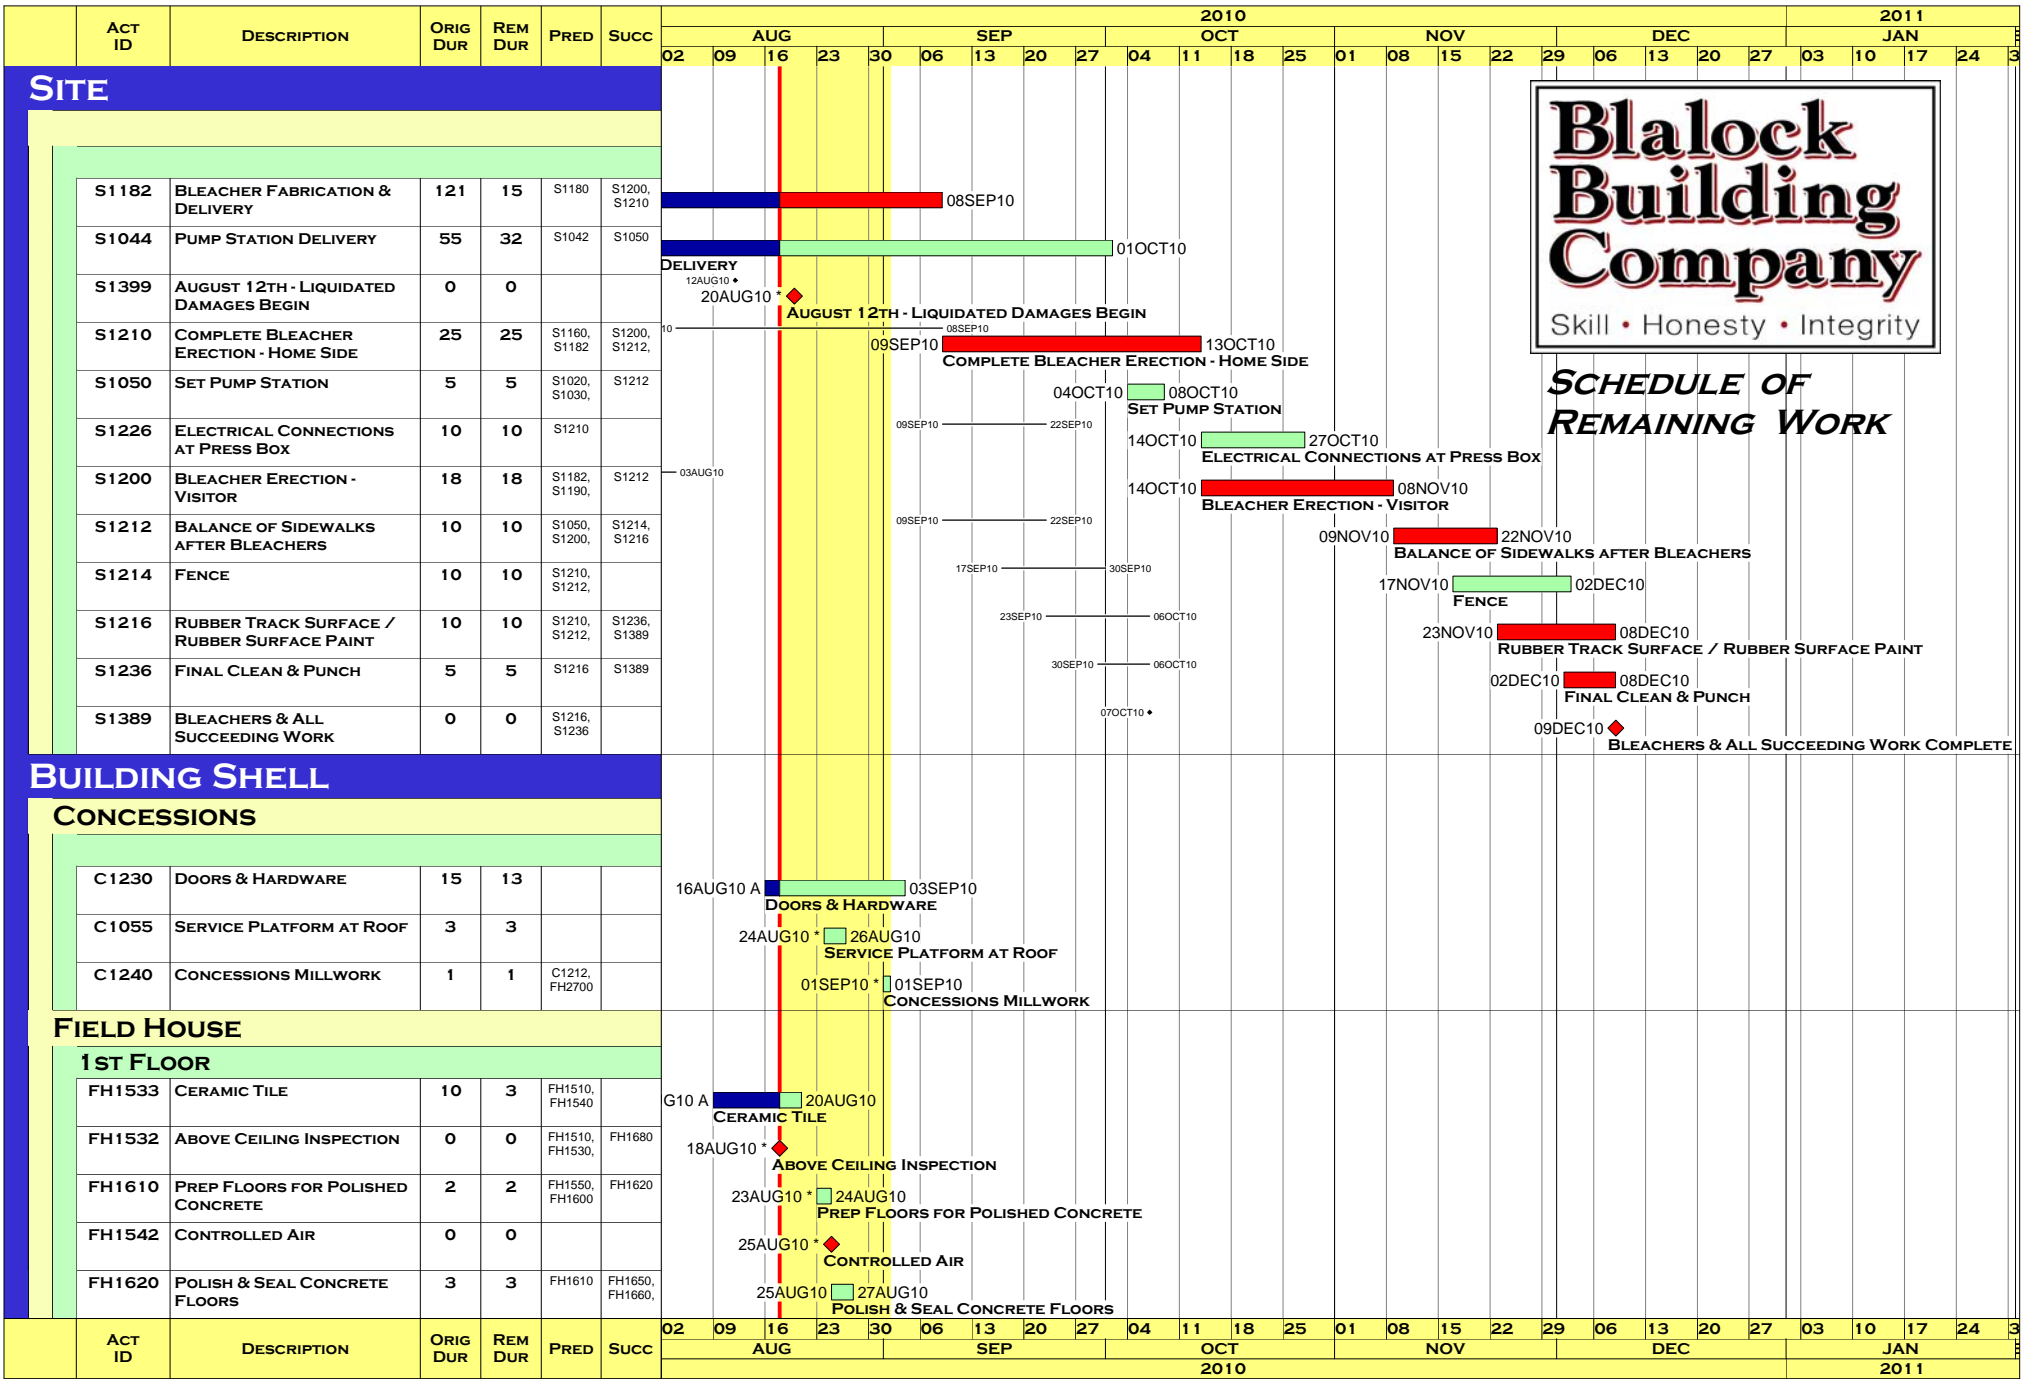

SCHEDULE OF REMAINING WORK

- Early bar
- Target bar
- Progress bar
- Critical bar
- ◆ Start milestone point
- ◇ Finish milestone point

PLGROVE (SURETRAK)
 REPORT: PLG1
 LAYOUT: LETTER BY AREA
 FILTER: REMAINING WORK

PLEASANT GROVE FOOTBALL STADIUM
BLALOCK BUILDING COMPANY

RUN DATE: 23AUG10
 DATA DATE: 18AUG10
 JOB# 1003
 PAGE 1A OF 3A



ACT ID	DESCRIPTION	ORIG DUR	REM DUR	PRED	SUCC	2010												2011											
						AUG					SEP				OCT			NOV				DEC				JAN			
						02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10
FH2932	PROJECT COMPLETE	0	0	FH1930, FH2930		12AUG10 •									15OCT10 ◆														
															PROJECT COMPLETE														

- Early bar
- Target bar
- Progress bar
- Critical bar
- Start milestone point
- Finish milestone point


PLGROVE (SURETRAK)
 REPORT: PLG1
 LAYOUT: LETTER BY AREA
 FILTER: REMAINING WORK

PLEASANT GROVE FOOTBALL STADIUM

BLALOCK BUILDING COMPANY

RUN DATE: 23AUG10
 DATA DATE: 18AUG10
 JOB# 1003
 PAGE 3A OF 3A



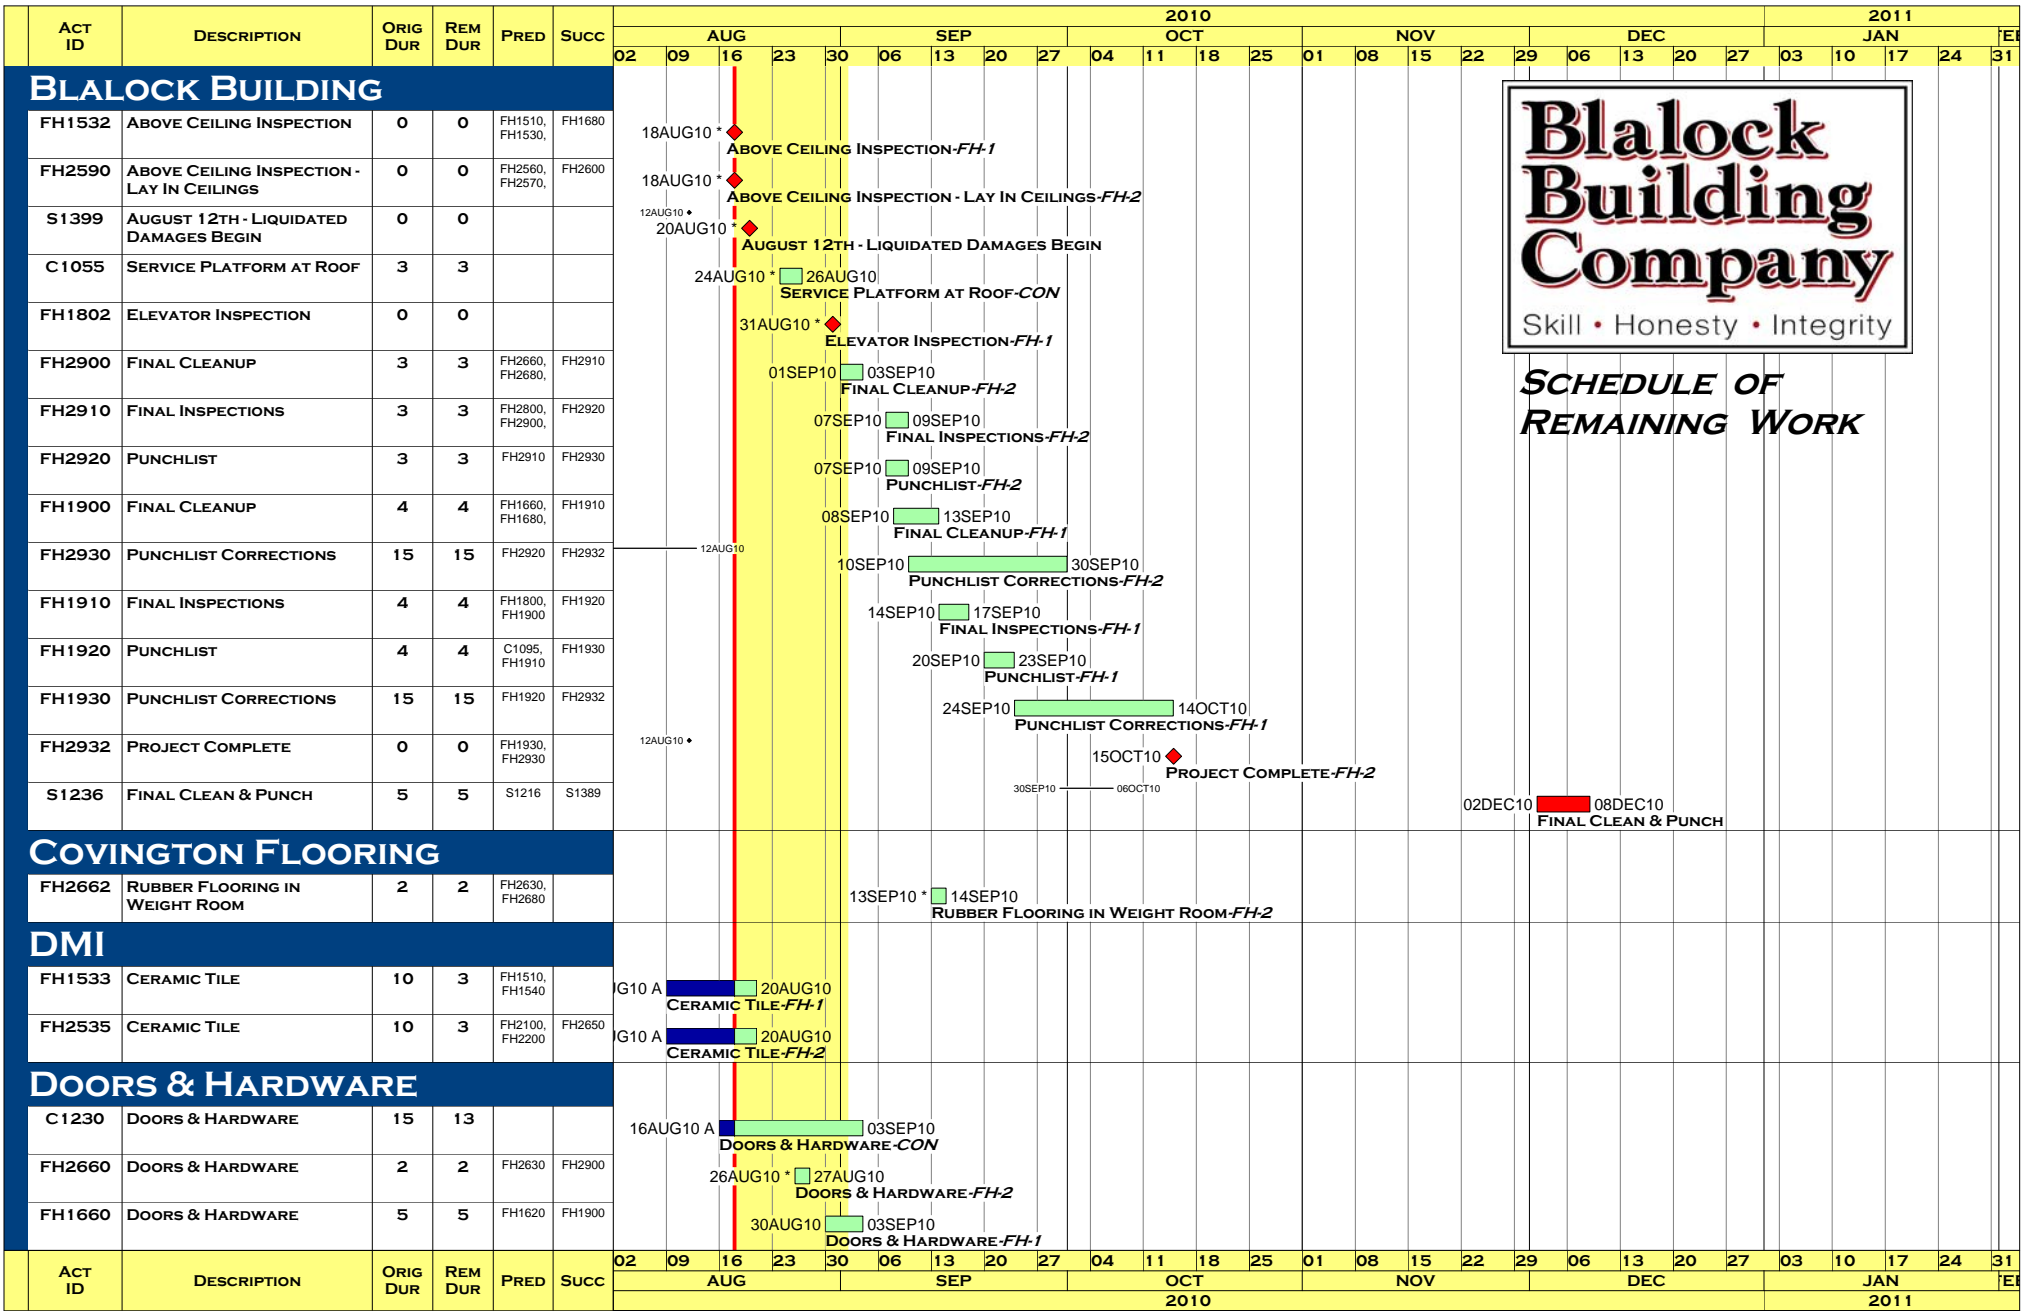

SCHEDULE OF REMAINING WORK

- Early bar
- Target bar
- Progress bar
- Critical bar
- Start milestone point
- Finish milestone point

PLGROVE (SURETRAK)
 REPORT: PLG2
 LAYOUT: LETTER BY RESP
 FILTER: REMAINING WORK

**PLEASANT GROVE FOOTBALL STADIUM
 BLALOCK BUILDING COMPANY**

RUN DATE: 23AUG10
 DATA DATE: 18AUG10
 JOB# 1003
 PAGE 1A OF 3A



ACT ID	DESCRIPTION	ORIG DUR	REM DUR	PRED	SUCC	2010																													
						AUG					SEP					OCT					NOV					DEC									
						02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	2011							
																				JAN															
STEEL STADIUMS																																			
S1182	BLEACHER FABRICATION & DELIVERY	121	15	S1180	S1200, S1210	08SEP10																													
S1210	COMPLETE BLEACHER ERECTION - HOME SIDE	25	25	S1160, S1182	S1200, S1212	09SEP10 - 13OCT10																													
S1200	BLEACHER ERECTION - VISITOR	18	18	S1182, S1190	S1212	03AUG10 - 14OCT10																													
S1389	BLEACHERS & ALL SUCCEEDING WORK	0	0	S1216, S1236		07OCT10 - 08NOV10																													
TRACK																																			
S1216	RUBBER TRACK SURFACE / RUBBER SURFACE PAINT	10	10	S1210, S1212, S1389		23SEP10 - 06OCT10																													
VICTORY PLUMBING																																			
S1044	PUMP STATION DELIVERY	55	32	S1042	S1050	DELIVERY 01OCT10																													
FH2650	SET PLUMBING FIXTURES	1	1	FH2535, FH2640	FH2690	23AUG10 - 23AUG10																													
FH2690	PLUMBING TRIM OUT	1	1	FH2650	FH2900	24AUG10 - 24AUG10																													
FH1650	SET PLUMBING FIXTURES	3	3	FH1620	FH1690	30AUG10 - 01SEP10																													
FH1690	PLUMBING TRIM OUT	5	5	FH1650	FH1900	31AUG10 - 07SEP10																													
ACT ID	DESCRIPTION	ORIG DUR	REM DUR	PRED	SUCC	2010																													
						AUG					SEP					OCT					NOV					DEC					2011				
																										JAN									

- Early bar
- Target bar
- Progress bar
- Critical bar
- ◆ Start milestone point
- ◆ Finish milestone point

PLGROVE (SURETRAK)
 REPORT: PLG2
 LAYOUT: LETTER BY RESP
 FILTER: REMAINING WORK

PLEASANT GROVE FOOTBALL STADIUM
BLALOCK BUILDING COMPANY

RUN DATE: 23AUG10
 DATA DATE: 18AUG10
 JOB# 1003
 PAGE 3A OF 3A



ACTION LIST

18AUG10

	#	DESCRIPTION	RESP	TO BE DONE BY
<input type="checkbox"/>	12	Schedule dates for press box delivery	Steel Stadiums	
<input type="checkbox"/>	13	Field house above ceiling inspection	All subs	06AUG10 09AUG10 18AUG10
<input type="checkbox"/>	22	Elevator inspection requirements (See Shane – All Subs)	All Subs	05AUG10
<input checked="" type="checkbox"/>	23	Grout color at ceramic wall tile	Lathan	05AUG10
<input checked="" type="checkbox"/>	24	Vanity bowl cover color	Lathan	05AUG10
<input type="checkbox"/>	25			
<input type="checkbox"/>	26			
<input type="checkbox"/>	27			
<input type="checkbox"/>	28			
<input type="checkbox"/>	29			
<input type="checkbox"/>	30			
<input type="checkbox"/>	31			
<input type="checkbox"/>	32			
<input type="checkbox"/>	33			
<input type="checkbox"/>	34			
<input type="checkbox"/>	35			
<input type="checkbox"/>	36			
<input type="checkbox"/>	37			
<input type="checkbox"/>	38			
<input type="checkbox"/>	39			
<input type="checkbox"/>	40			
<input type="checkbox"/>	41			
<input type="checkbox"/>	42			
<input type="checkbox"/>	43			
<input type="checkbox"/>	44			

Items denoted by an were reported to be complete at this meeting. They will be removed from the Action List at the next meeting
