


PLEASANT GROVE HIGH SCHOOL FOOTBALL STADIUM

PROGRESS MEETING
AUGUST 4, 2010

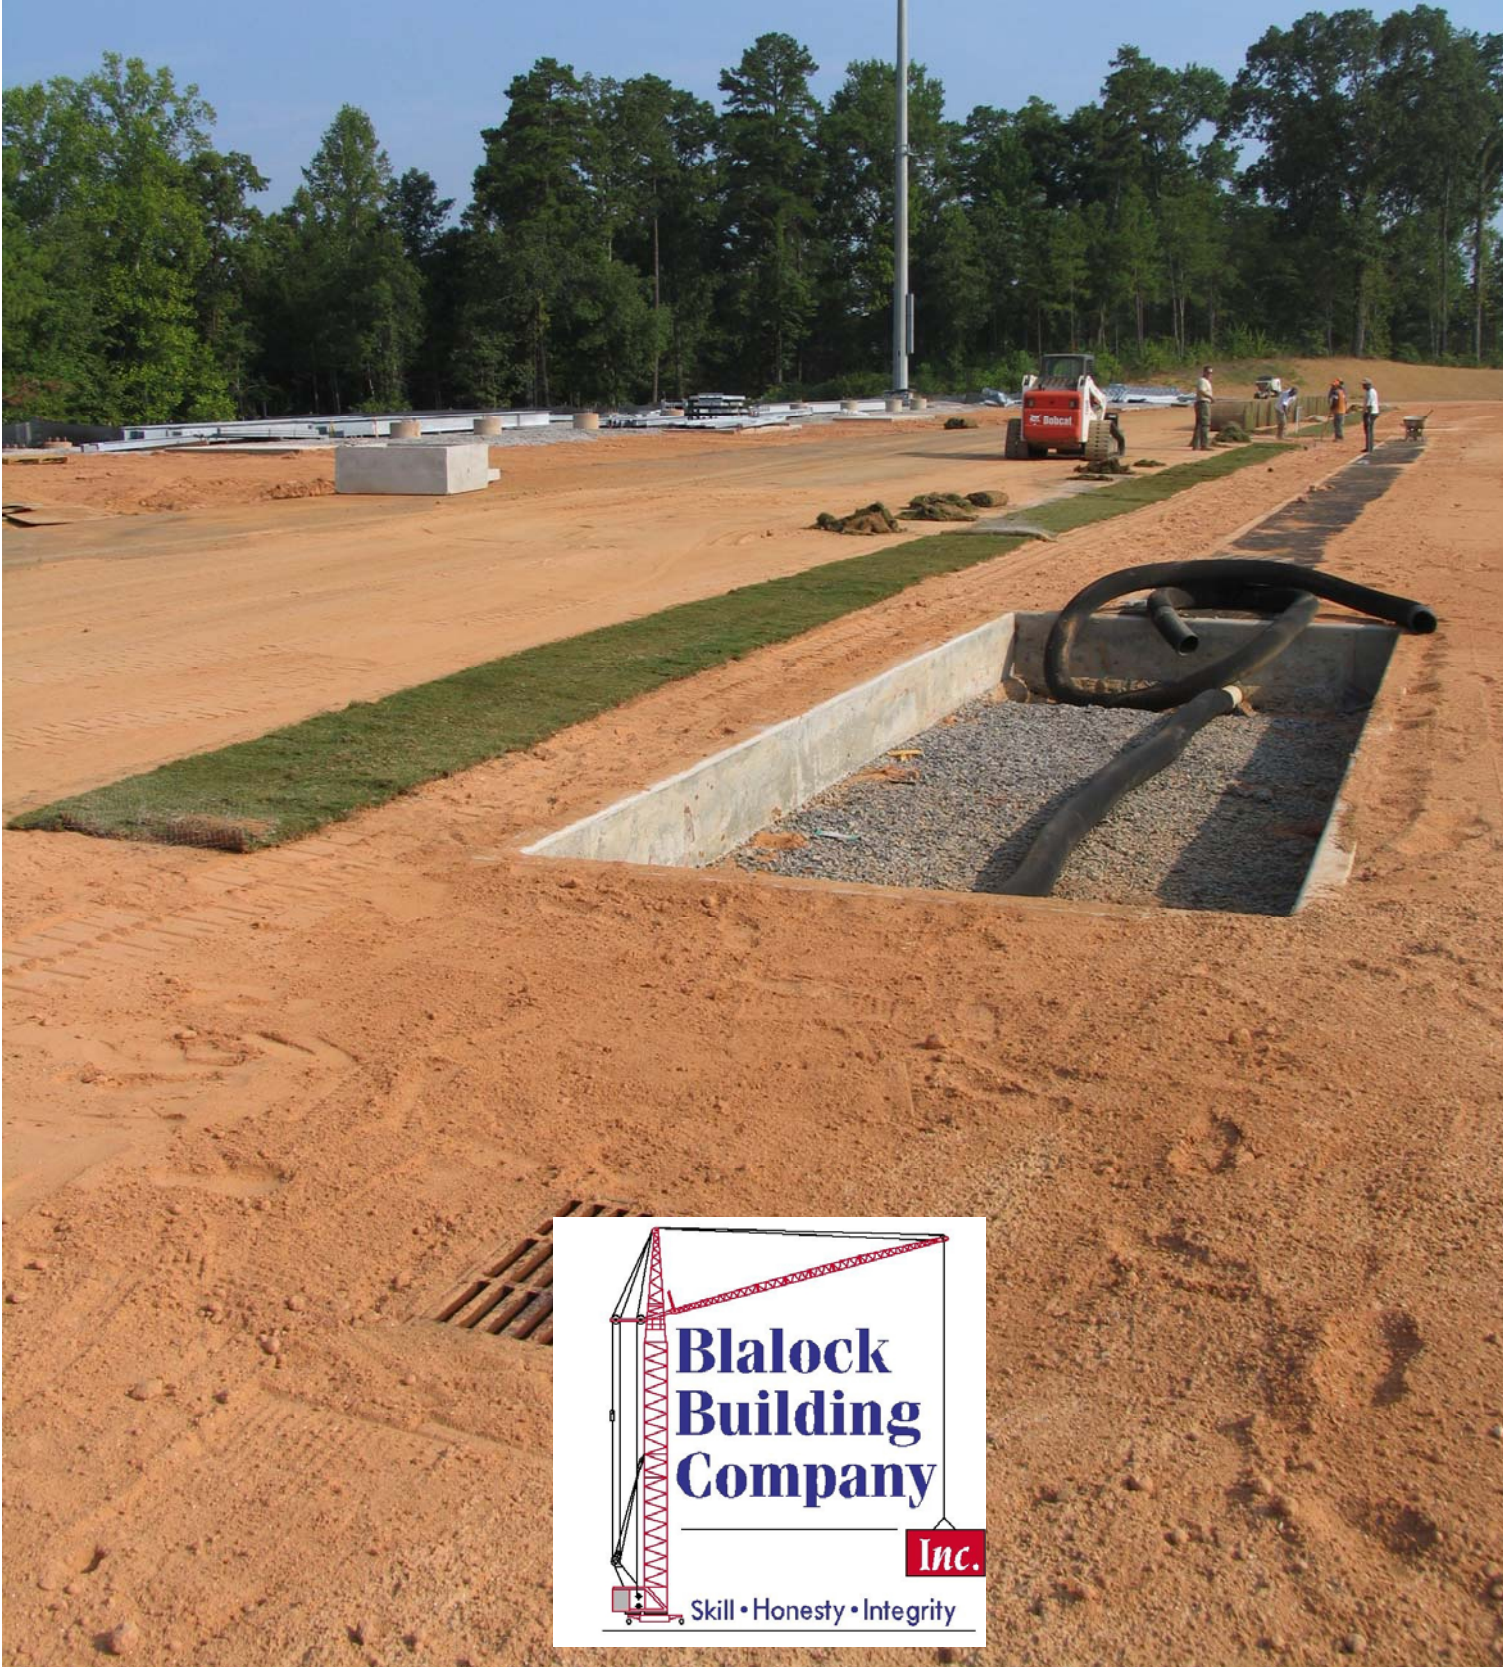

**Blalock
Building
Company**

Inc.

Skill • Honesty • Integrity

ATTENDEES / DISTRIBUTION LIST

04AUG10

MEETING ATTENDEES:

Steven Blalock	Blalock Building Company	Travis Moody	Knowles Con.
Brett Biel	Blalock Building Company	Duke Price	MSE Building Co.
Joey Bussey	Blalock Building Company	Keith Stewart	MSE Building Co.
Anthony Lutz	Blalock Building Company	Ray Calhoun	Montgomery Woodworks
Shane Lutz	Blalock Building Company	Charles Johnson	Selective Masonry
Billy Beardslee	B&B Painting	Arnold Bryant	Selective Masonry
Duane Beardslee	B&B Painting	Robby McCormick	Selective Masonry
Troy Ellison	E&E Acoustical	Jonathan Watts	Selective Masonry
Dave Coyte	Eagle Framing	James Boothe	Premier Service
Steve Early	J&K Electric	Derek Monk	Premier Service
Nick Stauder	J&K Electric	George Merchant	Victory Plumbing
John Britton	J&K Electric	David Shepherd	Victory Plumbing
Jeffrey McCool	Jeffco Concrete	A.J. Wolnski	Wolnski Scheduling Services

EMAIL DISTRIBUTION:


Michelle Best	Jefferson County BOE	Mike Wade	Joshco dba Butler Cont.
Dr. Rafael McDaniel	Jefferson County BOE	Linda Wright	Locker Pro
Lee Bryant	Lathan Associates	Todd Dunn	MC Precast
Joey Bussey	Blalock Building Company	WT Smith	MC Precast
Pam Garner	Blalock Building Company	Rodd Kindoll	MC Precast
Shane Lutz	Blalock Building Company	Ray Calhoun	Montgomery Woodworks
Bo Willis	ABG Caulking	Randy McDaniel	MSE Building Company
Keith Echols	Architectural Finishes	Mike Jones	MSE Building Company
Billy Beardslee	B&B Painting	Mike Schafer	Overhead Door Company
Jim Caradine	Building Specialties	Steven Stamps	Premier Service Company
Joe Cox	Covington Flooring	Jeremy Garrett	Schindler Elevator
Tommy Ellison	Covington Flooring	Jonathan Watts	Selective Masonry
Jimmy Isaminger	DMI Tile & Marble	Charles Johnson	Selective Masonry
Adam Easterling	E&E Acoustical & Drywall	Kirk Jones	Sizemore's Aluminum Prod.
C.J.	E&E Acoustical & Drywall	Frank Beaman	Steel Stadiums
Heith Comer	G&S Glass & Supply	George Merchant	Victory Plumbing
Jackie Keller	H2K Construction	A.J. Wolnski	Wolnski Scheduling
Karen Britton	J&K Electric	Susan Richardson	Wolnski Scheduling
George Henry	Jeffco Concrete		

HARD COPY DISTRIBUTION:

Brett Biel – 5 copies	Blalock Building Company		

PROJECT TIMELINE

JAN FEB MAR APR MAY JUN JUL AUG
2010



START 01JAN10

FINISH 12AUG10

NEXT MEETING: WEDNESDAY, AUGUST 18TH AT 9:00AM

PROGRESS MEETING SUMMARY

04AUG10

JOB CONTACTS

Name	Title	Cell/Pager #	Nextel #	email
Brett Biel	Project Manager	205-281-9842	154*86951*11	bbiel@blalockbc.com
Shane Lutz	Superintendent	205-281-5279		shanel@blalockbc.com

JOBSITE ADDRESS

1301 4th Place Pleasant Grove, AL 35127

MEETING ATTENDANCE

Everyone that was required to attend today's progress meeting did so.

Anyone with ongoing work or work scheduled to begin within the next 4 weeks is required to attend progress meetings. Anyone that is unable to attend a progress meeting should be sure to call Brett Biel or Shane Lutz before the meeting begins to give them the opportunity to ask any questions that would have come up at the meeting.

Below is a list of future meeting dates:

18AUG10

SAFETY

Blalock Building Company holds regular safety meetings every Tuesday morning at 9:00AM. Following is a list of key safety concerns:

- **Hard hats are required full time for everyone.**
- Step ladders – free standing, do not use top 2 steps, use proper height ladder.
- Competent person required on site during weekend work.
- Emergency phone numbers must be provided to all foremen.
- Fire extinguishers must be kept in place at all times.
- All subcontractors must attend safety meetings.
- Lull operators must wear a seatbelt during operation.
- Scaffolds must be erected in compliance with OSHA requirements.

CLEAN UP

All subcontractors are required to perform their own cleanup on a daily basis. Shane said that Blalock Building Company has been doing all of the cleanup. Consequently, a composite cleanup crew will be formed on Fridays to keep up with the work everyone is failing to do during the week. All subcontractors are required to contribute toward the composite cleanup crew.

DAILY REPORTS

Daily reports are required to be turned in on a daily basis, not weekly. Shane said that he is only getting daily reports from the HVAC contractor.

PROGRESS MEETING SUMMARY (CONT.)

O4AUG10

SUBMITTALS

Architect

There are currently no critical submittals out for approval.

REQUESTS FOR INFORMATION

27 RFI's have been issued to date. All of them have been answered. The vanity bowl cover color is still needed.

PAYMENT APPLICATIONS

Payment applications for the entire month's work are to be sent to Blalock's main office by the 20th of each month. The faxed copy must be sent by the 20th in order to process the request on time. Daily Reports and Sub Safety Meeting Minutes must also be up to date in order to receive payment.

CHANGE ORDER REQUESTS

Following is a list of Change Order requests with the status of each noted:

- COR #1 – Lift station – approved
- COR #2 – Bermuda grass – approved
- COR #3 – Deduct for header brick – accepted
- COR #4 – Rain delays for March – awaiting architect approval
- COR #5 – VE for concrete stadiums


SCHEDULE

A.J. reviewed and updated the schedule of remaining work. A revised copy is included in this report.







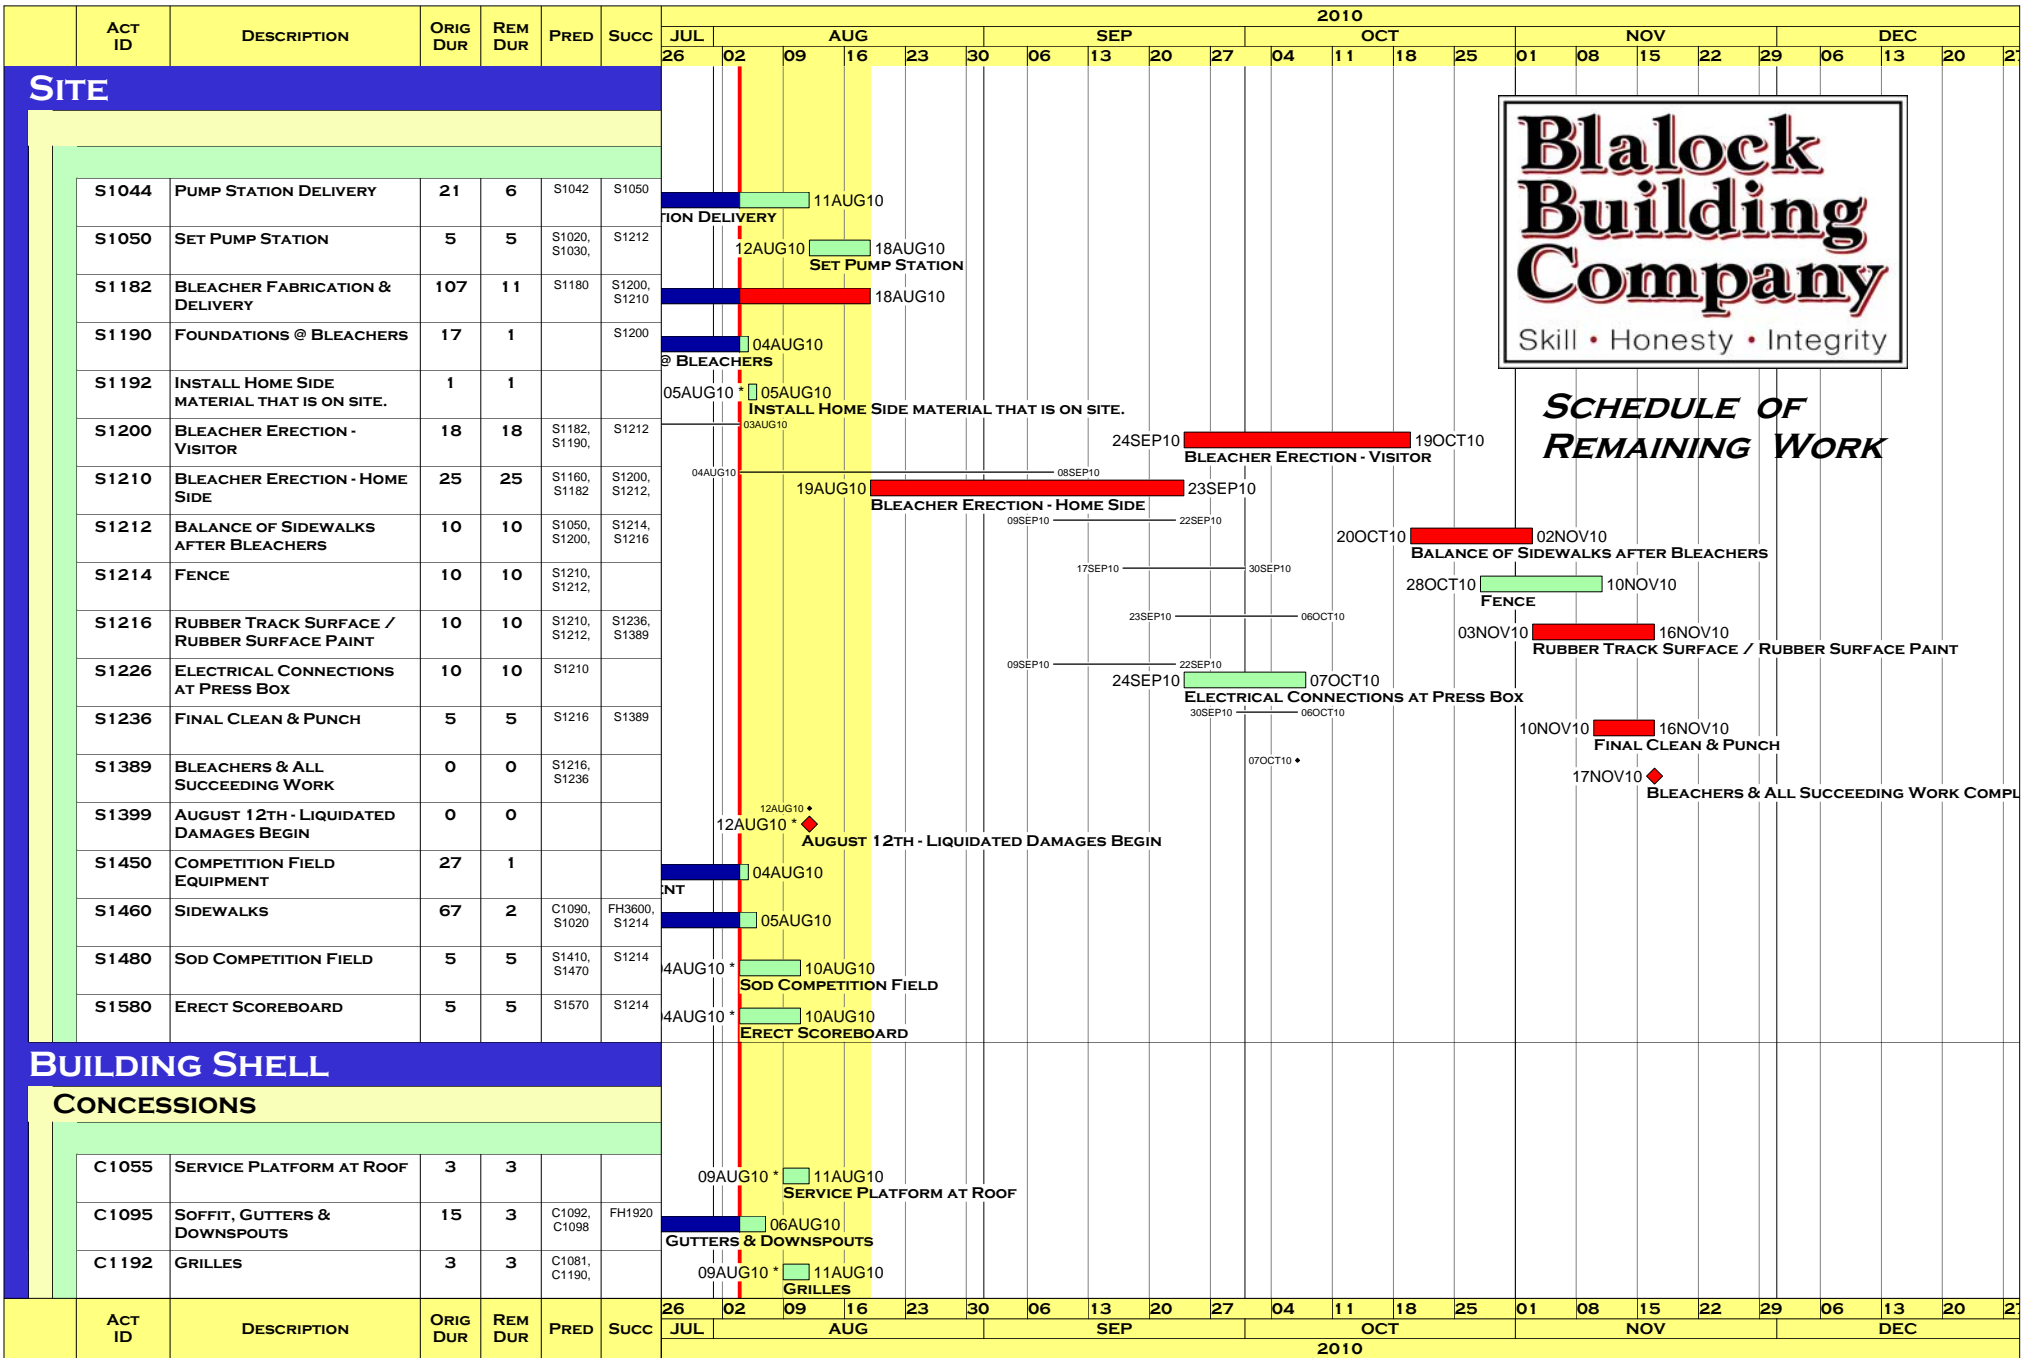

SCHEDULE OF REMAINING WORK


- Early bar
- Target bar
- Progress bar
- Critical bar
- ◆ Start milestone point
- ◇ Finish milestone point

PLGROVE (SURETRAK)
 REPORT: PLG1
 LAYOUT: LETTER BY AREA
 FILTER: REMAINING WORK

PLEASANT GROVE FOOTBALL STADIUM
BLALOCK BUILDING COMPANY

RUN DATE: 09AUG10
 DATA DATE: 04AUG10
 JOB# 1003
 PAGE 1A OF 3A



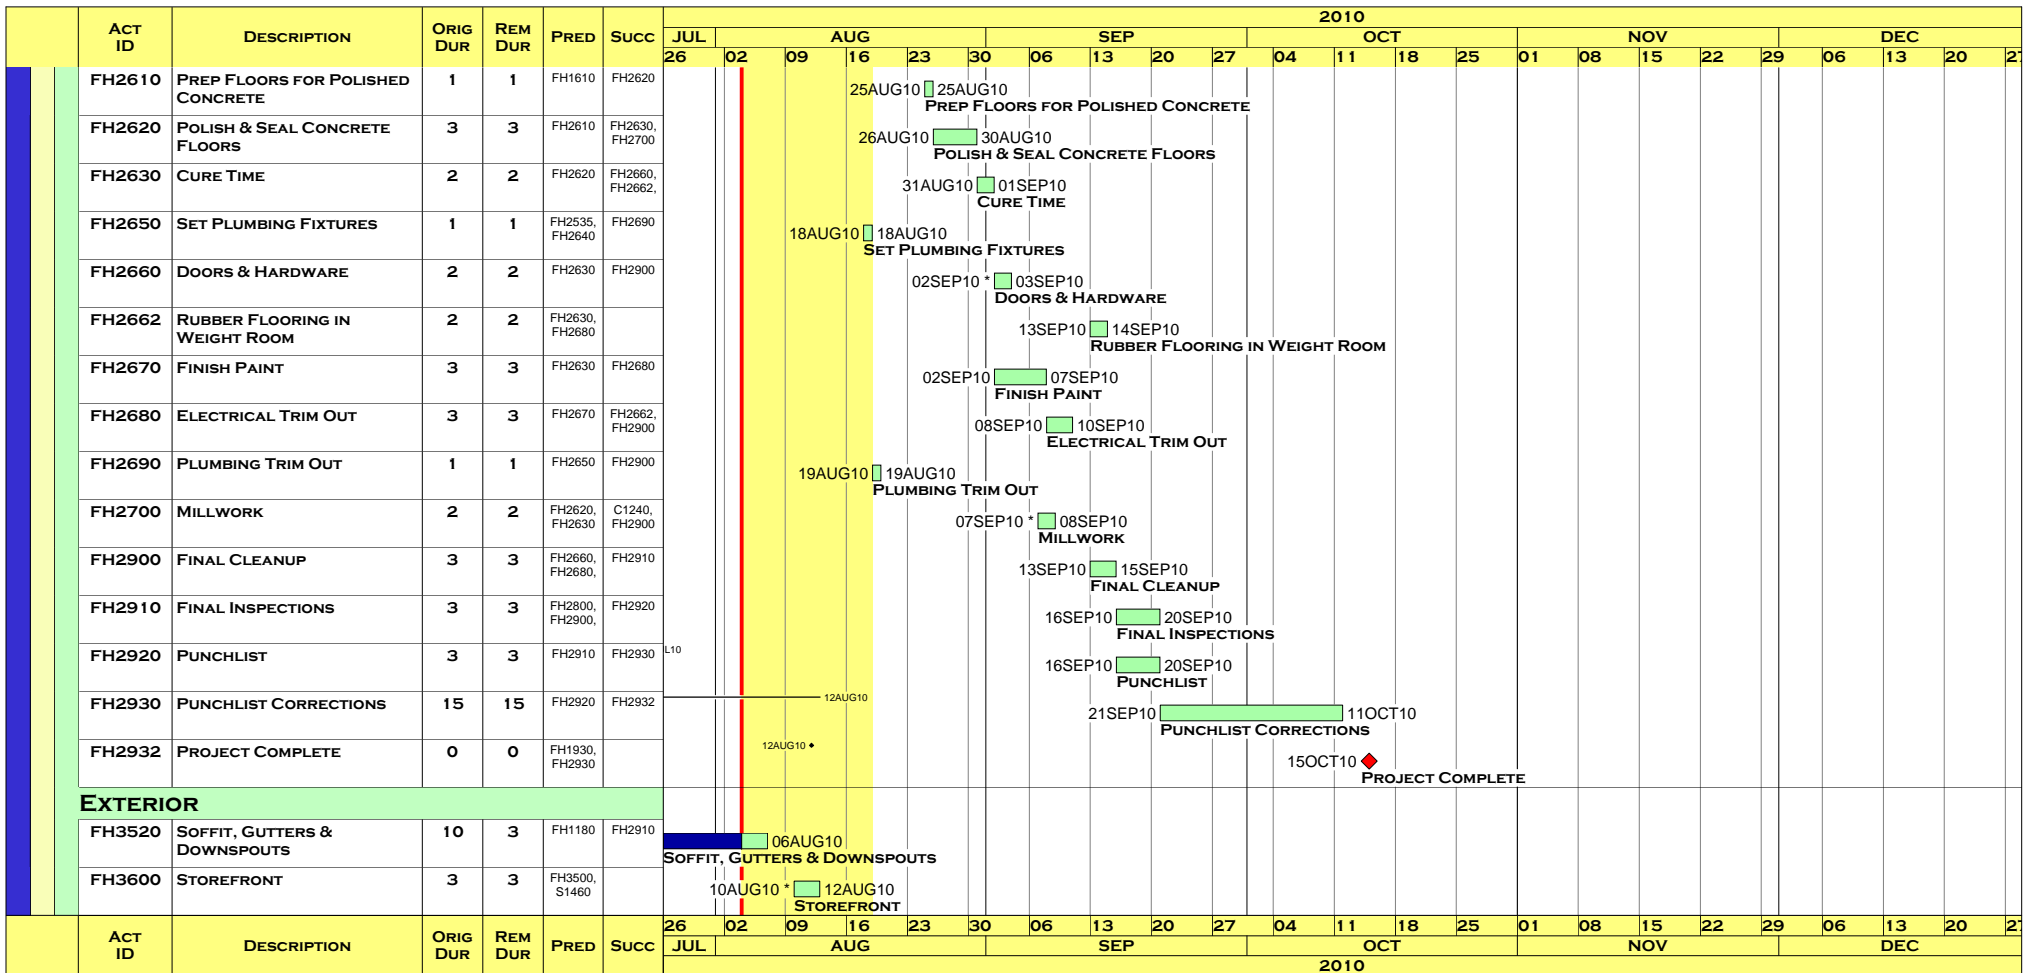

- Early bar
- Target bar
- Progress bar
- Critical bar
- Start milestone point
- Finish milestone point

PLGROVE (SURETRAK)
 REPORT: PLG1
 LAYOUT: LETTER BY AREA
 FILTER: REMAINING WORK

PLEASANT GROVE FOOTBALL STADIUM

BLALOCK BUILDING COMPANY

RUN DATE: 09AUG10
 DATA DATE: 04AUG10
 JOB# 1003
 PAGE 3A OF 3A



ACTION LIST

04AUG10

	#	DESCRIPTION	RESP	TO BE DONE BY
<input type="checkbox"/>	12	Schedule dates for press box delivery	Steel Stadiums	
<input type="checkbox"/>	13	Field house above ceiling inspection	All subs	06AUG10 09AUG10
<input checked="" type="checkbox"/>	15	Grille sizes at concessions	Premier / Brett	25JUN10
<input checked="" type="checkbox"/>	20	Broken conduit at High School project	Lathan	22JUL10
<input checked="" type="checkbox"/>	21	Select EIFS color	Lathan	22JUL10
<input type="checkbox"/>	22	Elevator inspection requirements (See Shane – All Subs)	All Subs	05AUG10
<input type="checkbox"/>	23	Grout color at ceramic wall tile	Lathan	05AUG10
<input type="checkbox"/>	24	Vanity bowl cover color	Lathan	05AUG10
<input type="checkbox"/>	25			
<input type="checkbox"/>	26			
<input type="checkbox"/>	27			
<input type="checkbox"/>	28			
<input type="checkbox"/>	29			
<input type="checkbox"/>	30			
<input type="checkbox"/>	31			
<input type="checkbox"/>	32			
<input type="checkbox"/>	33			
<input type="checkbox"/>	34			
<input type="checkbox"/>	35			
<input type="checkbox"/>	36			
<input type="checkbox"/>	37			
<input type="checkbox"/>	38			
<input type="checkbox"/>	39			
<input type="checkbox"/>	40			
<input type="checkbox"/>	41			
<input type="checkbox"/>	42			

Items denoted by an were reported to be complete at this meeting. They will be removed from the Action List at the next meeting
