


ACT ID	DESCRIPTION	ORIG DUR	REM DUR	PRED	SUCC	RESP	2011												2012															
							SEP			OCT			NOV			DEC			JAN			FEB			MAR			APR			MAY			
							19	26	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19	26
WYATT																																		
AREA A																																		
A 1498	PRE ROOFING CONFERENCE	0	0	1000, A1460	A1532	GCW	<div style="position: absolute; top: 10px; left: 10px;"> ◆ 11NOV11 ◆ 11NOV11 </div> <div style="position: absolute; top: 20px; left: 10px;"> ■ 18NOV11 — 22NOV11 PRE ROOFING CONFERENCE ■ 18NOV11 — 22NOV11 ROOF BLOCKING </div>																											
A 1520	ROOF BLOCKING	3	3	A1460	A1530	GCW																												
AREA B																																		
B 1410	EQUIPMENT PADS	3	3	B1400	B1430	GCW	<div style="position: absolute; top: 10px; left: 10px;"> ■ 16NOV11 — 18NOV11 EQUIPMENT PADS ■ 16NOV11 — 18NOV11 EQUIPMENT PADS </div>																											
AREA C																																		
C 1160	SET DOOR FRAMES	13	5	C1140	C1200	GCW	<div style="position: absolute; top: 10px; left: 10px;"> ■ 03OCT11 — 19OCT11 SET DOOR FRAMES ■ 03OCT11 — 19OCT11 SET DOOR FRAMES </div>																											
C 1410	EQUIPMENT PADS	3	3	C1400	C1430	GCW	<div style="position: absolute; top: 10px; left: 10px;"> ■ 18NOV11 — 22NOV11 EQUIPMENT PADS ■ 18NOV11 — 22NOV11 EQUIPMENT PADS </div>																											
APEX																																		
AREA A																																		
A 1600	OH DUCT ROUGH IN	5	5	A1460	A1595, A1602	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 18NOV11 — 24NOV11 OH DUCT ROUGH IN ■ 18NOV11 — 24NOV11 OH DUCT ROUGH IN </div>																											
AREA B																																		
B 1380	8" BATHROOM VENT STACK	1	1	B1250	B1400	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 09NOV11 — 09NOV11 8" BATHROOM VENT STACK ■ 09NOV11 — 09NOV11 8" BATHROOM VENT STACK </div>																											
B 1440	SET HVAC UNITS ON MEZZANINE	16	16	B1430	B1450	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 21NOV11 — 12DEC11 SET HVAC UNITS ON MEZZANINE ■ 21NOV11 — 12DEC11 SET HVAC UNITS ON MEZZANINE </div>																											
B 1600	OH DUCT ROUGH IN	5	5	B1400	B1610	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 16NOV11 — 22NOV11 OH DUCT ROUGH IN ■ 16NOV11 — 22NOV11 OH DUCT ROUGH IN </div>																											
AREA C																																		
C 1380	8" BATHROOM VENT STACK	1	1	C1250	C1400	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 04NOV11 — 04NOV11 8" BATHROOM VENT STACK ■ 04NOV11 — 04NOV11 8" BATHROOM VENT STACK </div>																											
C 1440	SET HVAC UNITS ON MEZZANINE	16	16	C1430	C1450	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 23NOV11 — 14DEC11 SET HVAC UNITS ON MEZZANINE ■ 23NOV11 — 14DEC11 SET HVAC UNITS ON MEZZANINE </div>																											
C 1600	OH DUCT ROUGH IN	5	5	C1400	C1610	APEX	<div style="position: absolute; top: 10px; left: 10px;"> ■ 18NOV11 — 24NOV11 OH DUCT ROUGH IN ■ 18NOV11 — 24NOV11 OH DUCT ROUGH IN </div>																											
BICE BUILDING Co.																																		
AREA B																																		
B 1400	FORM, PREP & POUR MEZZANINE SLAB	5	5	B1380, B1390	B1270, B1410	BICE	<div style="position: absolute; top: 10px; left: 10px;"> ■ 09NOV11 — 15NOV11 FORM, PREP & POUR MEZZANINE SLAB ■ 09NOV11 — 15NOV11 FORM, PREP & POUR MEZZANINE SLAB </div>																											
AREA C																																		
C 1400	FORM, PREP & POUR MEZZANINE SLAB	10	10	C1380, C1390	C1270, C1410	BICE	<div style="position: absolute; top: 10px; left: 10px;"> ■ 04NOV11 — 17NOV11 FORM, PREP & POUR MEZZANINE SLAB ■ 04NOV11 — 17NOV11 FORM, PREP & POUR MEZZANINE SLAB </div>																											
BRAWCO																																		
AREA A																																		
A 1300	DAMPROOFING	3	3	A1200, A1222	A1310	BRAWCO	<div style="position: absolute; top: 10px; left: 10px;"> ■ 27OCT11 — 31OCT11 DAMPROOFING ■ 27OCT11 — 31OCT11 DAMPROOFING </div>																											



NEAR TERM SCHEDULE

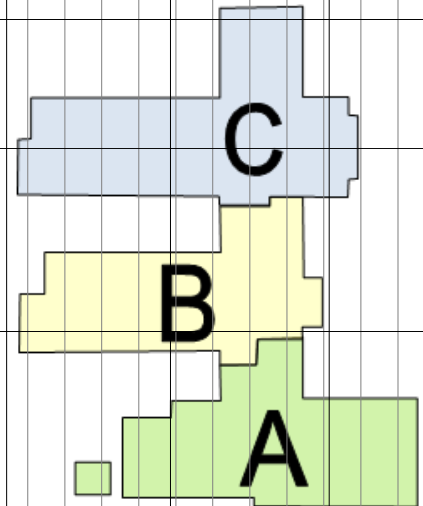

- Early bar
- Target bar
- Progress bar
- Critical bar
- ◆ Start milestone point
- ◆ Finish milestone point

CONCORD (SURETRAK)
 REPORT: CEL4
 LAYOUT: NEAR TERM BY RESP
 FILTER: NEAR TERM BY RESP

CONCORD ELEMENTARY
GARY C. WYATT, INC.

RUN DATE: 13OCT11
 DATA DATE: 13OCT11
 JOB# 1110
 PAGE 1A OF 6A



ACT ID	DESCRIPTION	ORIG DUR	REM DUR	PRED	SUCC	RESP	2011												2012															
							SEP			OCT			NOV			DEC			JAN			FEB			MAR			APR			MAY			
							19	26	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19	26
H2K																																		
AREA A																																		
A1260	STRUCTURAL STEEL	8	8	A1200, A1210,	A1226, A1270,	H2K																												
AREA B																																		
B1250	MEZZANINE DECKING & LADDERS	2	2	B1202, B1204,	B1260, B1380,	H2K																												
B1260	STRUCTURAL STEEL	8	8	B1200, B1204,	B1270, B1290,	H2K																												
AREA C																																		
C1250	MEZZANINE DECKING & LADDERS	5	5	C1200	C1260, C1380,	H2K																												
C1260	STRUCTURAL STEEL	8	8	C1200, C1250,	C1270, C1460	H2K																												
J&C ROOFING																																		
AREA A																																		
A1530	ROOF FLASHING & COPING	5	5	A1520	A1480, A1490,	J&C																												
A1532	TPO ROOFING	6	6	A1312, A1460,	A1534, A1552,	J&C																												
PHILLIPS SLIPFORM																																		
SITE																																		
1828	CURB & GUTTER	4	4	1826	1830	PSF																												
SANCHEZ																																		
AREA A																																		
A1200	CMU WALLS - GYM	17	4	A1150, A1160,	A1202, A1210,	SANC																												
A1202	CMU WALLS - CAFETERIA	20	7	A1200	A1204, A1222	SANC																												
A1204	CMU WALLS - KITCHEN	16	3	A1202	A1222	SANC																												
A1310	HIGH BRICK - NORTH	6	6	A1200, A1300	1902, 1910,	SANC																												
A1312	HIGH BRICK - WEST	6	6	A1310	A1314, A1532	SANC																												
A1314	FACE BRICK	25	25	A1312		SANC																												
AREA B																																		
B1200	CMU WALLS - MULTIPURPOSE	13	7	B1150, B1160,	1834, B1204,	SANC																												
B1202	CMU WALLS - TORNADO WALLS	13	5		B1200, B1250,	SANC																												

- Early bar
- Target bar
- Progress bar
- Critical bar
- Start milestone point
- Finish milestone point

CONCORD (SURETRAK)
 REPORT: CEL4
 LAYOUT: NEAR TERM BY RESP
 FILTER: NEAR TERM BY RESP

CONCORD ELEMENTARY

GARY C. WYATT, INC.

RUN DATE: 13OCT11
 DATA DATE: 13OCT11
 JOB# 1110
 PAGE 4A OF 6A



