Act ID	Description	Orig Dur	Rem Dur	Pred	Succ	Resp
WYATT						
AREA B						
B1520	Roof Blocking	3	3	B1510	B1530	Wyatt
AREA C						
C1520	Roof Blocking	3	3	C1510	C1530	Wyatt
ALABAMA CONTRACT SALES						
AREA A						
A1654	Basketball Goals	3	3	A1640, A1650	A1992	Alabama Contract
APEX						
AREA A						
A1562	Set RTU's	1	1	A1532, A1542	A1570, A1640	Apex
A1600	OH Duct Rough In	44	7	A1460	A1620	Apex
AREA B						
B1360	Set & Connect Condensing Units	3	3	B1350	B1750	Apex
B1450	Startup HVAC	5	5	B1440, C1540	B1760	Apex
B1596	OH Duct ABOVE Smoke Ceiling	5	5	B1460	B1597, B1598	Apex
B1600	OH Duct Rough In	5	5	B1400, B1430,	B1610	Apex
AREA C						
C1360	Set & Connect Condensing Units	3	3	C1350	C1750	Apex
C1582	OH Duct Rough In ABOVE Fire Ceiling	5	5	C1460, C1500	C1584	Apex
C1600	OH Duct Rough In	5	5	C1400, C1430,	C1610	Apex
BAIRD						
SITE						
1720	8" Backflow Vault	2	2	1596, 1710	1750	Baird
BICE BUILDING CO.						
SITE						
1910	Sidewalks	10	10	1814, A1310,	1920, 1922,	Bice Building

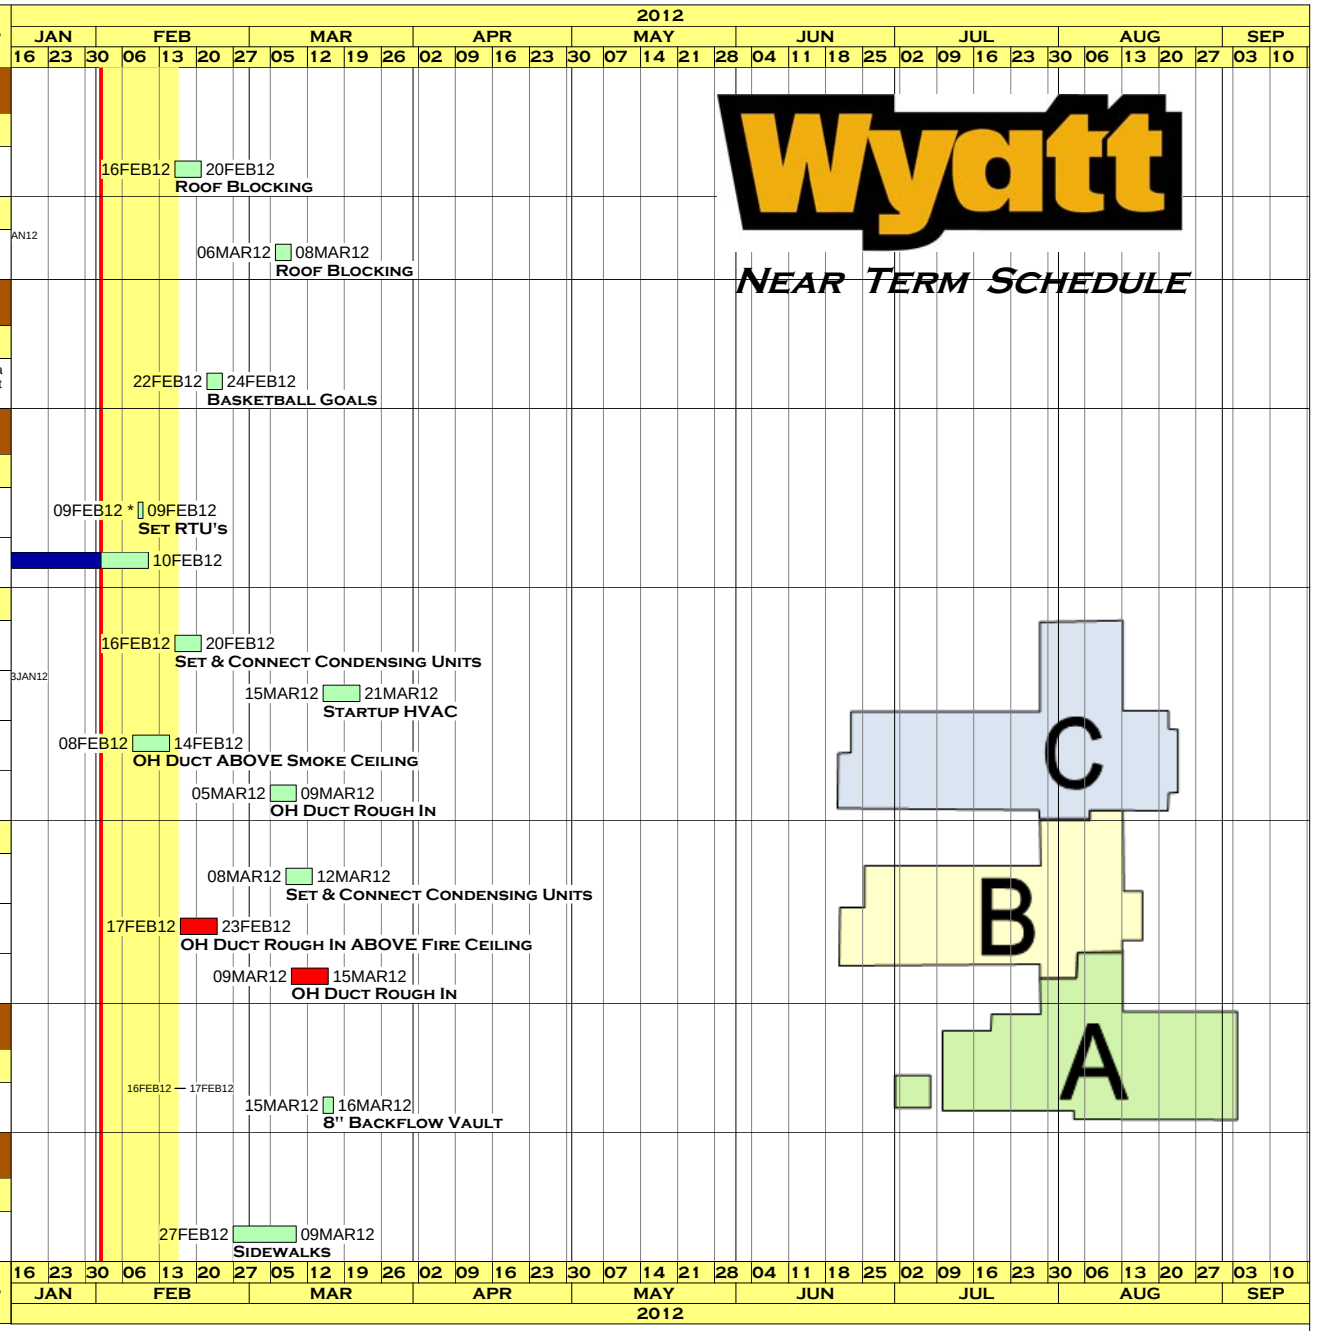

Wyatt

Near Term Schedule

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SureTrak)
Report: CEL4
Layout: Near Term by Resp
Filter: Near Term by Resp

CONCORD ELEMENTARY
GARY C. WYATT, INC.

Run Date: 03FEB12
Data Date: 02FEB12
Job# 1110

WSS
Wolnski Scheduling Services, Inc.

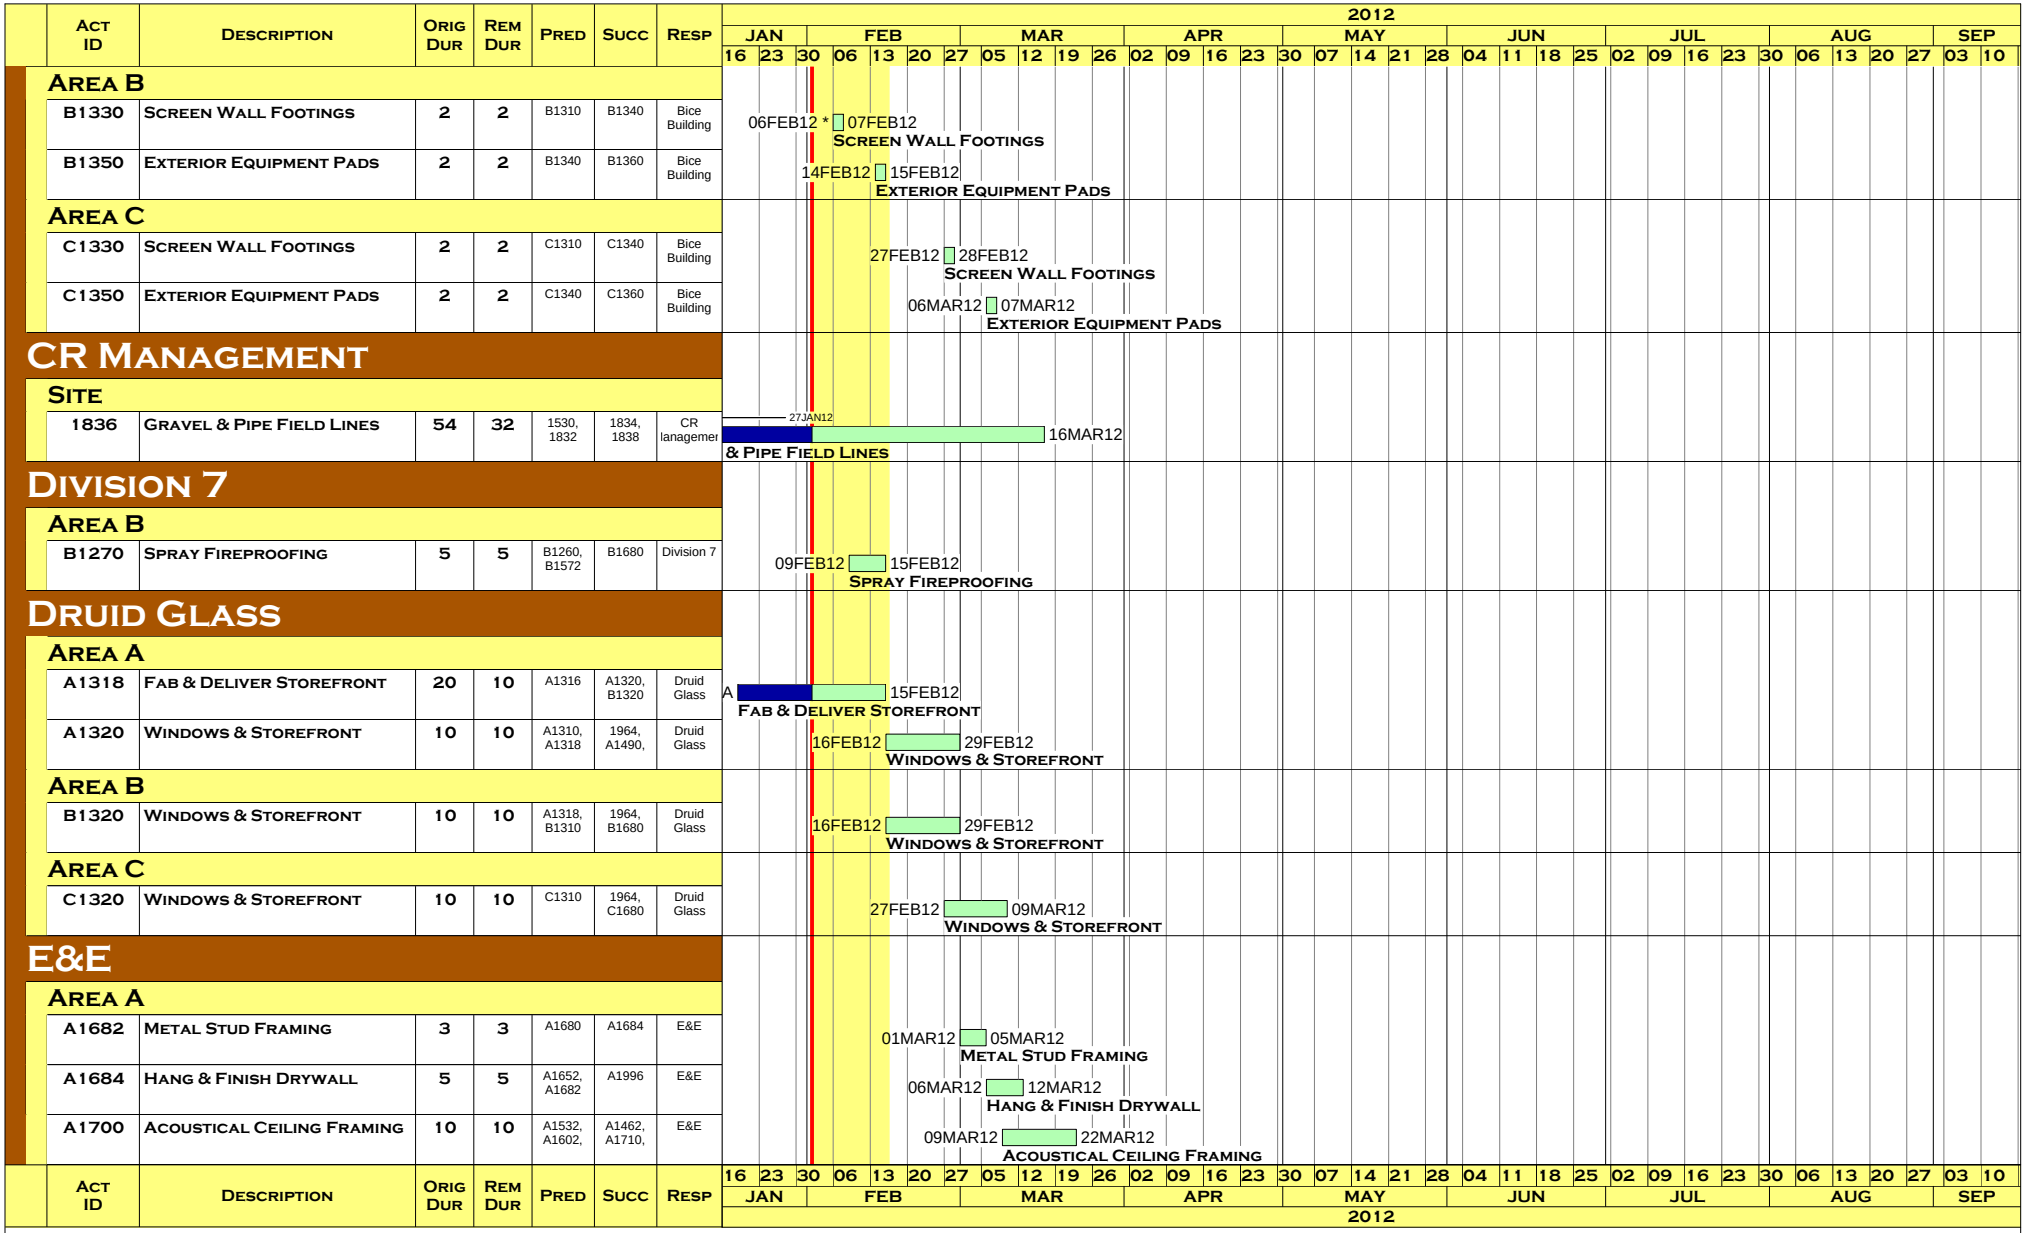

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SURETRAK)
REPORT: CEL4
LAYOUT: NEAR TERM BY RESP
FILTER: NEAR TERM BY RESP

CONCORD ELEMENTARY
GARY C. WYATT, INC.

RUN DATE: 03FEB12
DATA DATE: 02FEB12
JOB# 1110

WSS
WOLNSKI SCHEDULING SERVICES, INC.

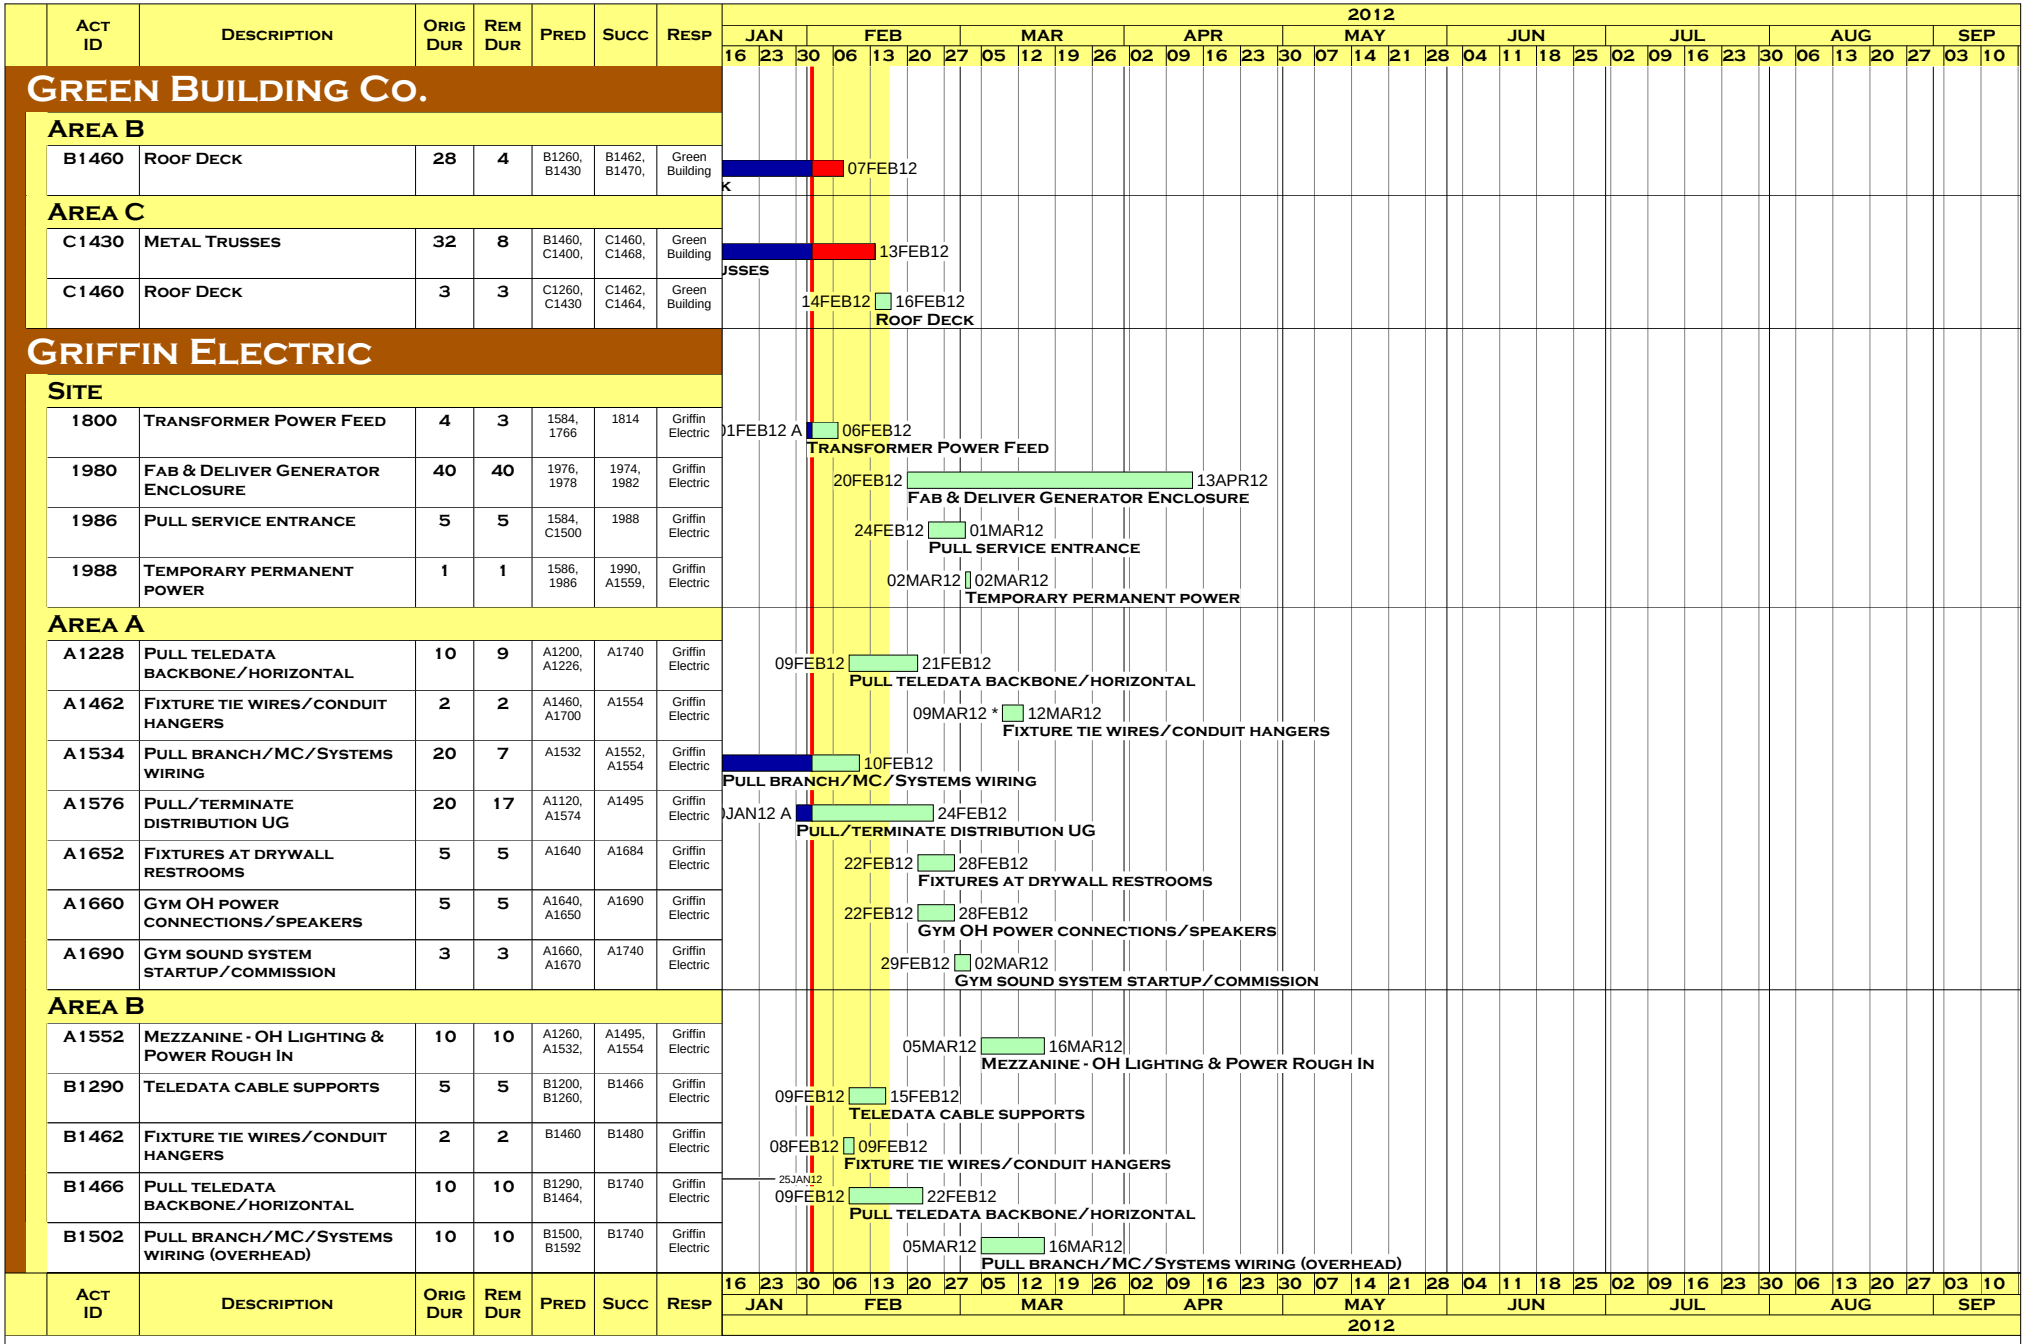

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SURETRAK)
REPORT: CEL4
LAYOUT: NEAR TERM BY RESP
FILTER: NEAR TERM BY RESP

CONCORD ELEMENTARY
GARY C. WYATT, INC.

RUN DATE: 03FEB12
DATA DATE: 02FEB12
JOB# 1110

WSS
WOLNSKI SCHEDULING SERVICES, INC.

Act ID	Description	Orig Dur	Rem Dur	Pred	Succ	Resp
B1504	Distribution electric room equipment	10	10	B1500	B1506, B1508	Griffin Electric
B1506	Pull/terminate distribution OH	5	5	B1504	B1740	Griffin Electric
B1508	Pull/terminate distribution UG	20	20	B1504	B1740	Griffin Electric
B1594	OH Electrical Rough In	10	10	B1592	B1700, B1710	Griffin Electric
B1630	OH Electrical Rough In	29	1	B1400	B1680, B1740	Griffin Electric
Area C						
C1220	In Wall Electrical	76	7	C1200		Griffin Electric
C1224	Teledata cable supports	5	5	C1200, C1552	C1464	Griffin Electric
C1462	Fixture tie wires/conduit hangers	2	2	C1460	C1466	Griffin Electric
C1464	Cable Tray	5	5	C1224, C1460	C1466	Griffin Electric
C1466	Pull teledata backbone/horizontal	10	10	C1462, C1464	C1740	Griffin Electric
C1502	Pull branch/MC/Systems wiring (overhead)	10	10	C1500	C1450, C1740	Griffin Electric
C1504	Distribution electric room equipment	5	5	C1500	C1450, C1506,	Griffin Electric
C1506	Pull/terminate distribution OH	5	5	C1504	C1450, C1740	Griffin Electric
C1508	Pull/terminate distribution UG	20	20	C1504	C1450, C1740	Griffin Electric
C1540	Temp / Perm Power On	0	0	A1532, A1574,	1990, A1570,	Griffin Electric
C1630	OH Electrical Rough In	15	15	C1400, C1460	C1540, C1680	Griffin Electric
C1632	OH Electrical Rough In	10	10	C1469	C1700	Griffin Electric
J&C Roofing						
Area A						
A1480	Aluminum Soffit	5	5	A1530	A1760	J&C Roofing
A1490	Gutters & Downspouts	5	5	A1320, A1530	A1960	J&C Roofing
A1530	Roof Flashing & Coping	10	10	A1520, A1532,	A1480, A1490,	J&C Roofing
Area B						
B1480	Aluminum Soffit	5	5	B1462, B1470,	B1490, B1760	J&C Roofing
B1490	Gutters & Downspouts	5	5	B1470, B1480	B1960	J&C Roofing

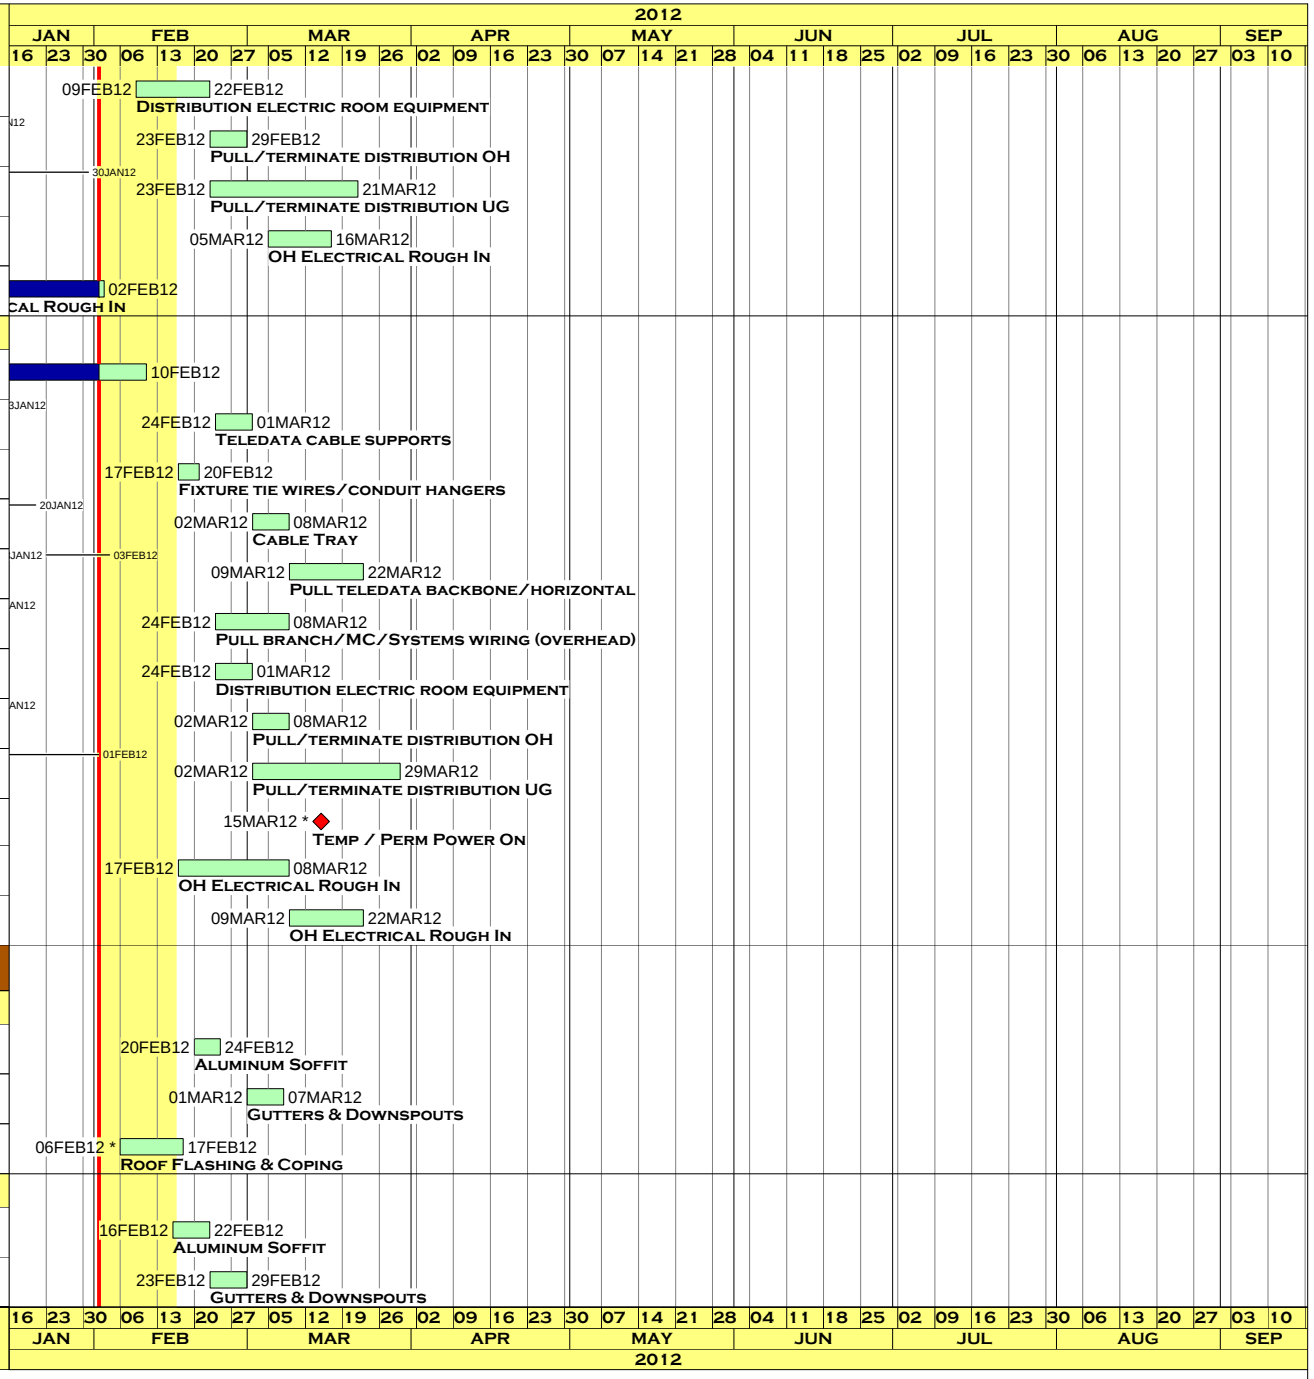

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SureTrak)
Report: CEL4
Layout: Near Term by Resp
Filter: Near Term by Resp

CONCORD ELEMENTARY
GARY C. WYATT, INC.

Run Date: 03FEB12
Data Date: 02FEB12
Job# 1110

WSS
Wolnski Scheduling Services, Inc.

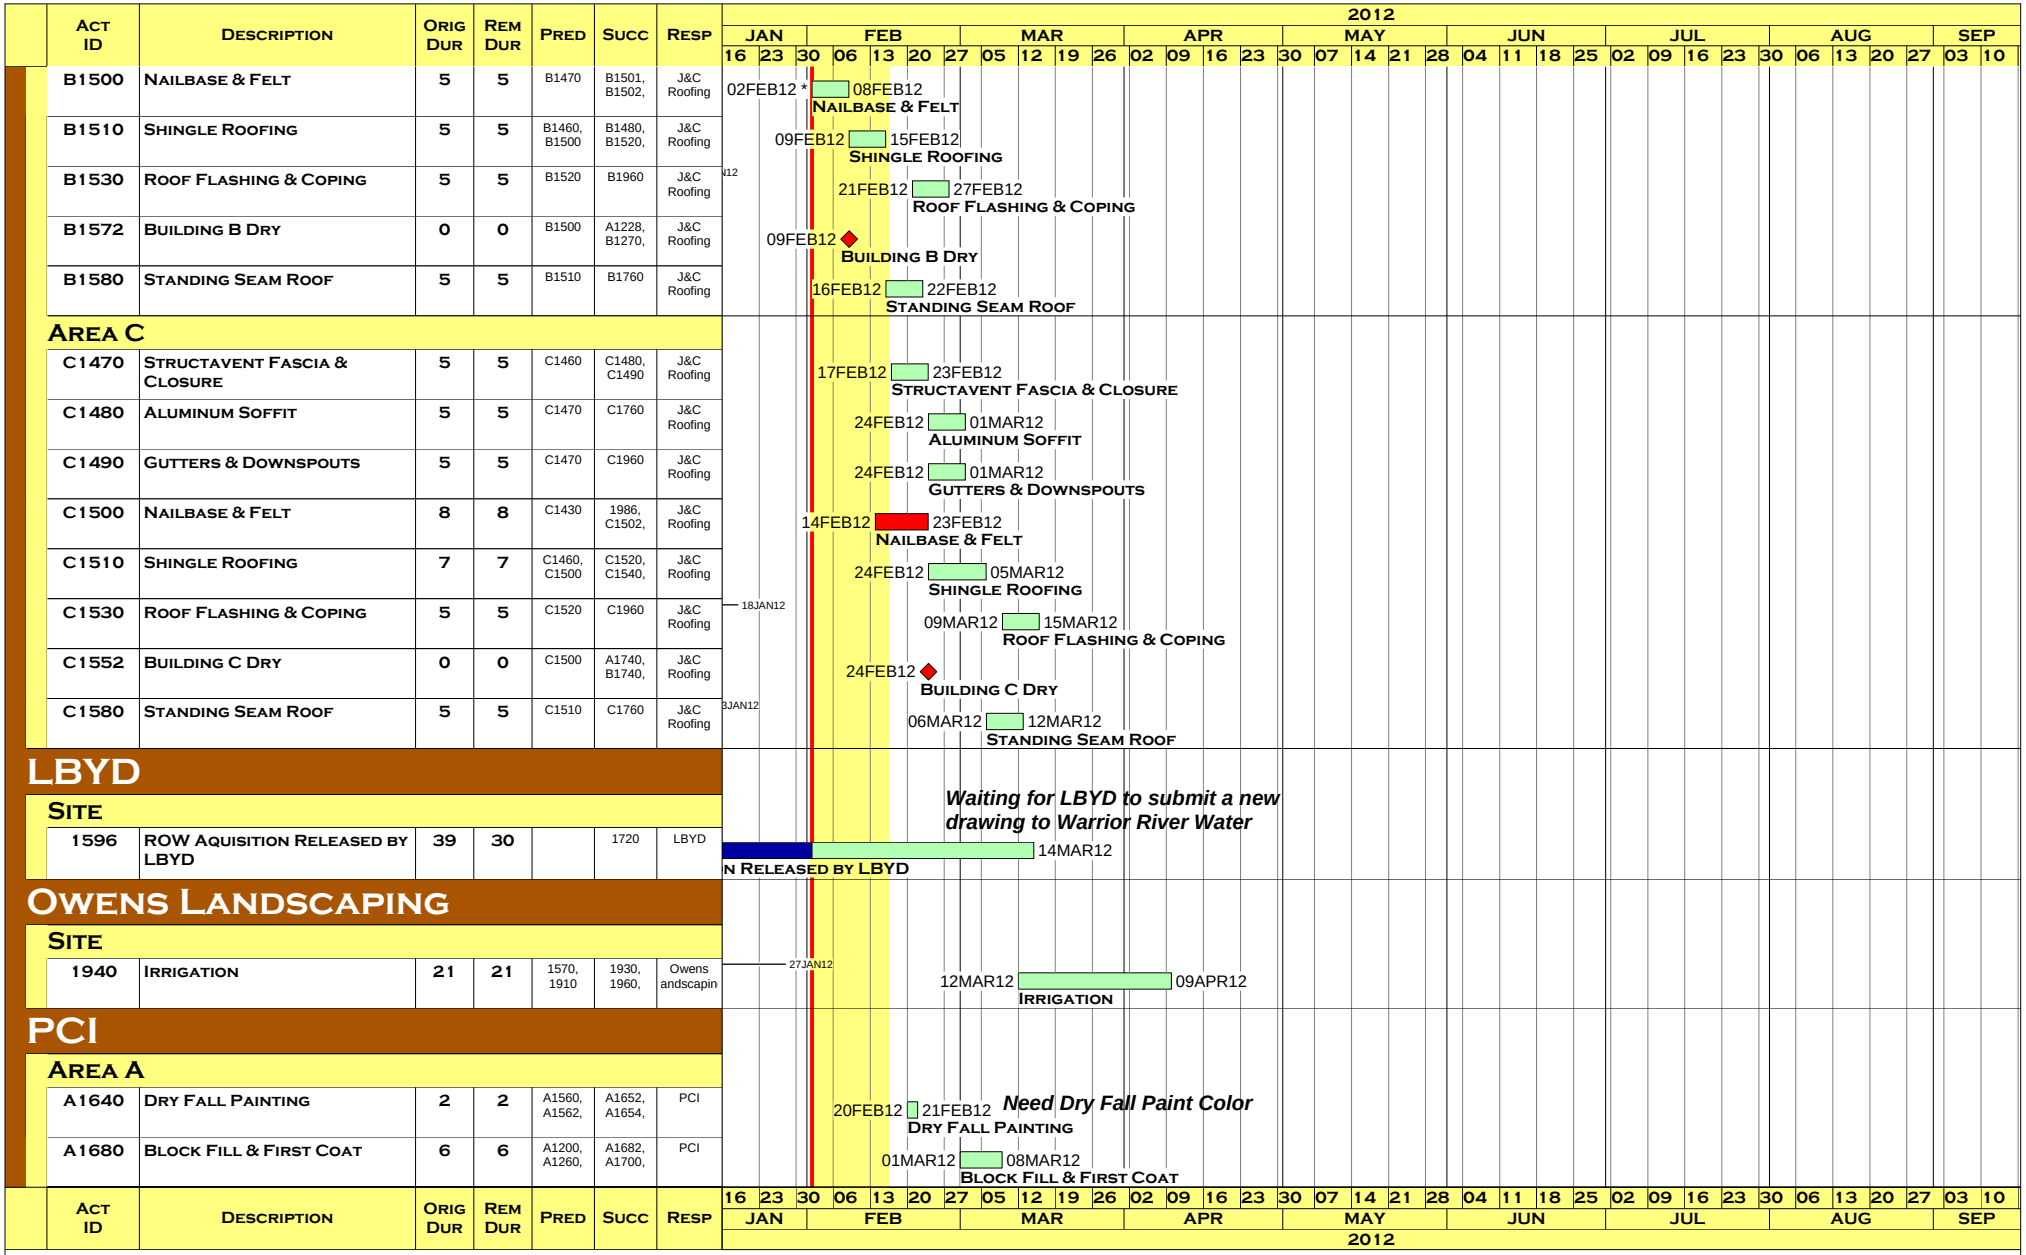

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SureTrak)
Report: CEL4
Layout: Near Term by Resp
Filter: Near Term by Resp

CONCORD ELEMENTARY
GARY C. WYATT, INC.

Run Date: 03FEB12
Data Date: 02FEB12
Job# 1110

WSS
Wolnski Scheduling Services, Inc.

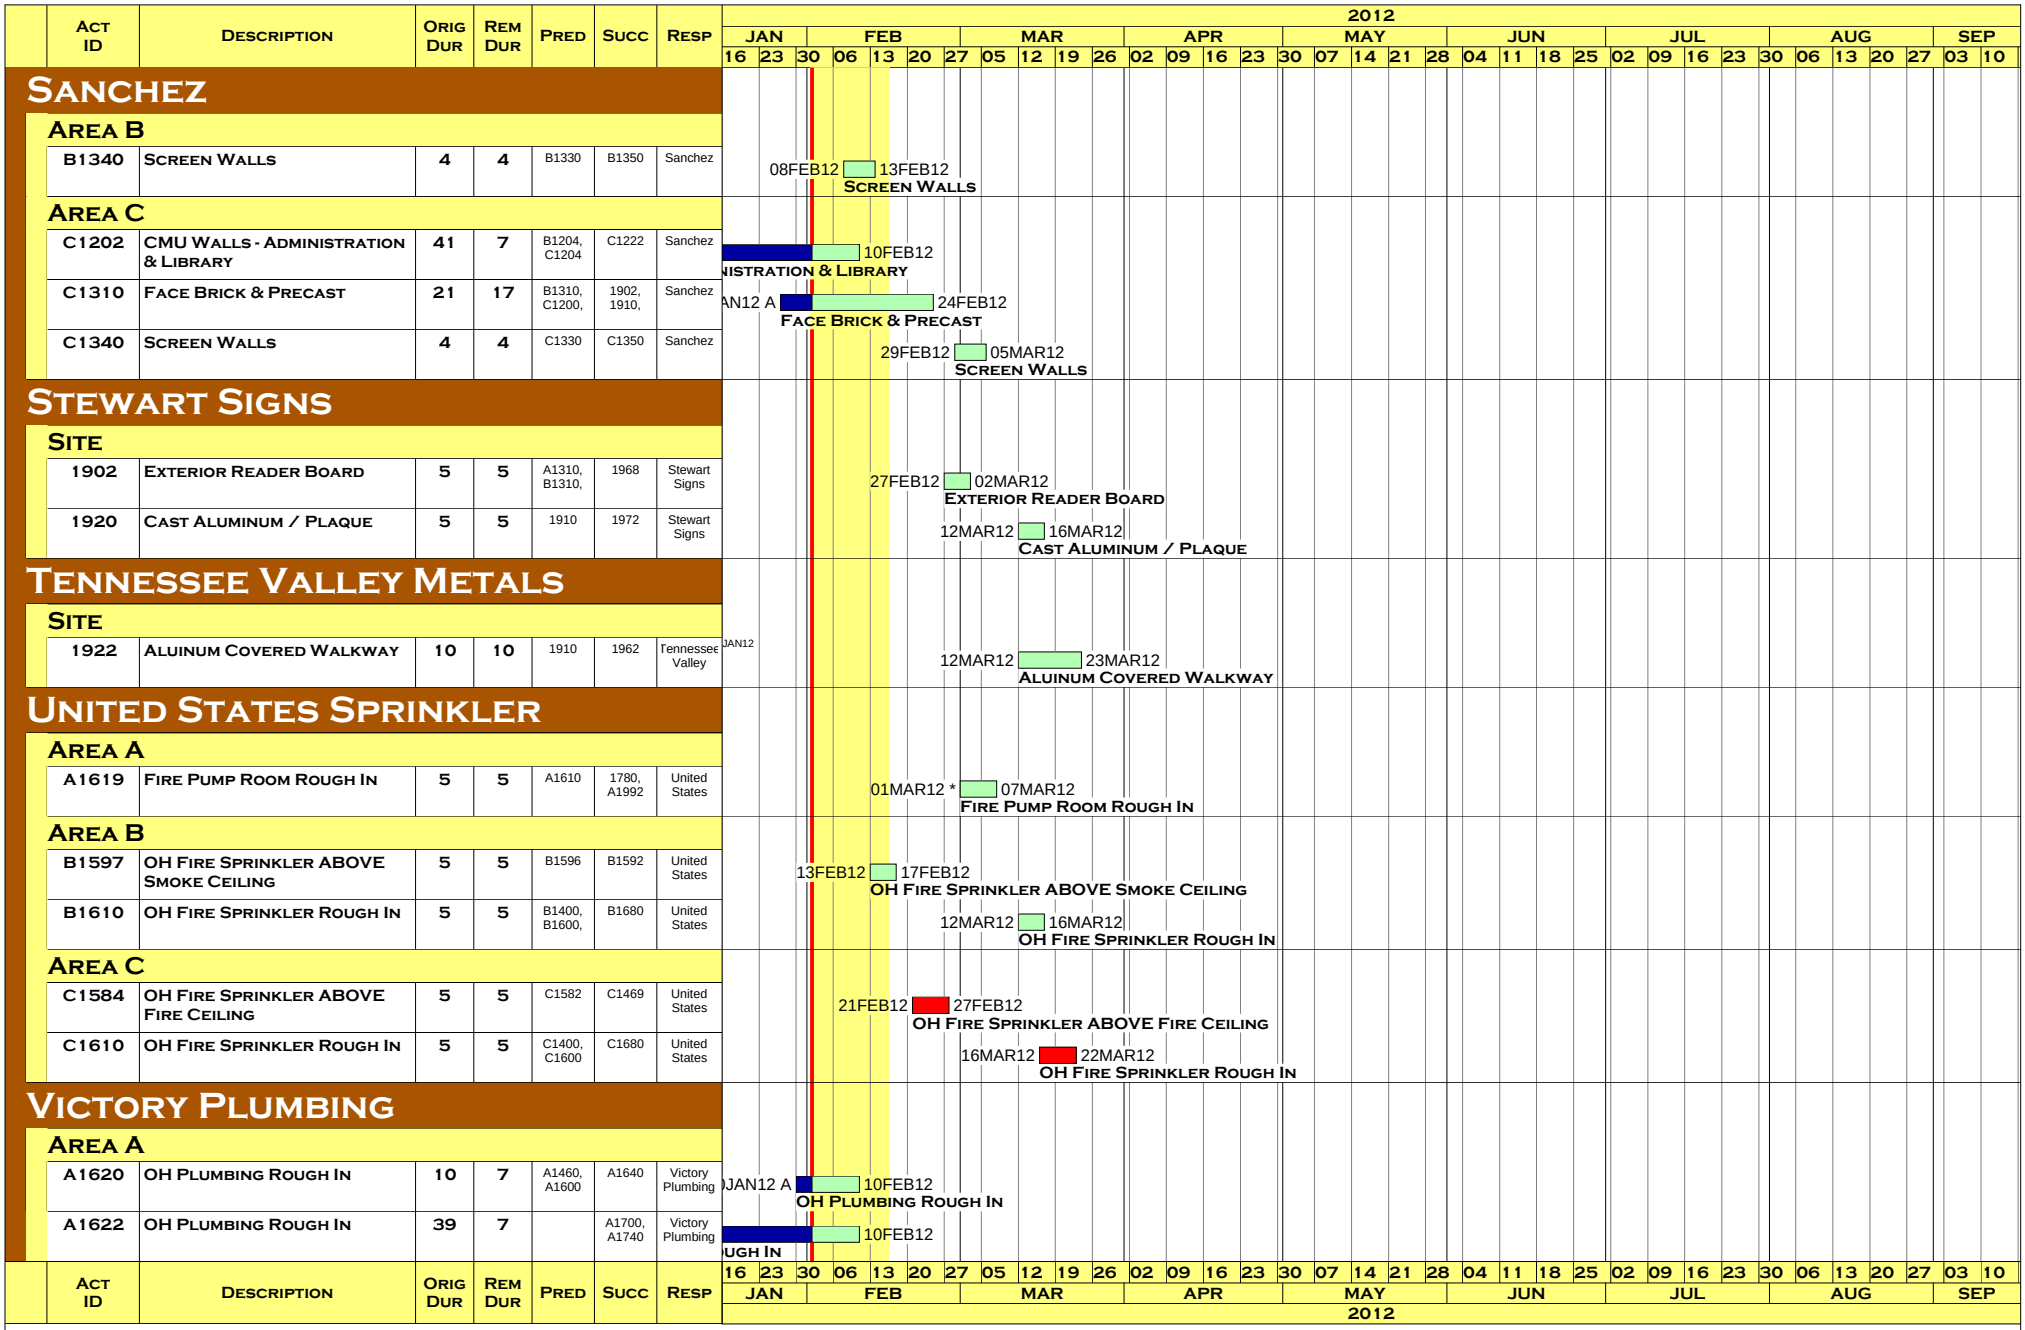

Act ID	Description	Orig Dur	Rem Dur	Pred	Succ	Resp
SANCHEZ						
AREA B						
B1340	SCREEN WALLS	4	4	B1330	B1350	Sanchez
AREA C						
C1202	CMU WALLS - ADMINISTRATION & LIBRARY	41	7	B1204, C1204	C1222	Sanchez
C1310	FACE BRICK & PRECAST	21	17	B1310, C1200,	1902, 1910,	Sanchez
C1340	SCREEN WALLS	4	4	C1330	C1350	Sanchez
STEWART SIGNS						
SITE						
1902	EXTERIOR READER BOARD	5	5	A1310, B1310,	1968	Stewart Signs
1920	CAST ALUMINUM / PLAQUE	5	5	1910	1972	Stewart Signs
TENNESSEE VALLEY METALS						
SITE						
1922	ALUINUM COVERED WALKWAY	10	10	1910	1962	Tennessee Valley
UNITED STATES SPRINKLER						
AREA A						
A1619	FIRE PUMP ROOM ROUGH IN	5	5	A1610	1780, A1992	United States
AREA B						
B1597	OH FIRE SPRINKLER ABOVE SMOKE CEILING	5	5	B1596	B1592	United States
B1610	OH FIRE SPRINKLER ROUGH IN	5	5	B1400, B1600,	B1680	United States
AREA C						
C1584	OH FIRE SPRINKLER ABOVE FIRE CEILING	5	5	C1582	C1469	United States
C1610	OH FIRE SPRINKLER ROUGH IN	5	5	C1400, C1600	C1680	United States
VICTORY PLUMBING						
AREA A						
A1620	OH PLUMBING ROUGH IN	10	7	A1460, A1600	A1640	Victory Plumbing
A1622	OH PLUMBING ROUGH IN	39	7		A1700, A1740	Victory Plumbing

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SURETRAK)
REPORT: CEL4
LAYOUT: NEAR TERM BY RESP
FILTER: NEAR TERM BY RESP

CONCORD ELEMENTARY
GARY C. WYATT, INC.

RUN DATE: 03FEB12
DATA DATE: 02FEB12
JOB# 1110

WSS
WOLNSKI SCHEDULING SERVICES, INC.

Act ID	Description	Orig Dur	Rem Dur	Pred	Succ	Resp
Area B						
B1501	Plumbing Rough In Mezzanine (Unit Vents)	5	5	B1500		Victory Plumbing
B1598	OH Plumbing ABOVE Smoke Ceiling	5	5	B1596	B1592	Victory Plumbing
B1620	OH Plumbing Rough In	5	5	B1400, B1430,	B1610	Victory Plumbing
Area C						
C1210	In Wall Plumbing	76	7	C1200		Victory Plumbing
C1586	OH Plumbing ABOVE Fire Ceiling	5	5	C1460, C1500	C1469	Victory Plumbing
Site						
1976	Generator Enclosure Submittal Approval	10	10		1980	
Area B						
B1590	Frame Smoke Barrier Ceiling Framing - Mezzanine	3	1	B1430, B1572	B1592	
B1592	Hang & Finish Smoke Barrier - Mezzanine	10	10	B1590, B1597,	A1552, B1502,	
Area C						
C1468	Smoke Barrier Ceiling Framing	3	3	C1430	C1469	
C1469	Smoke Barrier Ceiling - Hang & Finish	8	8	C1468, C1584,	C1600, C1632	

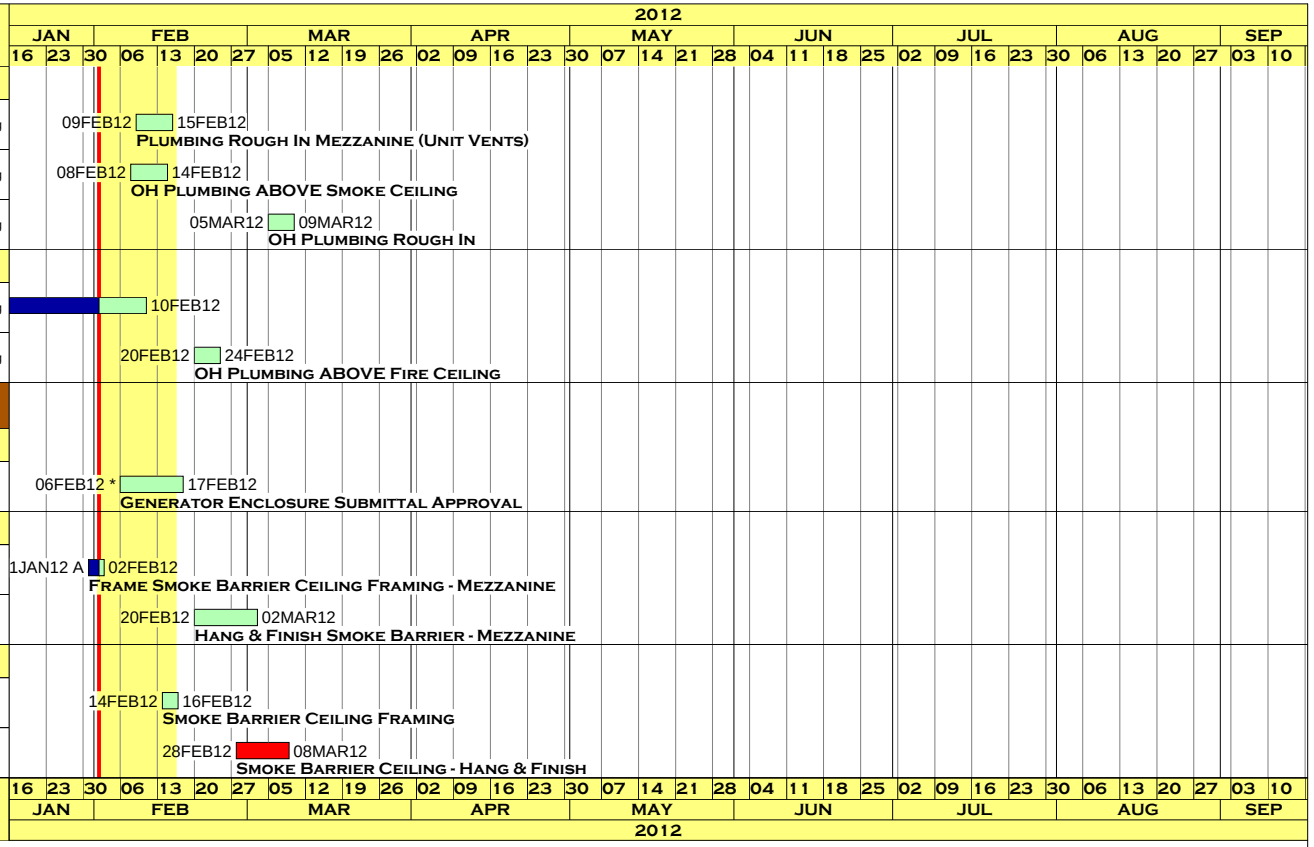

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

CONCORD (SureTrak)
Report: CEL4
Layout: Near Term by Resp
Filter: Near Term by Resp

CONCORD ELEMENTARY
GARY C. WYATT, INC.

Run Date: 03FEB12
Data Date: 02FEB12
Job# 1110

WSS
Wolnski Scheduling Services, Inc.
